



**Department of Finance
Budget and Planning Division
Capital Planning Section
175 E 2nd, Tulsa, Oklahoma 74103-3203 (918) 596-7653**

To: STOC
From: Gary Hamer, AICP
Capital Planning and Grants Manager
Date: March 23, 2021
Subject: March Meeting

Enclosed is the material for your March 23, 2021 meeting including the February 28, 2021 Financial Report for your review. 2017 and 2014 Sales Tax Program revenues for March 2021 and the fiscal year to date compared to 2017 and 2014 Sales Tax Program Adopted Budget Estimates are:

	Actual	Current Adopted Budget	Variance from Adopted Budget
Month of March	\$8,584,471	\$8,082,448	6.2%
Year to Date	\$81,253,906	\$77,577,801	4.7%

Please note the above amounts are the Sales Tax revenue only.

The 2017 and 2014 Sales Tax Programs Funds (4000 and 405), in addition to sales tax revenue, receives interest, and other revenues such as grants, transfers and miscellaneous revenues. Total revenue reported for the funds is not available until the end of the month so, the information provided below is for the most recently completed month. Total Fund 4000 and 405 revenue for the month of February was:

	<u>Month Ending: February 28, 2021</u>	<u>Variance from Adopted Budget</u>	<u>Year thru: February 28, 2021</u>	<u>Variance from Adopted Budget</u>
Sales Tax Revenue	\$9,360,728	2.4%	\$72,669,434	4.6%
Interest on Investments	\$191,823	N/A	\$1,986,890	N/A
Other Revenue	\$0	N/A	\$0	N/A
Total Fund Revenue	\$9,552,551	2.4%	\$74,656,324	7.1%



SALES TAX OVERVIEW COMMITTEE

**NOTICE AND AGENDA
REGULAR MEETING
SALES TAX OVERVIEW COMMITTEE
Tuesday, March 23, 2021, 8:00 A.M.
Go To Meeting**

The STOC will be meeting by Go To Meeting on March 23, 2021 at 8 am.

STOC March 23rd
Tue, Mar 23, 2021 8:00 AM - 10:00 AM (CDT)

Please join my meeting from your computer, tablet or smartphone.
<https://www.gotomeet.me/CityOfTulsa3/stoc-march-23rd>

You can also dial in using your phone.
United States: +1 (646) 749-3122

Access Code: 764-937-821

New to GoToMeeting? Get the app now and be ready when your first meeting starts:
<https://global.gotomeeting.com/install/764937821>

In this environment of COVID, the STOC would appreciate it if members of the Public wishing to join the meeting would do so using the GoTo Meeting option.

**NOTICE AND AGENDA
REGULAR MEETING
SALES TAX OVERVIEW COMMITTEE
Tuesday, March 23, 2021, 8:00 A.M.
Go To Meeting**

- I.** Call to Order
- II.** Minutes of February Meeting
- III.** Chair's Report to the City Council
- IV.** Subcommittee Reports
 - A. Tulsa Vision Economic Development Project Update
 - B. Public Safety
 - C. Parks
 - D. Streets and Stormwater, Transportation, Water and Sewer
 - E. Finance and Financial Report
- V.** Unfinished Business
- VI.** New Business
 - A. Chair Report presenters
- VII.** Adjournment

MINUTES

Sales Tax Overview Committee Meeting

February 23, 2021, 8:00 a.m.
Go To Meeting

The Sales Tax Overview Committee met for the regular monthly meeting at 8:00 a.m. on February 23, 2021.

I. Call to Order

Chair Ashley Webb called the meeting to order at 8:05 a.m.

The following members were present virtually:

Pamela Amburgy	Scott Grizzle	Renee Plocek
David Blatt	Jonathan Hall	Kathy Sebert
Janae Bradford	Linda Jenkins	
Marcia Bruno-Todd	Mareo Johnson	
Ellouise Cochran	Paul McTighe	

The following members were absent:

Alex Gomez	Sylvia Powell	Daryl Tannehill
------------	---------------	-----------------

Also present:

Gary Hamer	Jarrod Moore	Anne Boyd	Mary Kell
Josh Miller			

II. Approval of Minutes

The minutes of the October, November, December, and January were read. A motion was made by Janae Bradford to pass all four (4) months minutes as read, Linda Jenkins seconded the motion. The motion was carried unanimously by a roll call vote.

III. Chair's Report

The Chair's Report to Council was given by Ashley Webb. He stated that the meeting went well, and the Council had no questions.

IV. Financial Report

The January collections were \$9.36M which is about 2.4 percent over budget. Current sales tax collections are about 4.6 percent ahead of budget for the year to date. Both the current budget and collections are below the previous year.

V. Subcommittee Reports

A. Tulsa Vision Economic Development

Josh Miller reported on Peoria-Mohawk Business Park. He reported that soil stabilization on the site is being worked on. Muncie hopes to open by the third quarter of 2021. The City is doing water and street improvements on 36th Street North. Linda Jenkins reported that the Tulsa Arts Commission has made recommendations that are being sent to the Mayor. Concrete repair and art installation are all that remain at the Cox Business Center project. Striping work for the Bike Pedestrian Master Plan is being worked on. To date, \$2 million has been funded. There were no further comments or questions, and the report was accepted.

B. Public Safety

Ashley Webb gave an overview. He stated that the Mayors Office is taking over the Route 66 Xperience. Repeated requests for someone to give an update on the status of the project have gone unanswered. He reported that he had driven past the Thomas Gilcrease House site and the house looked wonderful. Notice to Proceed on work for the ADA projects for Centennial, Hicks, and Reed Parks was given on February 1st. The Police Department reports that the vehicles for the 2020 budget year have all been received. The vehicles for the 2021 budget year have been ordered but most have not yet been received. The shutdowns caused by COVID have placed these projects behind schedule. There were no further comments or questions, and the report was accepted.

C. Parks

Several members were called on to give an overview. Previously scheduled work at Ben Hill Park has been completed. Work on the design of the roof replacement for the community building has begun. The bid for work on the Reed Park pool reconstruction and water playground were awarded to Magnum Construction. Work is scheduled to begin in March or April. The Greenwood Cultural Center was added to the list this month. Consultant selection is underway. The Center is currently preparing for upcoming commemorative events. There were no further comments or questions and the report was accepted.

D. Street and Stormwater / Water and Sewer

There was no report given this month due to weather related events. There were no further comments or questions and the report was accepted.

VI. Unfinished Business

VII. New Business

A. Chair Report presenters for next month(s)

	<u>Presenter</u>	<u>Backup</u>
Mar 3	Mareo Johnson	Ashley Webb
Apr 7	Janae Bradford	Linda Jenkins
May 5	Mareo Johnson	

5/5, 6/2, 7/14, 8/4, 9/1, 10/6, 11/3, 12/1

VIII. **Adjournment**

The meeting was adjourned at 8:45 a.m.

Ashley Webb, Chair

Handwritten signature of Ashley R. Webb in black ink.

Linda Jenkins, Vice Chair

Handwritten signature of Linda Jenkins in blue ink.



Ashley Webb
Chair

Ashley R. Webb
Riggs, Abney, Neal, Turpen, Orbison & Lewis Inc.
Attorney At Law
Tulsa, OK 74119
(918) 699-8905

To: City Council

Date: March 3rd, 2021

Subject: March Report to City Council

Attached is the February 2020 Sales Tax Overview Committee (STOC) Status Report.

2006 Special Extended Sales Tax

January expenditures totaled \$37,685, almost all which was spent on the 91st & Harvard Intersection project. Encumbrances and commitments total \$4,429,258. Current appropriations for the Special Extended Sales Tax Fund total \$271,344,933. There is a current appropriation balance of \$10,586,355.

2008 Sales Tax Special Temporary Streets Fund

Expenditures in January totaled \$127,517, almost all of which was spent on the Citywide Non-Arterial Routine and Preventative project. To date, \$145,176,624 has been spent in this fund. Encumbrances and commitments total \$189,277. Life to date appropriations total \$145,493,500. There is a current appropriation balance of \$127,600.

2014 Sales Tax Fund

January expenditures totaled \$5,683,033, of which \$1.5 million was spent on the Citywide Arterial Rehabilitation project. To date, \$306,957,857 has been spent in this fund. Encumbrances and commitments total \$58,183,268. Total life-to-date appropriations for the 2014 Sales Tax Fund are \$567,377,764. There is a current appropriation balance of \$202,236,639.

2016 Sales Tax Fund

January expenditures totaled a net \$(1,499,376) within the 2016 Tulsa Vision Sales Tax Fund. This was due to a reversal of \$3.1 million in the Zink Lake and Related Infrastructure project. To date, \$73,646,525 has been spent in this fund. Encumbrances and commitments total \$22,375,578. Total life-to-date appropriations for the 2016 Sales Tax Fund are \$127,143,645. There is a current appropriation balance of \$31,121,541.

2016 Revenue Bond Fund

January expenditures totaled \$2,584,613 within the 2016 Tulsa Vision Revenue Bond Program with \$953,000 being spent on the GO Plan Priority project. Total life to date appropriations within the fund are \$350,600,000. Encumbrances and commitments total \$117,776,736. There is a current appropriation balance of \$68,884,015.

STOC Chair Report to the City Council
March 3rd, 2021

2020 General Obligation Bonds

January expenditures totaled \$223,927, of which \$39,000 was spent on the Maintenance Zone 1078 (55th St N from MLK Jr Blvd to Elgin Ave; Frankfort Ave from 51st Pl N to 54th St N; and Hartford Ave from 56th St N to 46th St N) project. To date, \$956,901 has been spent in this fund, all of which being spent on the Central Business District: MLK & Detroit street project. Encumbrances and commitments total \$4,113,857. Life to date appropriations for the 2020 General Obligation Bond Fund total \$17,500,000. There is a current appropriation balance of \$12,429,242.

2014 General Obligation Bonds

January expenditures totaled \$4,723,827, with \$937,000 being spent on the Maintenance Zone 3011 (Marshall St. south to Latimer Pl. / 71st E. Ave. west to 68th E. Ave). project. To date, \$163,934,780 has been spent in this fund. Encumbrances and commitments total \$37,729,440. Life to date appropriations for the 2014 General Obligation Bond Fund total \$277,500,000. There is a current appropriation balance of \$75,835,780.

2008 General Obligation Bonds

January expenditures totaled \$691, all of which was spent on the Maintenance Zone 1007 (North side Latimer St. / North side E. Haskell St. / West side N. Utica Ave.) project. To date, \$208,698,602 has been spent in this fund. Encumbrances and commitments total \$37,729,440. Life to date appropriations for the 2008 General Obligation Bond Fund total \$230,054,937. There is a current appropriation balance of \$20,923,872.

2005 General Obligation Bonds

There were \$40,986 expenditures in January, all of which was spent on the 91st St: Memorial to Mingo Rd project. To date, \$74,004,600 has been spent in this fund. Encumbrances and commitments total \$3,126. Current appropriations for the 2005 General Obligation Bond Fund total \$74,919,257. There is a current appropriation balance of \$911,531.

Respectfully submitted,

Ashley Webb, Chair



Attachments

cc: James Wagner
Keith Eldridge
Gary Hamer



FINANCIAL REPORT TO CITY COUNCIL

Wednesday, February 3, 2021

I. Financial Report

Revenue: 2014 Extended 1.1 Percent and 2016 Vision 0.305 Percent Sales Tax Funds

	Fiscal Year to Date		
	January	Thru January	Actual vs Budget
Actual	\$ 9,360,728	\$ 72,669,434	\$ 3,174,081
Adopted Budget - Current Year	9,138,718	69,495,353	222,010

Expenditures

Fund	January	Fiscal Year to Date Thru January
4001, 4003-4004 - Tulsa Vision Rev Bonds	\$ 2,584,613	\$ 42,945,026
4000 - Tulsa Vision Sales Tax	(1,499,376)	13,796,362
405 - 2014 Sales Tax	5,683,033	32,824,524
404 - 2008 Streets Temporary Sales Tax	127,517	2,458,550
402 - 2006 Special Extended Sales Tax	37,685	939,016

II. Expenditures in Other Funds

Fund	January	Fiscal Year to Date Thru January
403 - 2006 Advance Funded Sales Tax	0	0
401 - 2001 Sales Tax	11,359	241,084
408 - 2020 GO Bond	223,927	940,161
427 - 2014 GO Bond	4,723,827	16,741,816
426 - 2008 GO Bond	691	1,187,615
425 - 2005 GO Bond	40,986	194,294
TOTAL \$	5,000,790	\$ 19,304,969

III. Items for the City Council's Attention

- A. Monthly Financial Reports
- B. STOC Committee and Subcommittee Minutes and Reports

IV. Attachments

- A. Attendance Record for the last 12 months
- B. STOC Committee and Subcommittee Minutes and Reports

Respectfully submitted,

Ashley R. Webb, Chair

Attachments

cc: James Wagner
 Keith Eldridge
 Gary Hamer

MAJOR CAPITAL IMPROVEMENTS CONSTRUCTION FUNDS SUMMARY

As of January, 2021

	CURRENT		EXPENDITURES		ENCUMBERED	PERCENT	BALANCE
	APPROPRIATIONS		Current Month	To Date			
Fund 401 and Fund 403							
2001 Third Penny Sales Tax and 2006 Advance Funded Sales Tax	\$ 112,418,465	\$	11,359	\$ 112,333,976	\$ 59,407	100%	\$ 25,083
Fund 402							
2006 Third Penny Sales Tax Extension	\$ 271,344,933	\$	37,685	\$ 256,329,321	\$ 4,429,258	96%	\$ 10,586,355
Fund 404							
2008 Sales Tax Special Temporary Streets Fund	\$ 145,493,500	\$	127,517	\$ 145,176,624	\$ 189,277	100%	\$ 127,600
Fund 405							
2014 Sales Tax Fund	\$ 567,377,764	\$	5,683,033	\$ 306,957,857	\$ 58,183,268	64%	\$ 202,236,639
Fund 406: 4000							
2016 Sales Tax Fund	\$ 127,143,645	\$	(1,499,376)	\$ 73,646,525	\$ 22,375,578	76%	\$ 31,121,541
Fund 406: 4001, 4003, 4004							
2016 Revenue Bond Fund	\$ 350,600,000	\$	2,584,613	\$ 163,939,250	\$ 117,776,736	80%	\$ 68,884,015
Fund 428							
2020 General Obligation Bonds	\$ 17,500,000	\$	223,927	\$ 956,901	\$ 4,113,857	29%	\$ 12,429,242
Fund 427							
2014 General Obligation Bonds	\$ 277,500,000	\$	4,723,827	\$ 163,934,780	\$ 37,729,440	73%	\$ 75,835,780
Funds 426							
2008 General Obligation Bonds	\$ 230,054,937	\$	691	\$ 208,698,602	\$ 432,462	91%	\$ 20,923,872
Funds 425							
2005 General Obligation Bonds	\$ 74,919,257	\$	40,986	\$ 74,004,600	\$ 3,126	99%	\$ 911,531
Fund 740: 7401-7408							
TMUA--Water Capital Fund	\$ 380,354,697	\$	3,409,347	\$ 262,318,517	\$ 48,735,240	82%	\$ 69,300,940
Funds 750: 7501-7520							
TMUA-Sanitary Sewer Capital Funds	\$ 484,713,375	\$	1,028,948	\$ 343,367,672	\$ 78,246,225	87%	\$ 63,099,477

MINUTES

Sales Tax Overview Committee Meeting

January 26, 2021, 8:00 a.m.
10 North, 175 E 2nd St. and GoTo Meeting

The Sales Tax Overview Committee met for the regular monthly meeting at 8:00 a.m. on January 26, 2021.

I. Call to Order

Chair Ashley Webb called the meeting to order at 8:04 a.m.

The following members were present in person:

Jesse Guardiola	Ashley Webb
Rhonda Hinrichs	
Steve King	
Karen O'Brien	
Steven Watts	

The following members were present virtually:

Pamela Amburgy	Scott Grizzle	Renee Plocek
David Blatt	Jonathan Hall	Kathy Sebert
Janae Bradford	Linda Jenkins	
Marcia Bruno-Todd	Mareo Johnson	
Ellouise Cochran	Paul McTighe	

The following members were absent:

Alex Gomez	Sylvia Powell	Daryl Tannehill
------------	---------------	-----------------

Also present:

Gary Hamer	Jarrod Moore	Anne Boyd
------------	--------------	-----------

II. Approval of Minutes

There was not a quorum of members present in person as required by State Statute. No votes were taken at this meeting.

III. Chair's Report

The Chair's Report to Council was given by Rhonda Hinrichs. She stated that the report went well and that she highlighted the Berry Park Pool Reconstruction. She stated that there were some audio problems, so the Council was unable to ask questions.

IV. Financial Report

The December collections were \$9.28M which is about 2.8 percent over budget. Current sales tax collections are about 4.9 percent ahead of budget for the year to date. Both the current budget and collections are below the previous year.

V. Subcommittee Reports

A. Tulsa Vision Economic Development

Pamela Amburgy and Ashley Webb gave an overview. It was reported that the Cox Business Center was nearing completion. The art is to be installed in April. There are some cracking issues with the concrete that will be addressed when the weather permits, probably late spring. Work is continuing on the design and pre-construction requirements for the Pedestrian Bridge. The Bridge came in over budget due to increased costs of supplies and materials. Funds are being sought to cover the overage. The Gilcrease Museum is requesting a variance for the building height. There were no further comments or questions, and the report was accepted.

B. Public Safety

Ashley Webb gave an overview. He stated that there was no update from INCOG on the Route 66 Xperience. Repeated requests for someone to give an update on the status of the project have gone unanswered. It was reported that several of the items identified in the ADA study for City owned buildings will be addressed by upcoming construction projects at those sites so they will not be addressed separately by the ADA Transition Plan. A contract to address items in the ADA Parks Transition plan has been executed. The parks involved in this are Centennial, Hicks, and Reed. There were no further comments or questions, and the report was accepted.

C. Parks

Several members were called on to give an overview. Punch list inspections were held at Patrick and Plaza parks for the playground and safety surfacing. Final completion of these projects has been delayed because the shade shelters are held up in manufacturing due to COVID. Construction on McClure and Penny playground and safety surfacing began in December with 150-day construction timeline. Bids for Reed Park pool reconstruction and water playground will be opened later this month. Construction is slated to start in March. There were no further comments or questions and the report was accepted.

D. Street and Stormwater / Water and Sewer

Paul McTighe presented the overview. There was nothing of note in Stormwater. Water and Sewer did not give an update on Woodycrest 3. The Committee will be kept informed of the progress of this project, but, there will be no in person reporting by this group. These groups are nearing the end of the project lists that are funded in sales tax. The prices on Crow Creek Bridge came in high. It may be that they will have to completely close Peoria while work on the bridge is being done, around 180 days. There were no further comments or questions and the report was accepted.

VI. Unfinished Business

VII. New Business

A. Chair Report presenters for next month(s)

	<u>Presenter</u>	<u>Backup</u>
Feb. 10	Ashley Webb	Jesse Guardiola
Mar. 3	Mareo Johnson	Ashley Webb

3/3, 4/7, 5/5, 6/2, 7/14, 8/4, 9/1, 10/6, 11/3, 12/1

VIII. Adjournment

The meeting was adjourned at 8:44 a.m.

Ashley Webb, Chair



Linda Jenkins, Vice Chair



Sales Tax Overview Committee

STOC

SALES TAX OVERVIEW COMMITTEE

12-Month Attendance Record

Jan-21

Member	Expires	District	Jan-21	Feb-20	Mar-20	Apr-20	May-20	Jun-20	Jul-20	Aug-20	Sep-20	Oct-20	Nov-20	Dec-20	# Attended	# Possible	Comments
Hinrichs, Rhonda	Dec-22	1	P	P	C	C	A	P	P	P	P	A	A	A	6 of 12		
Jenkins, Linda (Vice-Chair)	Dec-24	1	P	P	C	C	P	P	P	P	P	P	P	A	9 of 12		
McTighe Jr., Paul	Dec-22	2	P	P	C	C	P	P	P	P	P	P	P	P	10 of 12		
Powell, Sylvia	Dec-20	2	A	A	C	C	A	A	A	A	P	P	A	A	2 of 12		D.Oxford Mar-Jul 2020
O'Brien, Karen (Secretary)	Dec-22	3	P	P	C	C	P	P	P	P	P	A	P	P	9 of 12		
Plocek, Renee	Dec-20	3	P	A	C	C	A	A	P	A	A	A	A	A	2 of 12		
Blatt, David	Dec-22	4	P	P	C	C	P	P	A	P	P	P	A	A	7 of 12		
Webb, Ashley (Chair)	Dec-20	4	P	P	C	C	P	P	P	P	P	P	P	P	10 of 12		
Sebert, Kathy	Dec-22	5	P	P	C	C	P	P	P	P	P	P	P	A	9 of 12		
Tannehill, Daryl	Dec-20	5	A	P	C	C	A	A	P	A	P	A	A	A	3 of 12		
Guardiola, Jesse	Dec-22	6	P	A	C	C	P	P	NM	P	P	OT	P	P	7 of 11		
Gomez, Alex	Dec-20	6	A	A	C	C	A	A	A	A	A	A	A	A	0 of 12		
Cochrane, Ellouise	Dec-22	7	P	OT	C	C	P	P	P	A	P	A	P	P	7 of 12		
Bradford, Janae	Dec-24	7	P	P	C	C	P	A	A	P	P	P	P	P	8 of 12		
Hall, Jonathan	Dec-22	8	P	P	C	C	P	P	P	P	P	P	P	P	10 of 12		
King, Steve	Dec-24	8	P	OT	C	C	P	A	NM	P	P	P	P	P	7 of 11		
Grizzle, Scott	Dec-22	9	P	P	C	C	P	P	A	P	P	P	P	A	8 of 12		
Watts, Steven	Dec-20	9	P	P	C	C	P	A	P	P	A	P	A	A	6 of 12		
Amburgy, Pamela	Dec-22	M	P	P	C	C	P	P	P	P	P	P	P	A	9 of 12		
Burno-Todd, Marcia	Dec-24	M	P	A	C	C	A	A	A	P	P	P	P	A	5 of 12		K.Hughart Jan -Jul 2020
Johnson, Mareo	Dec-22	M	P	P	C	C	P	P	P	P	P	P	P	A	9 of 12		
Members Present			18	14	0	0	15	13	13	16	18	14	14	8			

A = ABSENT
P = PRESENT
NM = NO MEMBER APPOINTED
OC = OUT OF COUNTRY
OT = OUT OF TOWN on Business

C = NO MEETINGS HELD DUE TO COVID 19

Prepared by City of Tulsa
Department of Finance
Budget & Planning Division
Capital Planning Section

Tulsa Economic Development Project

Attendees:

Linda Jenkins
Paul McTighe
Ellouise Cochrane
Steve King
Kathy Sebert
Mareo Johnson
Janae Bradford

Vision Tulsa STOC 03.23.2021

Project No.	Project Name	Page No.
1 170000	Zink Lake	2
2 170000 / 147200	New Pedestrian Bridge	3
3 170020	New Trail East Bank Cousins	4-5
4 170025	23rd & Jackson Redevelopment	6
5 170030	Gilcrease Museum Expansion	7
6 170035	Cox Business Center Renovation	8
7 170040	Tulsa Fairgrounds	9-10
8 170045.2	Airport Infrastructure - AFP3	11
9 170045.4	Airport Infrastructure - AA (American Airlines)	12-13
10 170050	Tulsa Zoo Elephant Exhibit	14
11 170055	Langston Healthcare	15
12 170060	BMX National Headquarters	16
13 170065	South Mingo Corridor	17
14 170070	Public Schools Safety First Initiative	18-19
15 170080	Citywide: Commercial Revitalization & Beautification	20
16 170080	Citywide: Route 66	21-22
17 170085	Peoria - Mohawk Business Park	23
18 170100	Air National Guard MTC	24
19 170125	McCullough Park	25
20 170130	Mohawk Sports Complex	26
21 170135	GO Plan Bike Ped Master Plan	27-28
22 170140	Route 66 Train Depot	29
23 170145	Tulsa Arts Commission	30-31
24 170155	PAC Master Plan	32

Projects to be added

170005	South Tulsa Jenks Dam	
170010	Turkey Mountain Urban Wilderness	
170015	Levee District 12 Rehabilitation	

Completed projects

		Compleat. Date
170035	Cox Arena District RFP	Jan-19
170045.1	Airport Infrastructure - AA Tail Slots	Jan-19
170095	Community Health East Clinic	Apr-20
170110	North Peoria Connection, 56th Street to Mohawk	Mar-20
170115	TCC Career Placement	Aug-19

EXHIBIT "F"



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date: 03.16.21

From: [City of Tulsa](#)

Contracting Party Representative: [Mary Kell \(Brooke Caviness, COT\)](#)

Project Name and No: [Zink Dam Modifications, Project No. 170000](#)

Project Funding:

Vision Tulsa Funding No. [170000.ArchEngr.4001-40013122-541101](#)

Total Funding: [\\$54,673,411.53](#)

Available Funding: [\\$54,673,411.53 Funded](#)

Total Expenditures:

 Contracted: [\\$47,011,196.99](#)

 Spent to date: [\\$13,173,605.63](#)

Status of any additional funding sources necessary for completion

- \$8,400,000.00 stormwater enterprise funding BA approved by Council 07.29.2020

Project Updates:

Status of Design and Construction

- Design Fees: CH2M Hill \$7,935,865.50
- Design Fees: HISINC, LLC \$140,832.00
- Crossland Construction Company: \$38,934.499.49
- Construction time frame is 850 days. Start 10.19.20, completion March 2023
- Obermeyer Gate Purchase Order: \$7,249,000.00 Signed by Mayor 01.21.21
- 404 permit approved. Operations Agreement approved by RPA 10.19.20.
- Construction **17.9%** complete
- **Compressor building construction pending pedestrian bridge 404/408 permits**
 - Located on west bank near Corps of Engineers Levee
 - Houses the air compressor equipment and elec. controls for operations of dam gates
 - Compressor building is integrated into levee system, thus requiring 408 permit
 - Located to get compressor equipment and controls above 100-year floodplain

EXHIBIT "F"



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: [City of Tulsa](#)

Contracting Party Representative: [Mary Kell \(Jeff Stava, RPA/TGP and Brooke Caviness, COT\)](#)

Project Name and No: [Arkansas River Pedestrian Bridge, Project No. 147200](#)

Project Funding:

Vision Tulsa Funding No.	170000.ArchEngr.4001-40013122-541101
Tulsa Sales Tax Funding No.	147200.Bridges.5453103.4058200-541107
Tulsa Sales Tax Funding No.	144104.Streets.5453101.6011-4043122-541106
Tulsa Sales Tax Funding No.	144104.Streets.5453104.6014-4053122-541106
Total Vision Funding:	\$15,000,000.00
Total Sales Tax Funding:	\$9,400,000.00 (+ \$3,000,000.00 Tier II)
Available Funding:	\$27,400,000.00 Funded
Total Expenditures:	
Contracted:	\$24,685,814.00
Spent to date:	\$3,918,580.57

Status of any additional funding sources necessary for completion

- **\$3,000,000.00 = Tier II Funding approved from leftover monies from past bond projects**

Project Updates:

Status of Design and Construction Activities

- Design Engineer: Schlaich Bergermann Partner (SBP)
- Design/Landscape Architect: Michael Van Valkenburgh Associates, Inc. (MVVA)
- Design and add alternate options for bridge enhancements included:
stainelss steel handrails, benches, westbank landscape and asthetic lighting
- Bids opened 09.22.2020
- TGP Board met on 10.23.20 to review and approve \$22,579,092 (packages approved include demo/piers/steel arches/deck/electric/general conditions, insurance, contingency and CM fee) included in GMP #1 with Crossland
- 2 bidders withdrew their bids after bid opening, adding approx \$1.3m in costs, making the new total cost \$33m (including \$2.4m contingency and \$1.4m add alternates)
- Finalized value engineering (VE) and cost cutting opportunities working with Mayor's Office to finalize list and are finalizing fundraising plan
- Bridge will begin and end in current ped bridge termination locations
- Project was included in TIGER grant scope (although no federal funds are applied to the project)
- The design team and the City **have satisfied all of FHWA (Federal Highway Admin) requirements** for the TIGER grant
- Bridge construction will be coordinated with Zink Dam work, scheduled to begin **Spring 2021** -1 through 2022 (weather and river flow dependent)
- 404 permit -- USACE has 404/Nationwide permit ready, they are finalizing the levee 408 permit, expect to receive both permits **by late March, 2021 - ONGOING**

EXHIBIT "F"



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date:	<u>03.16.2021</u>
From:	<u>City of Tulsa</u>
Contracting Party Representative:	<u>Mary Kell (Glen Sams, COT)</u>
Project Name and No:	<u>New Trail East Bank 101st to Cousins Park, Project No. 170020</u> <u>a.k.a. River Parks Trail 101st to 121st</u>

Project Funding:

Vision Tulsa Funding No.	<u>170020.ArchEngr.4000-40003122-541101</u>
Total Funding:	<u>\$4,000,000.00</u>
Available Funding:	<u>\$600,000.00 Funded</u>
Total Expenditures	
Contracted:	<u>\$68,474.00</u>
Spent to date:	<u>\$68,454.68</u>

Status of any additional funding sources necessary for completion

-
- Applied for a TAP (Transportation Alternative Program) grant through INCOG to fund design and construction of section from Vensel Creek to Creek Turnpike - 11.20.2020
 - **Received grant award March 2021 of reduced scope for design only = \$133,991.00**

Project Updates:

Status of Design and Construction

-
- Design Consultant: LandPlan Consultants, Inc. (LPCI)
 - Conceptual Design Fees: \$68,474
 - Construction expected to happen through multiple phases
 - Will design trail enough to develop a real cost then apply for TAP funds again
 - TAP grants have 2 categories: small is \$400,000, Large is \$ 1 Million
 - Consultant submitted final deliverables on 02.16.18
 - Conceptual Cost Estimate for the trail is \$6,470,000 (includes construction cost , design fees soils testing, Inspection, permitting and utility relocations)
 - Total cost is expected to be \$17,000,000 if the trail aquisition cost is added (\$10,530,000)
 - This excludes the aquisition cost of the dam site parcel.

2019 - 2021 INCOG URBANIZED TAP RECOMMENDED PROJECTS

Project Sponsor	Application Project Description	Federal Funds Requested	Local Funds Proposed	Recommended Project Description	Federal Funds Recommended	Local Funds Recommended	% Match	TOTAL
Broken Arrow	Signed bike route to connect neighborhoods and parks. Three Hawk Beacons and sidewalks/sidepaths to connect the existing sidewalks and multi-use trails at 1) Pittsburg St. & Elm St. 2) Washington St. & Juniper Ave. 3) New Orleans St. & Oak Ave.	\$1,000,000	\$420,675	Hawk Beacons and sidewalk/sidepath only	\$857,802	\$285,934	25%	\$1,143,736
Coweta	Sidewalk from Broadway (Hwy 72) to 305th Ave along Pecan St. to serve schools' campus. Project includes crossing over a creek and the UPRR line.	\$684,558	\$171,140	Entire Project	\$684,558	\$171,140	20%	\$855,698
River Parks Authority	Trail from River Spirit Casino to 91st St. The dual bike/ped trails will each be 10' wide. The fence line will be moved 20' to the west. The project will include environmental mitigation.	\$867,801	\$230,701	Design plans, construction documents, environmental mitigation and moving fence line only.	\$460,285	\$115,071	20%	\$575,356
Tulsa County	Shared-use path on 56th St N from Osage Prairie Trail to Lewis Ave. and sidewalks and new striping to include bike lanes on Lewis from 56th St N to E 66th St N	\$1,000,000	\$1,055,570	Sidewalk and restriping on Lewis Ave and expenses related to these projects.	\$444,164	\$148,055	25%	\$592,219
City of Tulsa <i>ADA & Memorial</i>	Sidewalks and ADA curb ramps on arterial streets. Memorial Dr. from 61st St S to 71st St S; 31st St S & U.S. 169; 41st St S & U.S. 169; 51st St S & U.S. 169; 61st St S & U.S. 169	\$615,000	\$205,000	Entire Project	\$615,000	\$205,000	25%	\$820,000
City of Tulsa <i>River Trail</i>	Construction of an asphalt trail from Vensel Creek crossing to the Creek Turnpike bridge, including retaining walls, bollards and striping.	\$990,000	\$490,000	Design plans and construction documents	\$107,193	\$26,798	20%	\$133,991
City of Tulsa <i>Schools & RFB</i>	RRFBs at Peoria Ave & 36th Pl S; Peoria Ave & 67th St S; Birmingham Ave & 11th St S; Lansing Ave & south of Pine; Denver Ave & Easton St; 61st St S & west of Yale. ADA ramps and sidewalks at various TPS & Union Schools	\$550,000	\$180,000	Entire Project	\$550,000	\$180,000	25%	\$730,000
		\$5,707,359	\$2,753,086		\$3,719,002	\$1,131,998		\$4,851,000

EXHIBIT "F"



CITY OF TULSA Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: City of Tulsa

Contracting Party Representative: Mary Kell (Marsha Hinds, COT)

Project Name and No: 23rd & Jackson Redevelopment Site - Relocation Study
Design and Acquisition, Project No. 170025

Project Funding:

Vision Tulsa Funding No. 170025.ArchEngr.4000-40003122-541101

Total Funding: \$1,000,000.00

Available Funding: \$500,000.00 Funded

Total Expenditures:

Contracted: \$403,652.06

Spent to date: \$403,341.35

Status of any additional funding sources necessary for completion

- No additional funds are expected to be needed

Project Updates:

Status of Design and Construction

- Design Consultant: Cyntergy
- Scope includes: planning, design work and partial acquisition costs to relocate Public Works, update master plan site at Harvard and Mohawk, appraise and acquire operation yard location
- Draft Final report being reviewed by Administration, February 2020
- Feasibility study for 23rd & Jackson redevelopment site to be done
- Acquisition of 2 parcels - Tulsa County Yard on North Harvard - \$320K (Vision funding), 56th & Garnett - \$1.46M (water enterprise funds) - Closing for both properties held 08.13.2020
- County has vacated North Harvard site as of 12.31.20. Environmental work ongoing by County.
- Traffic Engineering will be using the County site to move and store existing poles and materials from the west yard.
- **No changes on this project.**

EXHIBIT "F"



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: City of Tulsa

Contracting Party Representative: Mary Kell (Susan Neal, Gilcrease)

Project Name and No.: Gilcrease Museum Expansion, Project No. 170030

Project Funding:

Vision Tulsa Funding No. 170030.ArchEngr.4001-40013122.541101

Total Funding: \$83,600,000.00

Available Funding: \$65,000,000.00 Funded

Total Expenditures

 Contracted: \$52,814,765.57

 Spent to date: \$4,322,352.99

Status of any additional funding sources necessary for completion

- Private fundraising to occur - \$10 million raised to date for construction and design

Project Updates:

Status of Design and Construction

- Gallagher & Associates (G&A) - Owner's Representative (TU and City of Tulsa) and exhibit design
- G&A agreement (\$4,765,000.00)
- SmithGroup & 1 Architecture - architects, agreement through Schematic Design (\$2,920,833.28)
- Enercon agreement for environmental (\$106,860.00)
- Flintco CM agreement (\$45,022,072.29)
- Next National Board meeting **05.19.2021**
- Off-site art storage facility - closed 01.06.2021
- Task Force meeting held 03.11.2021, next is **04.15.2021**
- Weekly progress meetings held Thursdays
- 01.26.2021 BOA hearing - Special Exception to allow Museum, height variance
- **Move-in prep at off-site building underway**
- **Helmerich Center renovation completed 03.05.2021, art move started 03.08.2021**
- **Building and Exhibit design ongoing**

EXHIBIT "F"



CITY OF TULSA
Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: City of Tulsa

Contracting Party Representative: Mary Kell

Project Name and No: Cox Business Center, Project No. 170035

Project Funding:

Vision Tulsa Funding No. 170035.ArchEngr.4001-40013122.541101

Total Funding: \$55,000,000 (\$500,000 of this for Master Plan RFP)

Available Funding: \$55,000,000 Funding

Total Expenditures

 Contracted: \$54,823,090.68

 Spent to date: \$54,677,439.50

Status of any additional funding sources necessary for completion

-
- No additional funds are expected to be needed

Project Updates:

Status of Design and Construction

-
- Design Consultant: Matrix Architects, Engineers and Planners Inc., Design Fees \$2,747,189.88
 - Construction Manager: TVB (Tulsa Vision Builders), CMAR - Construction Manager at Risk
 - Construction July 2018 - 06.30.2020 substantial completion. Buidling operational.
 - Public art Artist Andy Tirado - **installation April 2021**
 - Instagram for Artist - artirado1
 - Closeouts in process
 - Concrete cracking issues - **repairs late Spring 2021**

EXHIBIT "F"



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: TCPFA

Contracting Party

Representative: Mary Kell (Amanda Blair, EXPO Square)

Project Name and No: Tulsa Fairgrounds, Project No. 170040

Project Funding:

Vision Tulsa Funding No. 170040.ArchEngr.4001-400013122-541101

Total Funding: \$30,000,000.00

Available Funding: \$30,000,000.00 Funded

Total Expenditures

 Contracted: \$30,000,000.00

 Spent to date: \$28,476,454.28

Status of any additional funding sources necessary for completion

- TCPFA has secured additional funds (**\$1,652,493.28**) for Golden Driller Plaza
Total cost is \$3,176,039.00 (Vision Tulsa funding is \$1,523,545.72)

Project Updates:

Status of Design and Construction

- Design Consultant: GH2 Architects \$1,841,914.17 fees
- Construction Manager: Crossland Construction Company, Inc.
- Projects complete - \$28.5 m
- **Golden Driller Plaza:** Project on hold due to COVID-19, March 2020 - October 2020
Re-bids opened 01.21.2021, GMP (Guaranteed Maximum Price) approved
02.10.2021 TCPFA Special Meeting, **construction 03.03.2021** to 09.06.2021



CITY OF TULSA
Sales Tax Overview Committee (STOC) Report

Date: 10.16.18
From: TCPFA
Contracting Party Representative: Mary Kell (Amanda Blair, EXPO Square)
Project Name and No: Tulsa Fairgrounds, Project No. 170040

Projects List: Updated 10.09.18



VISION RENEWAL (updated 10.09.18)
PROJECT SUMMARY INFORMATION

Project Descriptions	Forecasted Cost
Construct Additional Barn & Event Plaza (Under Construction) <ul style="list-style-type: none"> Add additional Barn; will include roof structure, walls, steel frames and overhead door installation; fire suppression system. Plaza entrance gate between barn and Central Park Hall. 	
Pavilion Exterior Update (Complete) <ul style="list-style-type: none"> New exterior lighting Updated landscape Roadway resurfacing Redesigned pedestrian traffic pattern 	\$ 19.6 Million
Construct New Gate Entrances for Exterior Perimeter and Interior Wayfinding Signage (95% Complete) <ul style="list-style-type: none"> Construct masonry identification sign; install electric and light poles; re-asphalt and create sidewalk. 2 Main (High Volume) Gates include LED Information Signs. Add Gate 3 LED Information Signs (approx. \$32,500); not complete. 	
Construct Permanent Outdoor Stage (Complete) <ul style="list-style-type: none"> Construct roof and steel structure; install electric power and lighting between Pavilion and Exchange Center. 	\$ 4.1 Million
Pavilion Roof Replacement	\$ 450,000
Improve Golden Driller Entrance and Lobby <ul style="list-style-type: none"> Construct new front entrance to Expo Center to accommodate bus loading and unloading; install covered walkways. 	\$ 1.5 Million
Old Driller Stadium and Health Department Demolition and Grade Work	\$ 600,000
Architecture Fees	\$ 1.85 Million
TCPFA Expenses	\$ 226,000
Change Orders and Unidentified Costs for above Projects	\$ 1.674 Million
Project Totals:	\$ 30 Million

EXHIBIT "F"



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: [City of Tulsa](#)

Contracting Party Representative: [Mary Kell \(Max Wells, COT\)](#)

Project Name and No: [Airport Infrastructure - Air Force Plant Three \(AFP3\) Electrical Upgrades, Project No. 170045.2](#)

Project Funding:

Vision Tulsa Funding No. [170045.ArchEngr.4001-40013122-541101](#)

Total Funding: [\\$27,300,000.00](#)

Available Funding: [\\$9,000,000.00 Funded](#)

Total Expenditures:

Contracted: [\\$1,865,260.21 \(\\$288,612.85 + \\$1,576,647.36\)](#)

Spent to date: [\\$1,324,474.16](#)

Status of any additional funding sources necessary for completion

- No additional funding needs projected

Project Updates:

Status of Design and Construction

- Cynergy is engineer
- Scope includes prioritized electrical upgrades for Navistar and Spirit
- Spirit and Navistar have \$22+ million in total needs
- Project has been split into 2 parts - Navistar (\$4M) and Spirit (\$5M)
- **Navistar**
 - Contract executed with S.E. Tulsa Construction, Inc. 08.12.19 (\$1,576,647.36)
 - Construction began on 09.29.2020 with social distancing protocols in place
 - Work ongoing with equipment installation, construction is **95%** overall
 - Punch list items working. Final inspection and Closeout pending.**
- **Spirit**
 - Spirit has decided to do electrical portion of work with separate Spirit funding
 - Phase 1 paving projects (Areas 1 - 4) completed 04.30.2020 \$2,407,759.00
 - Phase 2 : Completed mill and patch and overlay on Area 5 - 07.30.2020.
 - Area 6A & 6B completed 09.30.2020
 - Area 9 Completed 12.31.2020

Amendment in process to expend remaining \$1.6 M in funds on additional and different scope from original agreement, including: paving, striping, fire hydrants and backflow preventers on Spirit campus. **Ongoing**

EXHIBIT "F"



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: City of Tulsa

Contracting Party Representative: Mary Kell

Project Name and No: Airport Infrastructure - AA (American Airlines)
Project No. 170045.4

Project Funding:

Vision Tulsa Funding No. 170045.ArchEngr.4001-40013122-541101

Total Funding: \$27,300,000.00 (includes all airport projects)

Available Funding: \$14,500,000.00 Funded

Total Expenditures:

 Contracted: \$12,250,000.00

 Spent to date: **\$47,135.76**

Status of any additional funding sources necessary for completion

- No additional funding needs projected

Project Updates:

Status of Design and Construction

- Basewide reinvestment projects determined - \$14,500,000 total (includes tail slot project).
- 11.04.2020 AA presented to City Council bond plan.
- TMAP bond sale not to exceed \$175 million
- Agreement with list of projects signed by Mayor 12.02.2020
- List of projects on following page
- **Invoices for work starting to come in from AA 03.12.2021**

EXHIBIT A – SELECTED IMPROVEMENTS

Hangar 80 RE-skin

Estimated Cost: \$1.5M

Hangar 80 skin is past its planned useful life. American Airlines (AA) will remove all the through wall penetrations, replace the skin of the hangar, and reattach the equipment. AA will also inspect the fire foam generators and make any necessary repairs. AA will protect the wall vents from bird and insect infiltration.

American Airlines Engine Repair and Overhaul (AAERO) Auxiliary Power Unit (APU)

Estimated Cost: \$2.17M

AA will procure and install new test equipment in the no longer used MD80 test facility to allow for the APU's to be tested there after they have been repaired and inspected. The new test cells will allow for the testing of APU's that AA was not able to test previously.

Master plan

Estimated Cost: \$0.575M

Evaluate and plan the overall highest and best use of all buildings and open spaces at AA's maintenance base, including:

1. Evaluate the proposed location of Hangar 7 and Base Support Facility (BSF).
2. Evaluate and provide options for the potential layout to repurpose hangars 1-4.
3. Evaluate and propose alternate designs for parking and entry points of traffic flow, truck traffic and entrances, and pedestrian access; evaluate and propose alternate designs for the location of the main entrance to the base south guard house and the main guard house.
4. Plan out the industrial wastewater treatment plant (IWTP) project and provide the best location and size for the new building; recommend paving area and berm location, and the removal of outdated buildings.
5. Evaluate the condition of base utilities and make recommendation as to what needs to be replaced in electrical, storm water, sewer, and fire protection utilities.

Plating Shop Roof and Make-Up Air Units (MAU)

Estimated Cost: \$2.4M

Plating Shop is in need of roof replacement. AA will replace decking, flashing, and MAU's curbs. AA will coordinate the phasing of how to keep the shop open with the replacement of the roof. AA will replace MAU's that are associated with the shop.

Central Utility Plant (CUP) Cooling Tower and Design & Hangar 6 Cooling Tower Construction

Estimated Cost: \$5.6M

Design and replace the Hangar 6 CUP Cooling Tower with a similar configuration to what exists today, including the replacement of cooling towers, condenser water pumps, chillers, primary chilled water pumps, secondary chilled water pumps, boilers, deaerators, boiler feed water pumps, steam condensate return pumps, fuel oil pumps, controls, miscellaneous valves and accessories, switchgear and generators.

EXHIBIT "F"



CITY OF TULSA Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: City of Tulsa

Contracting Party Representative: Mary Kell (Gary Schellhorn, COT)

Project Name and No: Tulsa Zoo Elephant Exhibit, Project No. 170050

Project Funding:

Vision Tulsa Funding No. 170050.Buildings.4003-40033122-541104

Total Funding: \$25,000,000.00

Available Funding: \$20,000,000.00 Funded

Total Expenditures:

 Contracted: \$1,545,846.12 (\$1,515,846.12 Design + \$30,000 CM)

 Spent to date: \$385,435.19 Design

Status of any additional funding sources necessary for completion

- No additional funds are expected to be needed

Project Updates:

Status of Design and Construction

- Design Consultant: SelsersSchaefer Architects, Design Fees: \$1,515,846.12
- CM (Construction Manager) selection: Nabholz Construction
- 25% Design Documents received 07.20.2020
- 65% Design Documents received 02.15.2021
- 65% Design Documents review meeting held 03.11.2021
- **Design fees being gathered to move building out of compensatory storage area**
- **Moving building will remove need for 404 permit**

EXHIBIT "F"



CITY OF TULSA Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: OSU - LRFP (Long Range Facilities Planning)

Contracting Party Representative: Mary Kell (Mike Buchert, OSU - LRFP)

Project Name and No: Langston Healthcare Professions Complex, Project No. 170055

Project Funding:

Vision Tulsa Funding No. 170055.ArchEngr.4001-40013122-541101

Total Funding: \$16,250,000.00

Available Funding: \$16,250,000.00 Funded

Total Expenditures

 Contracted: \$16,250,000.00

 Spent to date: \$4,898,986.83

Status of any additional funding sources necessary for completion

- No additional funds are expected to be needed

Project Updates:

Status of Design and Construction

- OSU LRFP (Long Range Facilities Planning) providing project oversight
- Design Fees: Beck (\$1,017,385.00)
- Construction Manager: Flintco pre-con - \$75,310.00; OSU LRFP - (\$377,588.00)
- No asbestos found in existing building
- OAC (Owner Architect Contractor) calls set up every 2 weeks started 06.05.2020
- Construction: June 2020 to November 2021
- Jobsite camera: <http://ibeamsystems.com/camera/langstonuniversityproject>
- Overall construction **41%** complete
- Masonry walls at the hardened area roughly 95% complete.
- **Interior metal stud framing has begun**
- **Exterior metal stud framing is 90% complete, sheathing is 90% complete**
- **Roofing is approximately 60% complete on area B**
- **MEP overhead and in-wall rough-in has begun**

EXHIBIT "F"



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: [City of Tulsa](#)

Contracting Party Representative: [Mary Kell](#)

Project Name and No: [BMX National Headquarters, Project No. 170060](#)

Project Funding:

Vision Tulsa Funding No. [170060.ArchEngr.4001-40013122-541101](#)

Total Funding: [\\$23,000,000.00](#)

Available Funding: [\\$ 23,000,000.00 Funding](#)

Total Expenditures

 Contracted: [\\$22,777,606.41](#)

 Spent to date: [\\$9,791,110.04](#)

Status of any additional funding sources necessary for completion

- EDA Grant funding has been applied for, did not receive (\$1.2 M) as determined 06.11.19
- TPA (Tulsa Parking Authority) approved funding for parking lot - \$2.0 M on 08.22.19
Budget Amendment for \$2.0M to Council 02.26.2020, Mayor signed 03.09.2020
- BMX received additional funding sponsorships - \$1.5 M
- Brown Ordinance for \$3.6M approved at 05.08.19 CC meeting
- EDIF funding for \$900,000.00, approved at 06.19.19 City Council and by Mayor 07.22.19

Project Updates:

Status of Design and Construction

- Todd Architecture Group (previously Fritz Baily) is architect, Nabholz is CM
- Brownfield cleanup with funding from other sources: January 2017 to January 2020.
- Platting ongoing - multiple easement closings. Quiet Title filed with courthouse 08.04.2020
- Groundbreaking held 11.15.19, Demo of Fintube building 11.25.19 - 01.16.2020
- Updated lease executed 10.30.19 to reflect additional funding sources and obligations
- Construction: June 2020 to December 2021
- Artist coordination ongoing
- Feasibility study draft / RFP for south half of site by in process
- Jobsite camera registration: <https://oxblue.com/invite/f492d4/bmx-headquarters>;
once registered, go to: app.oxblue.com
- Arena steel roof framing started 01.04.2021, complete
- Roof panels for arena and HQ building started 02.08.21, **40%** complete
- Overall construction: **38%**

EXHIBIT "F"



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: City of Tulsa

Contracting Party

Representative: Mary Kell (Patty Parks, COT)

Project Name and No: South Mingo Corridor, Project No. 170065

Project Funding:

Vision Tulsa Funding No. 170065.ArchEngr.4001-4000131122-541101

Total Funding: \$15,000,000.00

Available Funding: \$ 15,000,000.00 Funded

Total Expenditures

 Contracted: \$8,889,408.20(\$ 295,180.17 + \$7,430,588.70 + \$742,156.00 + \$514,003.00)

 Spent to date: \$5,898,675.32

Status of any additional funding sources necessary for completion

- No additional funds are expected to be needed
- Right of Way Spent to Date: \$182,880.17

Project Updates:

Status of Design and Construction

- Current funding includes design fees for 3 phases of work, and construction for 1st phase
- **First Phase** Design Consultant: Benham Design, LLC - 71st to 81st on Mingo
 - Bids - \$7,430,588.70 - awarded Roadway option 1 (concrete)
 - Construction started 08.13.19, construction **78%** complete
 - Work started at South end of project near 81st and Mingo. Two lanes, one in each direction will be maintained throughout project.
 - South bound lanes are paved, project to be completed **April 2021 delayed due to weather**
 - **Pending Change Order for time extension**
- **Second phase** - 91st from Mingo to Memorial - Garver is consultant, contract \$813,975.00
 - Contract includes 3-4 mile MMLoS (multimodal study) - Sheridan to Garnett on 91st Street
 - \$10.7 in construction funding approved as part of Improve Our Tulsa 2019
 - Conceptual design report received 07.02.2020. The roadway recommendation is 5 lanes with bike lanes and sidewalks with alignment of the roadway to be along the section line. Estimate cost to construct the roadway is 8.3 million.
 - MMLoS report received 07.24.2020: Recommendations made for Design Segment Geometric, Transit, Bicycle & Pedestrian, Access & Mobility, Safety and Lighting.
 - Preliminary design plans submitted December 2020 **plans in review**
- **Third phase** - 81st to 91st on Mingo - Poe is consultant
 - Current funding only includes design, 60% plans submitted March 2020
 - Proposed design will include a 5-lane section with 8-inch barrier curb.
 - Lane dimensions: (14', 12', 13', 12', 14') 5-ft ADA sidewalks on both sides
 - Traffic signal modifications at 81st St and 91st Street intersections.
 - New drainage system to replace existing ditches.
 - Estimated Construction cost: \$9,000,000.00. Does not include ROW or Utilities.
 - Four parcels needed. One will involve Meadowbrook Golf Course.
 - ROW evaluation of Meadowbrook Golf Course completed with past report from February 2006
 - Contract fulfilled at 60% plans. Contract end 09.01.2020.
 - Construction funding in 2026 (earliest). Design will be completed at a later date.



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date:	03.16.2021
From:	City of Tulsa
Contracting Party Representative:	Mary Kell (Brent Stout, COT)
Project Name and No:	Public Schools Safety First Initiative, Project No. 170070

Project Funding:

Vision Tulsa Funding No.	170070.ArchEngr.4001-40013122-541101
Total Funding:	\$14,500,000.00
Available Funding:	\$ 14,500,000.00 Funded
Total Expenditures	
Contracted:	\$2,512,000.00 Design
Spent to date:	\$2,334,393.79
Contracted:	\$5,522,542.84 Construction
Spent to date:	\$3,773,617.74

Status of any additional funding sources necessary for completion

- No additional funds are expected to be needed

Project Updates:

Status of Design and Construction

- Design Consultant: Lee Engineering, LLC, design fees \$442,000; Amendment 1 - \$620,000; Amendment 2 - \$500,000; Amendment 3 - \$950,000
- **Bid package 1:** Punch list completed 09.04.2020. Field Engineering to issue final payment and invoke warranty and bond period.
- **Bid package 2:** Construction has been completed at all Priority 1 and Priority 2 Schools. Final inspection was held 10.08.2020. Contractor has completed all punch list items. Final payment routing for Mayor's signature.
- **Bid Package 3:** Lighting installation complete for Priority 1 and 2 schools. **TPS has executed bus shelter agreement and has delivered to City for signature. All bus shelters have been included in Bid Package 4. All work originally in Bid Package 3 has been done or will be done in Bid Package 4. No project plans will be produced.**
- **Bid Package 4:** Project consists of signing, pavement markings, sidewalks, drainage improvements, pavement, lighting and traffic signal improvements at Priority 3, 4 and 5 schools. Mylar plans submitted 10.19.2020, routing for approval signatures, and bidding to follow. ROW documents have been provided to CoT for acquisition. Construction anticipated to begin **Summer 2021**.

Vision Tulsa Project No 170070
 Public Schools Safety First Initiative Priority Schools List
 Updated 01.22.2020

Priority 1 Schools	Priority 2 Schools	Priority 3 Schools	Priority 4 Schools	Priority 5 Schools
ACADEMY CENTRAL	ANDERSON	TRAICE	CARNEGIE	COLLEGE BOUND
JOHN HOPE FRANKLIN	CARVER	BURROUGHS	CENTRAL JR & HIGH	TULSA MET
CELIA CLINTON	COOPER	WAYMAN TISDALE FINE ARTS ACADEMY	DISNEY	PEARY
UNITY LEARNING ACADEMY	DUAL LANGUAGE ACADEMY	DOLORES HUERTA	EDISON PREP	PHOENIX RISING
JONES (CLOSING 6/19)	EAST CENTRAL HIGH	EAST CENTRAL JR HIGH	ELIOT	PROJECT ACCEPT
LEWIS & CLARK	EISENHOWER & GRIMES (GRIMES CLOSING 6/19)	EMERSON	GRISSOM	STREET SCHOOL
LINDBERGH	GILCREASE	EUGENE FIELD	HOOVER	TSAS/TFA
MARK TWAIN (CLOSING 6/19)	KERR	HALE HIGH	KENDALL-WHITTIER	LEGACY UPPER
CLINTON WEST	MCCLURE	HALE JR HIGH	KEY	LEGACY PRIMARY
ROBERTSON	ECDC REED	HAMILTON	KIPP	TPS PRIORITY 5
SKELLY & SKELLY PRIMARY	THOREAU DEMONSTRATION	HAWTHORNE	MCKINLEY	
TPS PRIORITY 1	ALCOTT	LANIER	MEMORIAL HIGH	
JENKS EAST ELEMENTARY	WEBSTER MIDDLE/HIGH SCHOOL	COUNCIL OAK (LEE)	MEMORIAL JR HIGH	
JENKS EAST INTERMEDIATE	SPRINGDALE	MACARTHUR	MITCHELL	
JENKS SOUTHEAST ELEMENTARY	BELL & BELL PRIMARY	MARSHALL	MONROE DEMONSTRATION	
JENKS WEST ELEMENTARY	TPS PRIORITY 2	MAYO/WILSON	OWEN	
JENKS MIDDLE SCHOOL	BOEVERS ELEMENTARY	MCLAIN HIGH	BOOKER I WASHINGTON	
JENKS PRIORITY 1	DARNABY ELEMENTARY	PATRICK HENRY	TPS PRIORITY 4	
CEDAR RIDGE ELEMENTARY	JARMAN ELEMENTARY	ROGERS JR & HIGH		
CLARK ELEMENTARY	ROSA PARKS ELEMENTARY	SALK		
GROVE ELEMENTARY	UNION FRESHMAN ACADEMY	SEQUOYAH		
JEFFERSON ELEMENTARY	UNION PRIORITY 2	WHITMAN		
UNION 6TH/7TH GRADE CENTER		WRIGHT (CLOSING 6/19)		
UNION HIGH SCHOOL		ZARROW INT'L		
OCHOA ELEMENTARY		TPS PRIORITY 3		
UNION PRIORITY 1				

EXHIBIT "F"



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: [City of Tulsa](#)

Contracting Party Representative: [Mary Kell \(Spencer Mitchell, COT\)](#)

Project Name and No: [Citywide and Route 66 Beautification & Reinvestment, Project 170080 - Commercial Revitalization & Beautification](#)

Project Funding:

Vision Tulsa Funding No. [170080.EngrArch.4000-40003122-541101](#)

Total Funding: [\\$11,000,000.00](#)

Available Funding: [\\$3,600,000 Funded](#)

Total Expenditures:

 Contracted: [\\$225,000.00 \(\\$125,000.00 + \\$100,000.00\)](#)

 Spent to date: [\\$125,000.00](#)

Status of any additional funding sources necessary for completion

- No additional funds are expected to be needed

Project Updates:

Status of Design and Construction

Three funding priorities: Citywide Commercial Revitalization (\$3,600,000.00); Route 66 (\$3,700,000.00); and Citywide Beautification (\$3,700,000.00).

- Citywide Commercial Revitalization - \$3,600,000.00 (Spencer Mitchell)
 - Retail Market study by Place Dynamincs, Inc. (\$125K) completed January 2019.
 - Retail Market study will inform use of Commercial Revitalization fund, as well as assist Route 66 Commission in targeting Route 66 funds.
 - **Project 1:** \$100K - Belo+Company (formerly Cubic) media strategy consultant Marketing campaign concepts were presented in December 2020, finalization of the selected concept is ongoing. Expected launch Q2 2021. **No change**
 - **Project 2:** \$1.1 million from Commercial Revitalization used to seed Business Resilience and Recovery Fund, this is expected to be reimbursed from CARES Act dollars to fully fund the Commercial Revitalization Strategy. City is set to start receiving repayments Feb 2021 from TEDC. **No change**
 - **Project 3:** \$1.5 million BRT (Bus Rapid Transit) Revolving Loan Fund TEDC is evaluating projects for program and providing low to zero interest loans Finance in coordination to track projects. **No change**
 - **Project 4:** \$150K (3 years x \$50K) Destination Districts - MOU signed for INCOG to administer administrator. Greenwood, Route 66, Kendall Whittier and International Districts (21st & Garnett area) ongoing

EXHIBIT "F"



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: [City of Tulsa](#)

Contracting Party Representative: [Mary Kell \(Dennis Whitaker, INCOG\)](#)

Project Name and No: [Citywide and Route 66 Beautification & Reinvestment, Project 170080 - Route 66](#)

Project Funding:

Vision Tulsa Funding No. [170080.EngrArch.4000-40003122-541101](#)

Total Funding: [\\$11,000,000.00](#)

Available Funding: [\\$3,700,000 Funded](#)

Total Expenditures:

 Contracted: [\\$187,808.23](#)

 Spent to date: [\\$187,808.23](#)

Status of any additional funding sources necessary for completion

- No additional funds are expected to be needed

Project Updates:

Status of Design and Construction

Three funding priorities: Citywide Commercial Revitalization (\$3,600,000.00); Route 66 (\$3,700,000.00); and Citywide Beautification (\$3,700,000.00).

- Route 66 - \$3,700,000.00 (Dennis Whitaker)
 - Route 66 Commission and Tulsa Planning Office staff to provide oversight
 - Retail Market study to inform targeted use of funds on corridor
 - Other uses include: marketing, wayfinding, façade grants, neon sign grants, and project maintenance.
 - Contracts / PO's: Sole Source with Claude Neon for Meadow Gold - **Complete**
 - Donation from Jim Norton - Route 66 letters and shields - **Reviewing for right-of-way issues**
 - Vehicle damage to decorative wall at 11th & Mingo interpretive site - **Complete**
 - **Reviewing additional traffic calming devices**
 - Marketing: Economic Development Committee implemented 1st a Saturday event - **ongoing**
 - **Reaching out to Visit Tulsa and City Communications for support services**
 - Façade Grants: concept and criteria under development
 - Avery Plaza Southwest - Security Cameras for new Motel Neon Sign Park - **P.O.s issued**

Updated 03.16.2021

**VISION TULSA
ROUTE 66 BEAUTIFICATION
NEON SIGN GRANT**

Below is the status of Applications which have been recommended by the Rt 66 Commission to the Mayor for Approval.
Since launching the program in April 2019, 31 signs have been Recommended by the Rt 66 Commission.

	BUSINESS	TOTAL COST	GRANT AMT	ADDRESS	STATUS	SIGN TYPE
1	Alpha Graphics	\$ 9,697.00	\$ 4,848.50	2616 E. 11th St	Permitting	New
2	Benchmark Monument	\$ 12,170.00	\$ 6,085.00	1735 E. 11th St.	Complete	Replace lost sign
3	Billy Ray's BBQ	\$ 5,230.00	\$ 2,615.00	3524 Southwest Blvd	Complete	Restoration
4	Bobby O's Pizza	\$ 15,316.00	\$ 7,658.00	1502 E. 11th St.	Waiting on Street Construction	New
5	Buck Atom's Curios on 66	\$ 16,140.00	\$ 8,070.00	1347 E. 11th St.	Complete	New
6	Burnett's Flowers	\$ 6,578.00	\$ 3,289.00	1408 E. 11th St.	Complete	New
7	Cities Service	\$ 17,223.76	\$ 8,611.88	1648 Southwest Blvd	Complete	Replace
8	Day & Nite Rug	\$ 8,162.95	\$ 4,081.48	1012 S. Egin St	Fabrication	Replace
9	Decopolis	\$ 12,348.00	\$ 5,268.50	1401 E. 11th St	Permitting	New
10	Eleventh Street Lofts & Shops	\$ 23,959.00	\$ 10,000.00	2002 E. 11th St	Permitting	Restore /Modify
11	Euforia	\$ 36,194.22	\$ 10,000.00	11730 E. 11th St.	Permitting	New
12	Flo's Burger Diner	\$ 12,700.00	\$ 6,350.00	2604 E. 11th St.	Complete	New
13	Interparts Of Tulsa	\$ 4,984.06	\$ 2,492.03	3615 E. 11th St.	Complete	Restore
14	Justin Thompson Restaurant	\$ 13,975.25	\$ 6,987.00	1115 S. Lewis Ave	Complete	New
15	Mon Amie Nails & Spa	\$ 4,652.00	\$ 2,326.00	1406 E. 11th St	Permitting	New
16	Meadow Gold Lofts & Shops	\$ 9,566.18	\$ 4,783.09	1306 E. 11th St.	Complete	New
17	Mother Road Motor Sports	\$ 7,192.31	\$ 3,596.16	2208 Southwest Blvd	Permitting	New
18	Perkins Architecture	\$ 4,950.00	\$ 2,150.00	20 S. Lewis Ave.	Complete	New
19	Renaissance Brewing Co	\$ 13,239.07	\$ 6,619.54	1147 S. Lewis Ave.	Complete	New
20	Sky Gallery(The)	\$ 8,602.82	\$ 4,301.41	1401 E. 11th St.	Permitting	New
21	Smoke on 66 BBQ	\$ 8,258.29	\$ 4,129.15	4265 Southwest Blvd	Complete	New
22	Spirit Dog Training	\$ 2,200.00	\$ 1,100.00	1621 E. 11th St	Fabrication	Modify
23	Tally's Good Food Café	\$ 25,749.00	\$ 10,000.00	1102 S. Yale Ave.	Complete	New
24	Thelms's Bar	\$ 10,289.93	\$ 5,145.00	2008 Admiral Blvd	Fabrication	Restoration
25	Transcendent	\$ 12,637.00	\$ 6,318.00	1401 E. 11th St. Unit E	Fabrication	New
26	Tulsa Community College	\$ 10,767.00	\$ 5,383.00	909 S. Boston Ave	Complete	New
27	Tulsa Market District	\$ 18,572.00	\$ 9,286.00	1102 s. Lewis Ave.	Complete	New
28	Tulsa Welding School	\$ 21,066.00	\$ 10,000.00	2547 E. 11th St.	Complete	Modify
29	U.S. Studio 66	\$ 14,723.00	\$ 7,361.50	5202 E. 11th St.	Complete	New
30	Vault Restaurant (The)	\$ 21,727.54	\$ 10,000.00	620 S Cincinnati Ave	Fabrication	New
31	Wildflower Café	\$ 18,107.83	\$ 8,953.00	1306 E. 11th St.	Fabrication	New
		\$ 406,978.21	\$ 187,808.23			

EXHIBIT "F"



CITY OF TULSA Sales Tax Overview Committee (STOC) Report

Date:	03.16.2021
From:	City of Tulsa
Contracting Party Representative:	Mary Kell (Michelle Barnett, COT; Josh Miller GKFF)
Project Name and No:	Peoria-Mohawk Business Park - Site Improvements Project No. 170085

Project Funding:	
Vision Tulsa Funding No.	170085.landimp.4000
Total Funding:	\$10,000,000.00
Available Funding:	\$5,800,000.00 Funded FY19
Total Expenditures:	
Contracted:	\$4,317,301.00
Spent to date:	\$3,981,296.82

Status of any additional funding sources necessary for completion

- Funding is sufficient for current scope of work

Project Updates:

Status of Design and Construction

- Agreement with GKFF executed October 2019
- Construction is Vision funded reimbursement of GKFF
- Design by Cedar Creek for GKFF not included in Vision reimbursement
- Reimbursement to GKFF includes mass grading and utilities. Vision-funded improvements include both GKFF-performed site mass grading, public utilities and COT-performed public roads with associated utilities.
- Bid Package #1 Mass grading with earth change permit - completed 04.30.2020.
- Bid package #2 - Public Road and Site Utilities - completed 09.30.2020
- Muncie on schedule to be complete **September 2021**
- Bid package #3 - Crossland is contractor. Pre-work 10.22.2020
Scope: water line, paving, storm and sidewalks/trail for Mohawk Boulevard and the Utica cul-de-sac off of 36th street North.
Waterline, grading, agg base and curbs are in for Utica. Paving Utica is next.
Mohawk Blvd to follow Utica. Soil stabilization in process.
46% billed, 34% time from Field Engineering

EXHIBIT "F"



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: [City of Tulsa](#)

Contracting Party Representative: [Mary Kell](#)

Project Name and No: [Air National Guard 138FW MTC \(Mission Training Center\)](#)
[Project No. 170100](#)

Project Funding:

Vision Tulsa Funding No. [170100.ArchEngr.4001-400113122.541101](#)

Total Funding: [\\$9,400,000.00](#)

Available Funding: [\\$9,400,000.00 Funded](#)

Total Expenditures:

 Contracted: [\\$9,347,000.00](#)

 Spent to date: [\\$9,327,000.00](#)

Status of any additional funding sources necessary for completion

- No additional funds are expected to be needed

Project Updates:

Status of Design and Construction

- Design Consultant: LWPB Architects, design fees \$839,545.33
- Construction Manager (CM) Crossland, CM at Risk
- Building operational June 2020
- Closeouts in process - **all payments made except for \$20k warranty maintenance items**
- TAIT staff submitted art application with FAA, pending approval
- Art: Plan is to have agreement with City, TASM, and TAIT to locate art at TASM if approved by FAA - approvals expected March 2021 **PENDING**

EXHIBIT "F"



CITY OF TULSA Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: City of Tulsa

Contracting Party Representative: Mary Kell (Gary Schellhorn, COT)

Project Name and No: McCullough Site Improvements, Project No. 170125
(25th and Garnett area; 11.5 acres)

Project Funding:

Vision Tulsa Funding No. 170125.Buildings.4003-40033122-541104

Total Funding: \$3,600,000.00

Available Funding: \$540,000.00 Funded FY20

Total Expenditures:

 Contracted: \$540,000 (design)

 Spent to date: \$419,015.81

Status of any additional funding sources necessary for completion

- **Parks Department soliciting philanthropic funding**

Project Updates:

Status of Design and Construction

- Design Consultant: LandPlan Design Consultants, Design Fees: \$540,000.00
- 25% Design documents received 05.11.2020, 65% design documents received 08.31.2020
- 95% design documents received 1.20.2021
- **100% documents received 03.10.2021**
- Design Phases scheduled for February 2020 to May 2021
- Advertising for bids is scheduled to occur in May 2021 with bids opening June 2021
- Construction is scheduled to occur from September 2021 through June 2022
- Project is expected to be completed in June 2022

EXHIBIT "F"



CITY OF TULSA Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: City of Tulsa

Contracting Party Representative: Mary Kell (Gary Schellhorn, COT)

Project Name and No: Mohawk Sports Complex, Project No. 170130

Project Funding:

Vision Tulsa Funding No. 170130.ArchEngr.4001-400141110541101

Total Funding: \$3,500,000.00

Available Funding: \$3,500,000.00 Funded

Total Expenditures:

 Contracted: \$3,761,208 (\$320,076 + \$3,440,444)

 Spent to date: \$4,053,527.30 (\$289,204.74 + \$3,764,322.56)

Status of any additional funding sources necessary for completion

- No additional funds are expected to be needed

Project Updates:

Status of Design and Construction

- Design Consultant: Benham Design LLC, Design Fees: \$320,764.00
- Notice to proceed with construction 01.23.19
- Contractor is Daris Contractors, LLC - \$3,440,444.00
- Construction is 100% complete
- Project is operational
- Warranty items ongoing
- **Copper thefts at lights and sprinkler system and fire lines froze and broke, not a contractor issue.**

EXHIBIT "F"



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: City of Tulsa

Contracting Party Representative: Mary Kell (Glen Sams, COT)

Project Name and No: GOPLAN - PRIORITY IDENTIFIED IN THE BICYCLE/PEDESTRIAN MASTERPLAN - Project No. 170135

Project Funding:

Vision Tulsa Funding No. 170135.streets.4004.40043122-541106

Total Funding: \$3,125,000.00

Available Funding: \$3,125,000.00

Total Expenditures _____

 Contracted: \$3,125,000.00

 Spent to date: \$2,027,500.00

Status of any additional funding sources necessary for completion

No additional funds are expected to be needed

Project Updates:

Status of Design and Construction

(Additional detail for Group locations on following page)

IOT (Improve Our Tulsa) funds used first

Group 1A - Construction completed 12.31.2019 (IOT \$312k)

Group 1B - Construction completed 07.31.2020 (IOT \$1.4m)

Group 2 - Bids opened 03.06.2020. Construction 99% (IOT \$200k / Vision \$2.1m) **no change**

Group 3 - Bids opened 04.07.2020. Construction 90% (IOT 525k / Vision \$970k) **no change**

Removed Houston and SW Blvd from the project. To be completed as temperature allows

Group 4 - On hold to repair Osage Trail bridge over Flat Rock Creek

Striping 2021 Schedule

Striping progress and updates 03.16.2021

- **Group 1A:** Elgin, 10th, North Boulder. Project completed 12.31.19
- **Group 1B:** 11th (Elgin to Lewis), Boulder (10th to Riverside), 3rd street (Madison to Harvard), W Edison (Cheyenne to 33rd W Ave). Project completed 07.31.2020
- **Group 2:** 11th (Lewis to 129th), Pine (Gilcrease Museum Rd to Memorial), N Main (Haskell to Pine). Final plans (premylar) to be submitted on Dec 13, 2019. Grade Line is contractor. Work is underway. Work is approximately 99% complete. The contractor is working on the final punch list. **No change**
- **Group 3:** 6th St. (Boulder to South Delaware Ave.), Southwest Blvd (W. 48th Street to Riverside Dr to Heavy Traffic Way to Guthrie to Archer.), Houston (Riverside Drive to Heavy Trafficway), Charles Page Blvd (65th W Ave to Houston Ave).
 - Becco is contractor (\$1,487,000).
 - Construction started asphalt work on Sixth Street on 09.07.20.
 - The contractor is currently finishing striping on Chas Page Blvd and 6th Street.
 - Overruns on the asphalt and concrete apron work due to very rough road surface along 6th street, in this Group, and Pine Street in Group 2.
 - To offset this, the striping on SW Blvd. and Houston from the Group 3 contract is being removed from contract.
 - Work is 90% complete on 6th street and Charles Page Blvd. To be completed as temperatures allow. **No change**
- Group 4:** S Boston Ave (18TH St to 3rd St.), Peoria Ave (Pine St to Admiral Blvd), Greenwood (3rd to Archer), Delaware Ave (E 11th St to E 15th St),
 - Cost estimates exceed Goplan funding to do Group 4
 - Group 4 striping on hold for the time being and switching IOT funds to the repair of the Osage Trail bridge over Flat Rock Creek.

IOT and IOT-2 funding remaining for design of additional Groups.

EXHIBIT "F"



CITY OF TULSA

Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: City of Tulsa

Contracting Party Representative: Mary Kell (Marsha Hinds, COT)

Project Name and No: Route 66 Village Train Depot, Project 170140
3770 SW Blvd

Project Funding:

Vision Tulsa Funding No. 170140.ArchEngr.4001-40013122-541101

Total Funding: \$3,000,000.00

Available Funding: \$3,000,000.00 Funded

Total Expenditures:

 Contracted: \$2,928,283.31

 Spent to date: \$1,529,478.33

Status of any additional funding sources necessary for completion

- No additional funds are expected to be needed

Project Updates:

Status of Design and Construction

- Design Consultant: Keith D. Robertson Architect
- Design Fees: \$301,136.00
- Construction: June 2020 through June 2021
- Contractor is VOY Construction, notice to proceed 06.24.2020 (\$2,627,147.31)
- Framing complete, roof complete, MEP top out complete, insulation complete, drywall ongoing
- Construction 46% complete
- **Curb & Gutter 90% complete, Wall dry wall hung, windows , doors and millwork underway**

EXHIBIT "F"



CITY OF TULSA Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: City of Tulsa

Contracting Party Representative: Mary Kell (Jack Blair, Mayor's Office)

Project Name and No: Tulsa Arts Commission, Project No. 170145

Project Funding:

Vision Tulsa Funding No. 170145.ArchEngr.40004322-541101

Total Funding: \$2,250,000.00

Available Funding: \$600,000.00

Total Expenditures:

 Contracted: \$299,998.00

 Spent to date: \$0.00

Status of any additional funding sources necessary for completion

- No additional funds are expected to be needed

Project Updates:

Status of Design and Construction

- Ordinance changes approved by Council 02.05.2020.
- Recommendation for \$300K to be used for COVID-19 artist relief grants approved
- 17 small organizations and 12 large recipient organizations received grants
- 29 agreements signed by Mayor on 09.02.2020
- 2nd round of grants equaling \$300K RFP issued 10.13.2020, 34 applications received 11.30.2020. Grant review meeting held 01.08.2021.

**Awards recommended to Arts Commission at 02.15.2021 meeting.
Selections for second round of grantees on following page**

A breakdown of Vision Arts 2 organizations and funding amounts approved by the Mayor on 3/3/21:

The program will invest a total of \$187,000 in 22 organizations whose annual donations do not exceed \$400,000/year:

- \$141,000 to 16 performing arts organizations
 - \$10,000 to Chamber Music Tulsa, Inc.
 - \$10,000 to Choregus Productions, Inc.
 - \$8,000 to Clark Youth Theatre Incorporated
 - \$10,000 to Craft Productions
 - \$8,000 to Heller Theatre Company
 - \$10,000 to Horton Records, Ltd.
 - \$8,000 to Portico Dance Theatre
 - \$7,000 to Talk of Tulsa Show Chorus
 - \$7,000 to The Barthelmes Conservatory, Inc.
 - \$10,000 to Theatre North
 - \$10,000 to Theatre Tulsa, Inc.
 - \$10,000 to Town Hall of Tulsa Corporation
 - \$10,000 to Tulsa Area Youth Symphony
 - \$7,000 to Tulsa Latino Theater Company
 - \$8,000 to Tulsa Oratorio Chorus, Inc. a/k/a Tulsa Chorale
 - \$8,000 to Vocal Pride Foundation
- \$21,000 to three miscellaneous organizations:
 - \$9,000 to Circle Cinema Foundation Inc.
 - \$5,000 to Harmony Project Tulsa Inc.
 - \$7,000 to Tulsa Glassblowing Studio, Inc.
- \$15,000 to two cultural heritage museums or centers
 - \$7,000 to Casa de la Cultura
 - \$8,000 to Greenwood Cultural Center
- \$10,000 to Brady Craft, Inc. d/b/a 108 Contemporary, an art gallery

Additionally, the program will invest a total of \$113,000 in 11 larger organizations whose annual donations equal or exceed \$400,000/year:

- \$46,000 to four performing arts organizations
 - \$10,000 to Tulsa Ballet Theatre, Inc.
 - \$12,000 to Tulsa Opera, Inc.
 - \$12,000 to the Tulsa Performing Arts Center Trust
 - \$12,000 to Tulsa Symphony Orchestra
- \$26,000 to two art museums
 - \$13,000 to the Gilcrease Museum Management Trust
 - \$13,000 to Philbrook Museum of Art, Inc.
- \$13,000 to two miscellaneous organizations
 - \$5,000 to Fab Lab Tulsa
 - \$8,000 to Tulsa Girls Art School Project, Inc.
- \$12,000 to the Living Arts of Tulsa, an art gallery
- \$8,000 to the Tulsa Historical Society, a history museum or center
- \$8,000 to Tulsa Children's Museum, a science or children's museum

EXHIBIT "F"



CITY OF TULSA Sales Tax Overview Committee (STOC) Report

Date: 03.16.2021

From: City of Tulsa

Contracting Party Representative: Mary Kell (Mark Frie, PAC)

Project Name and No: Tulsa PAC Trust Master Plan, Project No. 170155

Project Funding:

Vision Tulsa Funding No. 170155.ArchEngr.40004322-541101

Total Funding: \$1,000,000.00

Available Funding: \$1,000,000.00 Funded

Total Expenditures:

 Contracted: \$998,713.00

 Spent to date: \$954,758.97

Status of any additional funding sources necessary for completion

- No additional funds are expected to be needed for Master Plan.
- Fundraising for building to run concurrent with Visioning and Master Plan process

Project Updates:

Status of Design and Construction

- Design Consultant: Beck Design
- Master Plan Feasibility phase 1 final draft received 01.31.19
- PAC Trust meeting 03.25.19 to discuss next steps
- PAC Trust requested that \$320 M be broken into more than 2 phases
- Revised phasing and costs presented at 11.18.19 PAC Trust meeting, total preliminary cost in 4 phases is \$77-\$78 Million
- Draft budget package received 01.28.2021 increased to \$104m - \$117 million
- Survey work received 02.16.2021, consultant **updated** budget based on impact of utilities that will need to be relocated as a result of expanding the building footprint
- **Final report submitted 03.03.2021 regarding fundraising, renderings and budget. In review by Administration.**

	B	C	D
1	VISION TULSA - PROJECT ACTIVITY / NEXT STEPS 03.04.2021		
2	PROJECT - Economic Development	COST	COMMENTS AND NEXT STEPS
3	Arkansas River Infrastructure & Amenities (City of Tulsa Share)		
4	Zink Lake and Related Amenities		- Design coordination team: CH2 (Jacobs), GKFF, MVVA, Holly Frontier, AEP/PSO, LandPlan, INCOG, City, River Parks and PMG.
5	Low-Water Dam with Recreational Gates & Flume	\$48,000,000.00	- Crossland Construction Company, \$38,934,499.49. - Construction time frame is 850 days, Start 10.19.20 - As of 01.31.2021 16.2% billed, 12.2% time - Major areas of work: west half dam demolition for gates, cofferdams and dewatering, power, coordination with Obermeyer for gates, and rebar installation. - Change order discussions related to delays in Pedestrian Bridge. Per dam contract, City is to keep cofferdams in-place until October. Contractor working ahead of projected pace. Claims for overhead costs etc. are being evaluated.
6	New Pedestrian Bridge	\$15,000,000.00	- Design Team: SBP, MVVA, GKFF, and River Parks - City identified funding sources for Tier 1: \$24.4 million (\$15 million Vision funding + \$9.4 Sales tax funding), Tier 2: \$3 million identified in savings in 2005 and 2008 funding packages. Transfers being prepared. Tier 3: Pending - GKFF and Mayor coordinating efforts to raise funds. - Bridge 404 Permit and 408 Permit pending anticipated EACH week . - USACE had employees ill and could not work on permits. USACE told hydrologist that it will be 2 weeks (from 03.03.2021) for USACE review and permit issuance. ONGOING
7	Mitigation, Bank Stabilization & Outfall Protection for Dam		- 404 permit issued, land banking for mitigation has been purchased.
8	South Tulsa/Jenks Lake and Related Amenities	\$64,214,000.00	- Vision Tulsa: ON HOLD - Other partners contribution \$32,862,000 for the project by 12.31.22. Both Jenks and City of Tulsa have the same reallocation date. - Funding includes long-term operating and maintenance endowment for both dams and related amenities. Zink Dam OM portion is \$18 million. NO CHANGE
9	Low-Water Dam and Pedestrian Bridge		- \$8.3 million for land acquisition includes land for trail to Cousins Park. NO CHANGE
10	East Bank Park, Boat Dock, and Abutment Improvements		
11	Vensel Creek Park and Boat Dock		
12	East Bank Trail Connection from Low-Water Dam to Vensel Creek		
13	Mitigation, Bank Stabilization & Outfall Protection		
14	Turkey Mountain Urban Wilderness	\$7,600,000	- Master Plan adopted by RPA - River Parks Foundation property (south of 61st Street and west of Turkey Mountain water tank). Closed on 12.28.2020. - New parking lot and entrance drive being planned for property north of 61st Street. Scope being defined. - City Legal reviewing CPA with River Parks for the remaining Vision Tulsa. +/- \$1.6m (existing balance plus \$1m FY22 appropriation). ONGOING
15	Levee District #12 Rehabilitation - Local Matching Funds	\$5,000,000	- Feasibility study approved by General Semonite 04.23.2020. PED phase is next step. - COE Emergency Management has granted \$10m to perform repairs for damages to and defects in levee facilities under the Flood Control and Coastal Emergency Act PL 84-99. - PL 84-99 work is in 2 general phases: 1. Levee issues, e.g. filters, sloughs, lining of pipe penetrations, etc. 2. Pump stations improvements, e.g. pumps and associated electrical systems, etc. - 02.04.2021 Meeting with District and PMG to discuss cost share. City has expressed interest in acquisition as a priority. Several homes had standing water during April/May 2019 event. Next meeting 03.04.2021 - 02.12.2021 Draft participation agreement for Preliminary Engineering Design sent City Legal for review. Reviewed 02.19.2021, document forwarded to District 03.03.2021. - Sales tax funds to be used first.
16	New Trail, East Bank-101st to Cousins Park (Design and Matching Funds), AKA "River Parks Trail 101st to 121st"	\$4,000,000	- LandPlan is design consultant. - Concept cost estimate \$10.2 million, with time value at 3% for 13 years - \$15.0m - Cost estimate with land is \$26m. - City received 2 projects, one on Riverside Drive (Vensel Creek to south of Creek Turnpike) reduced scope to design only to fit in more projects per INCOG and for City to secure rights-of-way. ONGOING
17	23rd & Jackson Redevelopment Site - Relocation Study, Design & Acquisition	\$1,000,000	- Cyntergy team is project consultant - Feasibility study of redevelopment for 23rd & Jackson to be done by others - Draft final report submitted February 2020. - Traffic Engineering is occupying the old County yard on North Harvard. - NO CHANGE
18	Gilcrease Museum Expansion	\$65,000,000	- Gallagher & Associates (G&A) - Owner's Representative (TU and City of Tulsa) - SmithGroup Architect / Flintco CM - Gilcrease Museum Mayor's Task Force held 02.11.2021. Next 03.11.2021. Discussion planning and move of collection. - Final walk through of storage area at Helmerich 03.05.2021. - Apache fitout costs are ongoing. - Apache radioactive survey complete, building is clean. - Moving insurance resolved with Crozier, HUB, and City Legal.
19	Cox Business Center	\$54,500,000	- Matrix is project architect, TVB (Tulsa Vision Builders) is Construction Manager - Substantial Completion received 06.30.2020. Building is operational. - Artist is Andrew "Andy" Tirado, design ongoing, installation in April 2021 . - Wi-Fi is pending with operational funds; Purchasing working on Wi-Fi (2 sole sources and 1 CSP). It is in queue to be advertised. Money rolled last year and cutoff is pending again for this year. Dropping other projects to move WIFI up.
20	Arena District Master Plan	\$500,000	- Resolve concrete cracking issues - repairs late spring 2021
21	Tulsa Fairgrounds	\$30,000,000	- Project completed January 2019
22	Airport Infrastructure		- Design consultant is GH2; Construction Manager (CM) is Crossland. - Projects complete - \$28.5 m - Improve Golden Driller Entrance - \$1.5 million - Golden Driller Plaza bids opened 01.21.2021. Special Meeting of board 02.10.2021 to approve, Notice to proceed 02.22.2021. To complete by 09.06.2021. - Demolition started 03.03.2021
23	[AA - All projects]	\$14,500,000	- Projects isolated below with descriptions (\$27,300,000 total) - Projects complete: \$2.4 m - Agreement with list of projects signed by Mayor 12.02.2020 NO CHANGE
24	[Air Force Plant 3 (AFP3) - Navistar]	\$2,200,000	- Cyntergy is engineer; SE Tulsa Construction is contractor for electrical upgrades - Construction is 75% complete Substantial completion scheduled 03.17.2021
25	[City Airport Facilities]	\$3,800,000	- Buildings 5, 6 and 116 repairs to roof, electrical and asbestos abatement - Building 6 roof replacement bids opened 01.29.2021. - Award to Lowry Construction pending. Contracts being prepared for execution.

	B	C	D
1	VISION TULSA - PROJECT ACTIVITY / NEXT STEPS 03.04.2021		
2	PROJECT - Economic Development	COST	COMMENTS AND NEXT STEPS
26	[Spirit Leasehold Properties]	\$5,000,000	- Spirit: \$5.0 million for various City owned facilities improvements - paving and resurfacing list of projects received from Spirit - Areas 1-4, 5, 6A, 6B, and 9 completed. - Area 7 and 8 Request from Spirit to substitute other work - Legal finalizing amendment to reflect change in employment projections and revise work scope: waterline valves, backflow preventers, hydrants and drive paving and striping (approx. \$1.6m) ONGOING
27	Grant Matching Opportunity	\$1,800,000	- MOED evaluating grant opportunities. NO UPDATE
28	Tulsa Zoo & Living Museum	\$25,000,000	- Selsler Schaefer is design consultant and Nabholz is CM; - 02.15.2021 Consultant is to submit revised 65% Design Documents. Review meeting scheduled for 03.11.2021 ONGOING
29	Langston University - Tulsa Healthcare Professions Complex Expansion	\$16,250,000	- OSU Long Range Planning Committee oversight, Architect - Beck, CM - Flintco - Schedule - construction May 2020 - November 2021 - Jobsite camera: http://ibeamsystems.com/camera/langstonuniversityproject - Overall construction - 41%
30	BMX National Headquarters	\$18,600,000	- Architect - Todd Architecture Group (prev. Fritz Baily), CM - Nabholz - BMX Vision (\$15M) UCAT Vision money (\$3.6M), EDIF funding (\$900K), Hardesty (\$1.5M), TPA (\$2M) - \$23M total funding - Jobsite camera registration: https://oxblue.com/invite/f492d4/bmx-headquarters ; Once registered, go to: app.oxblue.com - Overall construction 37% - Off-site storm RR permits: modified language per RR comments - ONGOING - Received right-of-entry for railroad area received. - PSO notice of line submitted for approval by City.
31	South Mingo Corridor	\$15,000,000	- Benham is design consultant for Mingo, 71st to 81st; Contractor is APAC Oklahoma - Construction 78% billed, 80% time ; Scheduled completion: March 2021 will be delayed due to weather. Pending Change Order for time extension. - 2nd Phase - Preliminary Design (Garver) 91st, Memorial to Mingo submitted December 2020 plans in review - 3rd Phase - Preliminary Design (Poe) Mingo, 81st to 91st - COMPLETE
32	Public Schools - Safety First Initiative	\$14,500,000	- Lee Engineering is design consultant. - 50+ schools on list and 5 priority levels of work to be performed. - Bid package 1, 2, and 3: Complete - TPS negotiating with MTTA to maintain bus shelters - Bid package 4: Working with ROW for sidewalk easements, construction to start Summer 2021 ONGOING
33	Capital Equipment (non-Public Safety)	\$12,000,000	- No action required
34	Citywide & Route 66 Beautification and Reinvestment		- Order of work: 1. Commercial Revitalization, 2. Route 66 3. Beautification - Total of \$11,000,000 split into projects below
35	Route 66	\$3,700,000	- Route 66 Commission and Tulsa Planning staff to provide oversight - Neon sign grant program - 26 in various stages of contracting, variance / permitting and construction. \$155k in matching grants awarded to date (\$320k total spent) - February Board Meeting was to discuss 4 new neon sign grant applications. Meeting did not meet quorum.
36	Citywide Commercial Revitalization	\$3,600,000	- Project 1: \$100K - Belo+Company (formerly Cubic) media strategy consultant - Report submitted end of December 2020 is under review by City staff - Selection of final concept then launch in 2Q of 2021 ONGOING - Project 2: \$1.1 million from Commercial Revitalization used to seed Business Resilience and Recovery Fund, reimbursement from CARES Act dollars is expected to fully fund the Commercial Revitalization Strategy. - City is to start receiving payments from TEDC February 2021. - Project 3: \$1.5 million BRT (Bus Rapid Transit) Revolving Loan Fund - TEDC is evaluating projects for program and providing low to zero interest loans NO UPDATE - Project 4: \$150K (3 years x \$50K) 4 Destination Districts - INCOG administering: Greenwood, Route 66, Kendall Whittier and International District (21st & Garnett area) NO UPDATE
37	Citywide Beautification	\$3,700,000	- Councilors Cue, Patrick and Lakin 12.01.2020 - Working group Meeting held 12.10.2020 to discuss next steps, follow up meeting held 01.25.2021 - Streets and Stormwater developing cost estimates for the meeting NO UPDATE
38	Peoria-Mohawk Business Park	\$10,000,000	- Bid Package 3 waterline, paving, storm and sidewalks underway. - Project 46% billed, 34% time from Field Engineering.
39	Public Schools - Partnership with Union, Jenks & Tulsa Public Schools in Teacher Retention, Recruitment, and Training Efforts	\$10,000,000	- Schools share \$1.4 million per year - Union and Jenks have agreements in place for 2020-2021 - Waiting for TPS agreement to be updated. PENDING
40	Community Health Connection East Clinic	\$9,975,000	- Project complete facility opened 04.13.2020
41	Air National Guard F35 (Mission Training Center) Simulator Training Center	\$9,400,000	- LWPB is design consultant, Crossland is CM - Building operational June 2020 - TAIT staff submitted art application with FAA, approvals expected in March 2021 PENDING - All payments made except for \$20k warranty maintenance items with Crossland.
42	Discovery Lab - Tulsa Children's Museum Permanent Site	\$8,000,000	- Property to be acquired and then leased to GKFF. - Additional public improvements are required to use full Vision budget. Estimated at \$230k. - GKFF reports that City Legal is near finalizing purchase and lease agreements.
43	Peoria Connection - North Peoria Avenue, 56th St. to Mohawk Blvd.	\$7,000,000	- HNTB is design consultant for BRT. BRT completed 03.31.2020 - BRT funding at \$4.8M. - Remaining balance to enhancements along corridor. - No activity other than BRT NO UPDATE
44	TCC Career Placement	\$5,320,000	- Project complete August 2019
45	University Center at Tulsa Authority/OSU-Tulsa		- Brown Ordinance; project deleted. Money (\$3,600,000.00) reallocated to BMX, 05.08.19
46	McCullough Park	\$3,600,000	- Consultant is LandPlan. - 100% documents due 03.10.2021 - Parks Department soliciting philanthropic funding ONGOING
47	Mohawk Sports Complex	\$3,500,000	- Benham is design consultant, Daris is contractor - Project is operational. - Copper theft lights and sprinkler system and fire lines froze and broke - Not a contractor issue.
48	GO Plan - Priority Projects Identified in the Bicycle/Pedestrian Master Plan	\$3,125,000	- Group 1A - Completed December 2019 (IOT \$312k) - Group 1B - Completed 07.30.2020 (IOT \$1.4m) - Group 2 - Construction 99% (IOT \$200k / Vision \$2.1m) - Group 3 - Construction 90% (IOT \$526k / Vision \$970k) NO CHANGE
49	Route 66 Village Train Depot	\$3,000,000	- Keith Robertson is architect, VOY Construction is contractor - Construction 49% complete. Substantial completion scheduled for June 2021

	B	C	D
1	VISION TULSA - PROJECT ACTIVITY / NEXT STEPS 03.04.2021		
2	PROJECT - Economic Development	COST	COMMENTS AND NEXT STEPS
50	Tulsa Arts Commission	\$2,250,000	<ul style="list-style-type: none"> - 1st round \$300K for COVID-19 artist relief grants signed by Mayor 09.02.2020 - 17 small organization grants totaling \$85,000 - 12 large organization grants totaling \$214,998 - 2nd round of grants equaling \$300K RFP issued 10.13.2020, 34 applications received 11.30.2020. - Awards recommended at special meeting of Arts Commission. Forwarded to Mayor 02.15.2021 NO UPDATE
51	Tulsa Performing Arts Center Trust	\$1,000,000	<ul style="list-style-type: none"> - Beck team is designer/consultant. - Revised phasing with costs totaling \$78 m submitted March 2020, represents most critical and prioritized needs for facility updates - Draft budget package received 01.28.2021 increased up to \$104 m to \$117 m, impacts of underground utilities to be added pending potholing results - Beck stated that underground utilities and building footprint have no effect on budget. - New survey 02.16.2021 shows otherwise. Budget adjusted to reflect adjusting service lines (electrical, water, sewer, and storm). - Final report submitted 03.03.2021 regarding fundraising, renderings, and budget package. Report forwarded to Blair, Neely, and America. Mark Frie to schedule meeting for presentation and discussion.
52	TOTAL	\$510,634,000	

GATEWAY BRIDGE

Tulsa, OK

Owner
 River Parks Authority /
 Gateway Bridge, LLC
 7030 South Yale Avenue, Suite 600
 Tulsa, OK 74136
 Tel: 918.392.1612

DESIGN TEAM

LANDSCAPE ARCHITECT (TEAM LEAD)
 Michael Van Valkenburgh Associates, Inc.
 Tel: 718.243.2044

BRIDGE AND STRUCTURAL ENGINEER
 Schlaich Bergermann Partner

CIVIL ENGINEER
 Wallace Engineering


LIGHTING CONSULTANT
 Domingo Gonzalez Associates

SOILS CONSULTANT
 Olsson Associates

ELECTRICAL ENGINEERING
 Phillips + Gomez

SITE STRUCTURAL ENGINEERING
 Wallace Engineering

GEOTECHNICAL ENGINEERING
 Terracon Consultants, Inc.

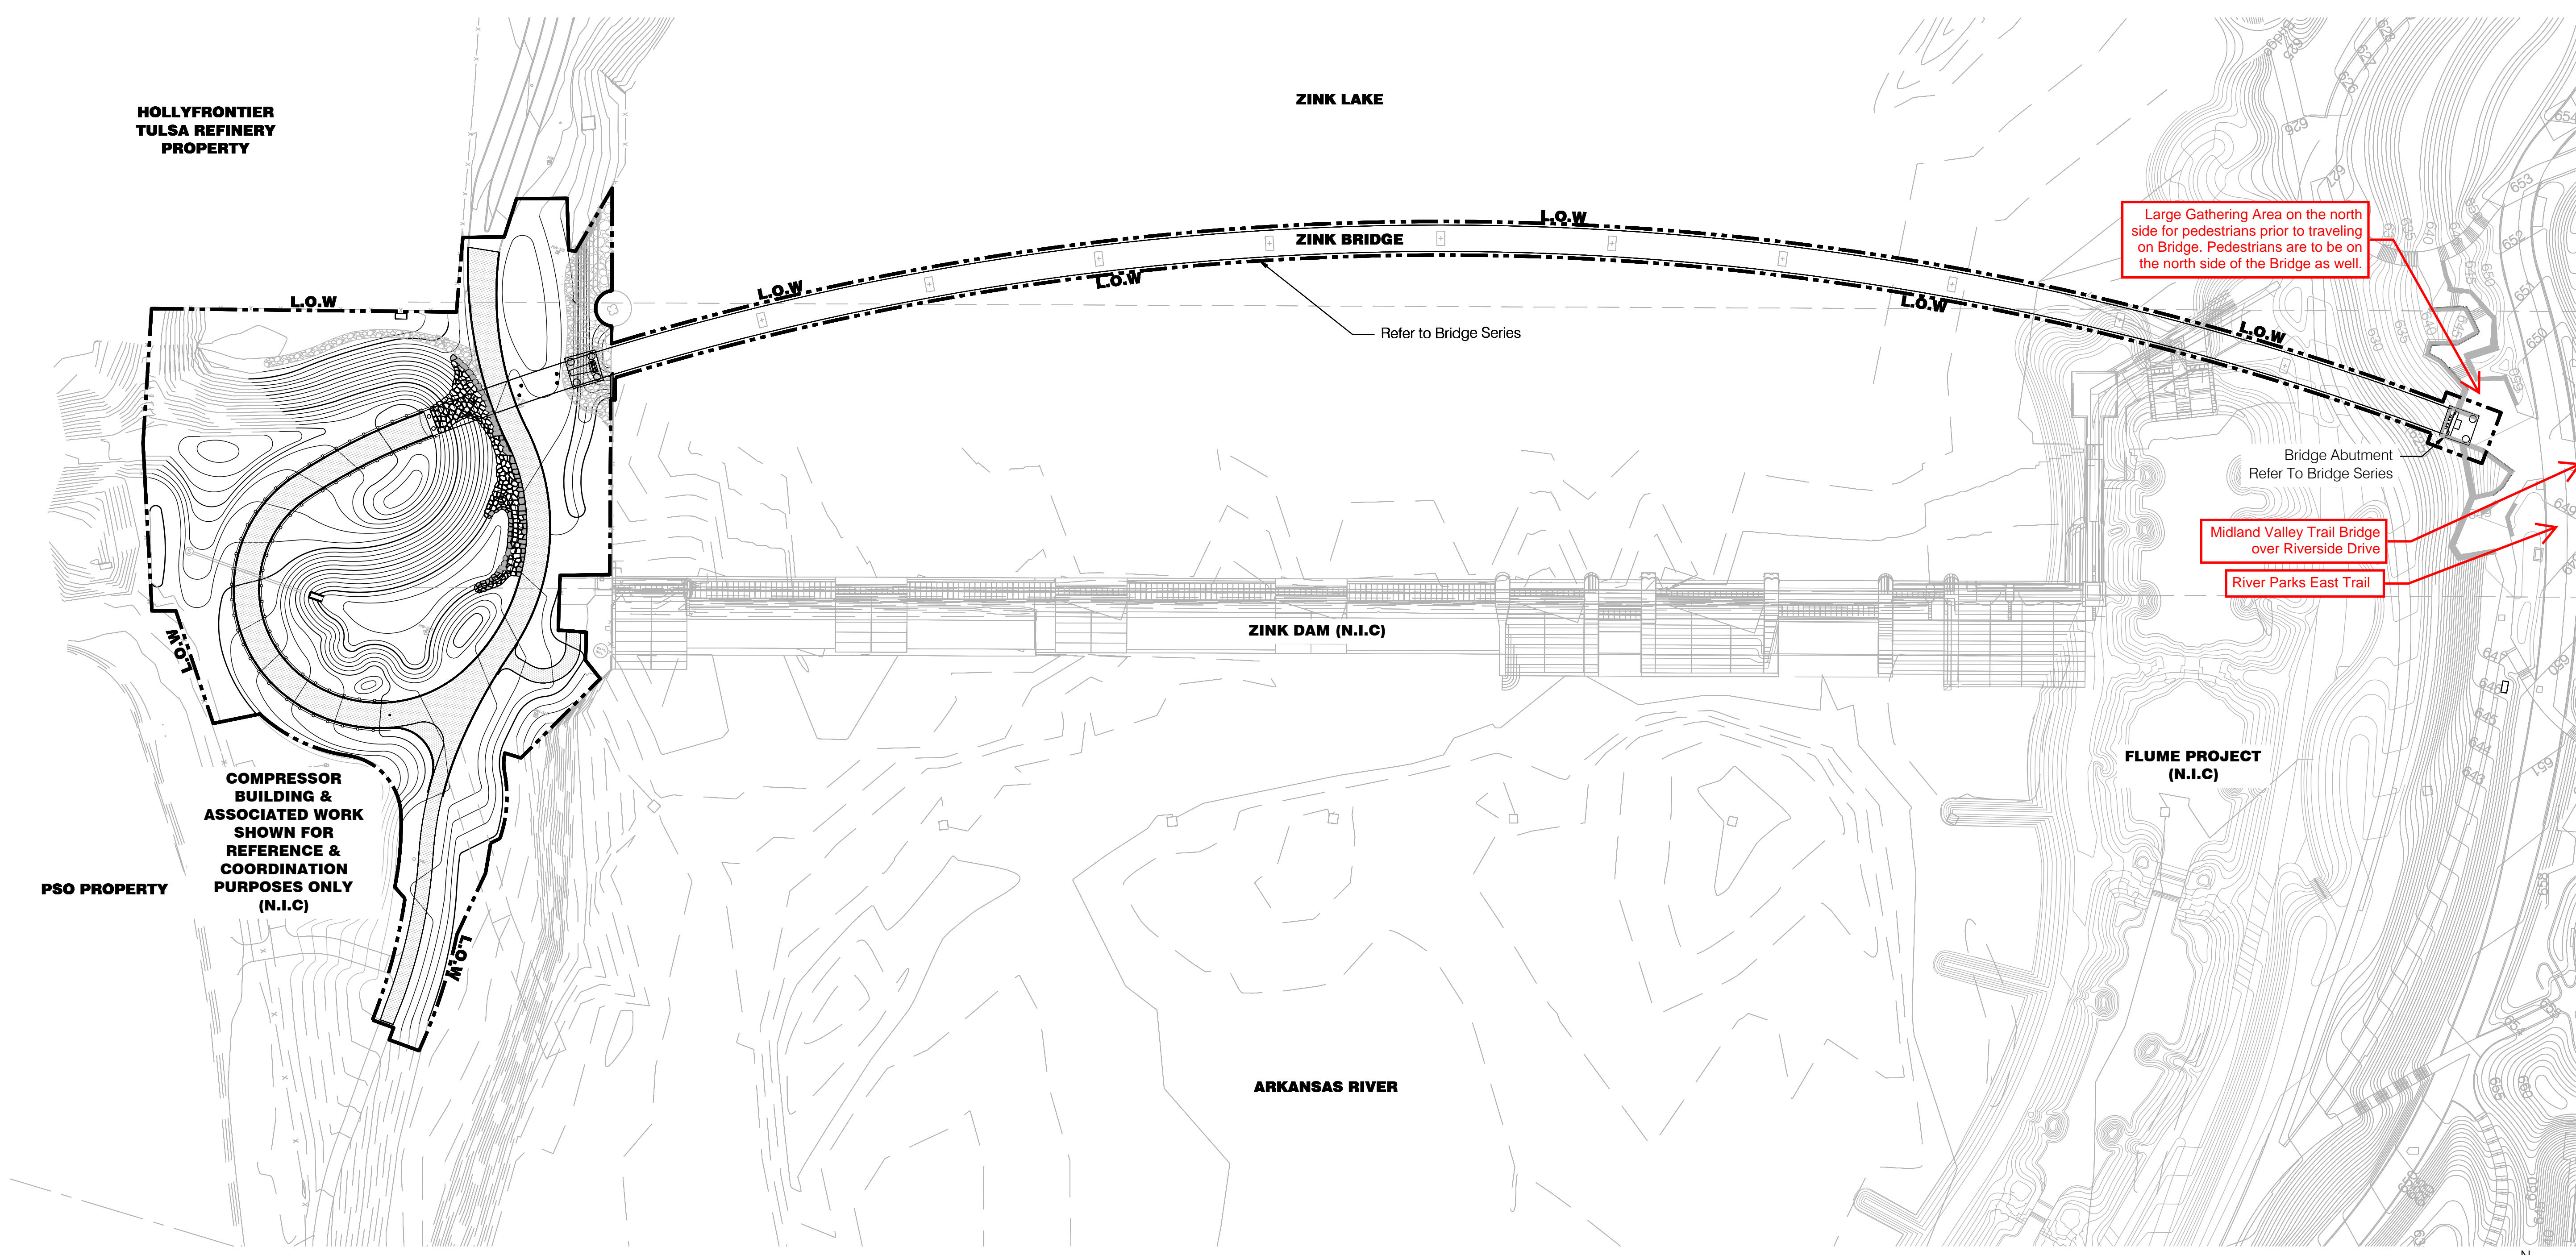


1 Site Plan
 Scale: 1"=60'-0"



06/18/2020

KEY PLAN

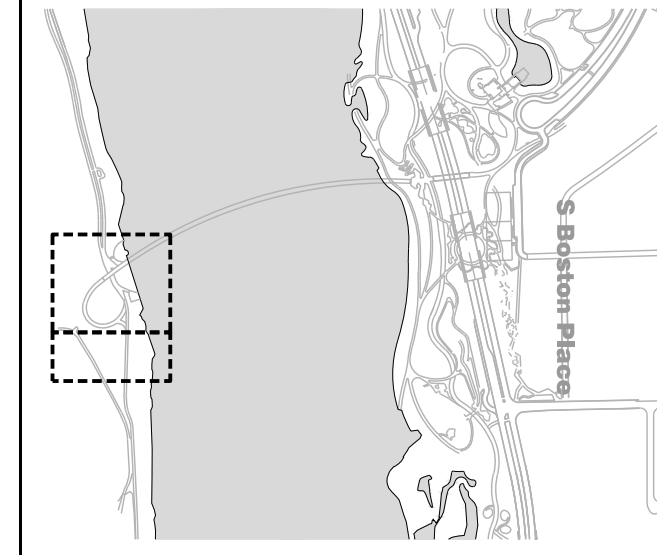

STATUS
 Bid Documents
 Issued for Permitting

REVISIONS

NO.	DATE	DESCRIPTION

DRAWING TITLE

Site Plan

JOB NUMBER 11003.06 **SHEET NO.** OF
DATE 06/18/2020
SCALE AS NOTED **G002**
DRAWN BY MVVA
CHECKED BY MVVA

S:\11003.06_Tulsa_Zink_Bridge\12_Cad_Drawings\Sheet\G002_Site_Plan.dwg - Friday, July 10, 2020 11:38:31 AM

GATEWAY BRIDGE

Tulsa, OK

Owner
 River Parks Authority /
 Gateway Bridge, LLC
 7030 South Yale Avenue, Suite 600
 Tulsa, OK 74136
 Tel: 918.392.1612

DESIGN TEAM

LANDSCAPE ARCHITECT (TEAM LEAD)
 Michael Van Valkenburgh Associates, Inc.
 Tel: 718.243.2044

BRIDGE AND STRUCTURAL ENGINEER
 Schlaich Bergermann Partner

CIVIL ENGINEER
 Wallace Engineering


LIGHTING CONSULTANT
 Domingo Gonzalez Associates

SOILS CONSULTANT
 Olsson Associates

ELECTRICAL ENGINEERING
 Phillips + Gomez


SITE STRUCTURAL ENGINEERING
 Wallace Engineering

GEOTECHNICAL ENGINEERING
 Terracon Consultants, Inc.

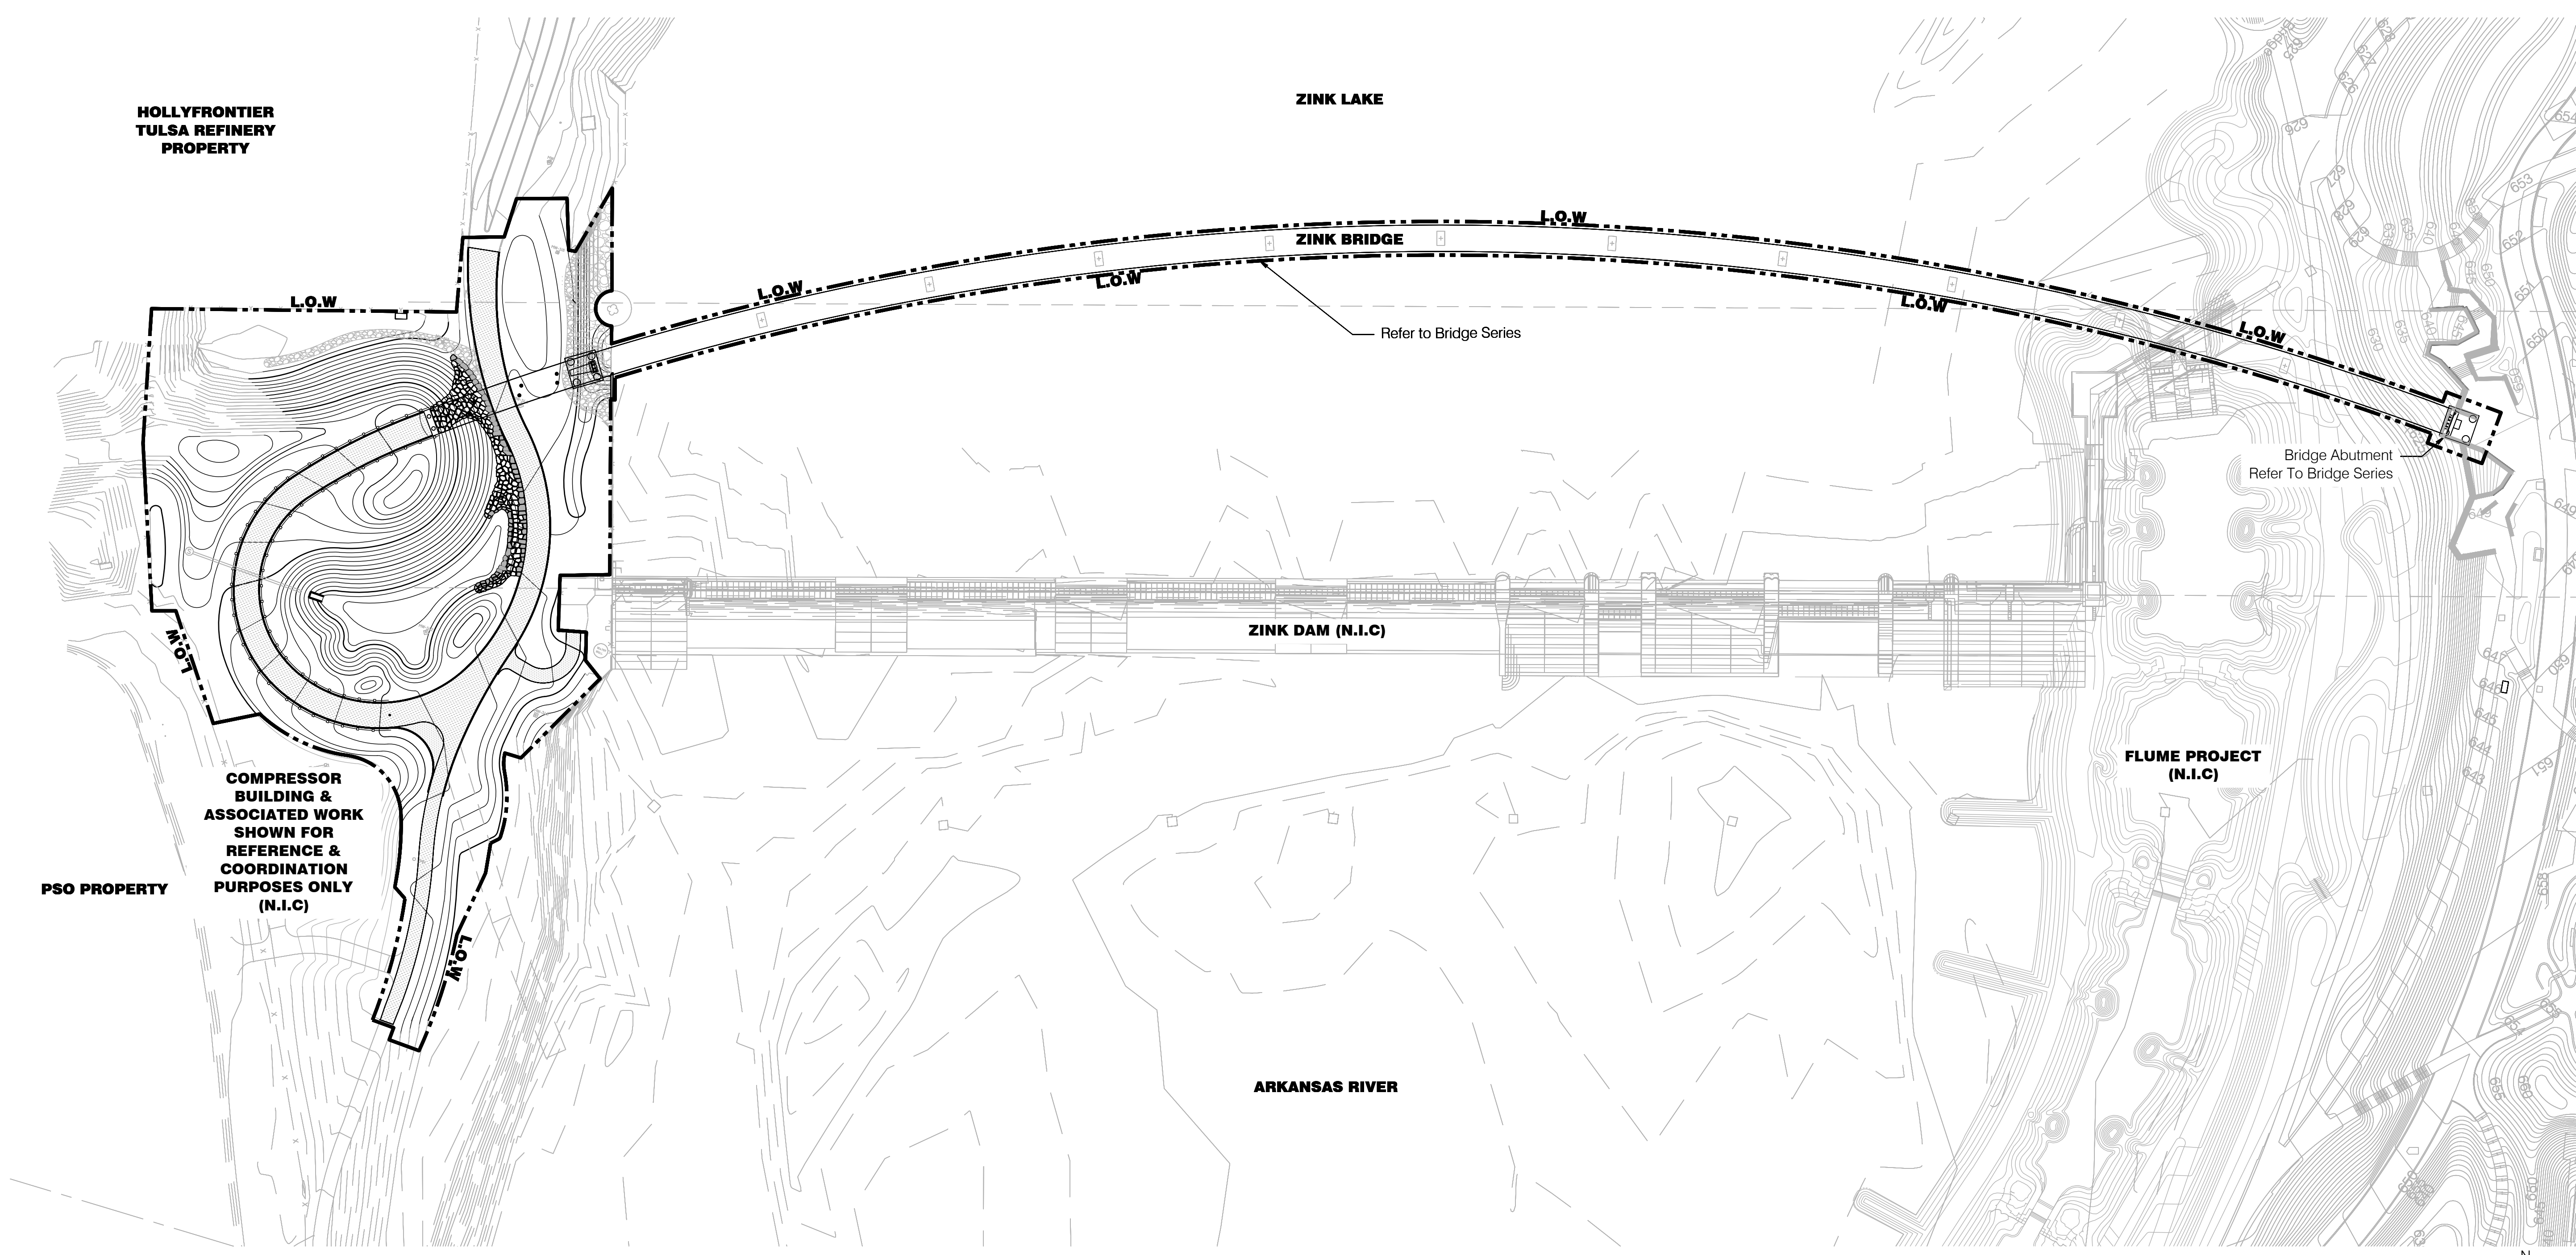

1 Site Plan
 Scale: 1"=60'-0"

Professional seal and signature of Michael Van Valkenburgh, dated 06/18/2020.

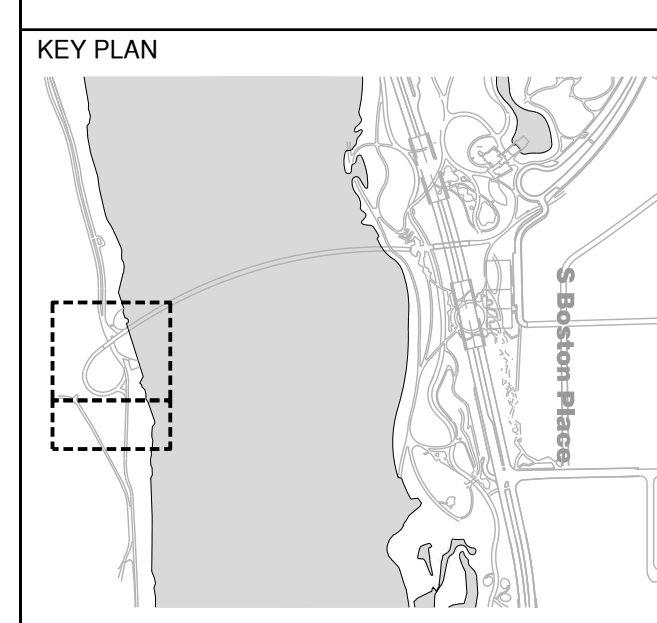

STATUS
 Bid Documents
 Issued for Permitting

REVISIONS

NO.	DATE	DESCRIPTION

DRAWING TITLE
 Site Plan

JOB NUMBER 11003.06 **SHEET NO.** OF
DATE 06/18/2020
SCALE AS NOTED **G002**
DRAWN BY MVVA
CHECKED BY MVVA

S:\11003.06_Tulsa_Zink_Bridge\12_Cad_Drawings\Sheet\G002_Site_Plan.dwg - Friday, July 10, 2020 11:38:31 AM

L 101/201/301/401/501/511

**HOLLYFRONTIER
TULSA REFINERY
PROPERTY**

ZINK LAKE

**ZINK
BRIDGE**
Refer To
Bridge Series

**ZINK DAM
(N.I.C.)**

**PSO
EQUIPMENT
(N.I.C.)**

L 102/202/302/402/502/512

**ARKANSAS
RIVER**

**COMPRESSOR BUILDING &
ASSOCIATED WORK SHOWN FOR
REFERENCE & COORDINATION
PURPOSES ONLY (N.I.C)**

**PSO
PROPERTY**

1 Key Plan
Scale: 1"=30'-0"

GATEWAY BRIDGE

Tulsa, OK

Owner
River Parks Authority /
Gateway Bridge, LLC
7030 South Yale Avenue, Suite 600
Tulsa, OK 74136
Tel: 918.392.1612

DESIGN TEAM

LANDSCAPE ARCHITECT (TEAM LEAD)
Michael Van Valkenburgh Associates, Inc.
Tel: 718.243.2044

BRIDGE AND STRUCTURAL ENGINEER
Schlauch Bergemann Partner

CIVIL ENGINEER
Wallace Engineering

LIGHTING CONSULTANT
Domingo Gonzalez Associates

SOILS CONSULTANT
Olsson Associates

ELECTRICAL ENGINEERING
Phillips + Gomez


SITE STRUCTURAL ENGINEERING
Wallace Engineering

GEOTECHNICAL ENGINEERING
Terracon Consultants, Inc.



06/18/2020

KEY PLAN



STATUS
Bid Documents
Issued for Permitting

REVISIONS

NO.	DATE	DESCRIPTION

DRAWING TITLE

Key Plan

JOB NUMBER	11003.06	SHEET NO.	OF
DATE	06/18/2020		
SCALE	AS NOTED	L001	
DRAWN BY	MVVA		
CHECKED BY	MVVA		

**HOLLYFRONTIER
TULSA REFINERY
PROPERTY**



GRADING LEGEND

See L 302 For Grading Notes.

- LOW** Limit of Work
- Bridge Deed and 200'-0" Right of Way
- OPDES Pipe Easement
- Bentonite Clay Barrier Wall
- (XX) Existing Contour
- XX Proposed Contour (Minor)
- XX Proposed Contour (Major)
- XX.X Proposed Contour (10')
- + (xx.xx) Existing Spot Elevation
- + xx.xx Proposed Spot Elevation
- MEX + Meet Existing Grade
- X.X% Direction and Percentage of Slope
- X:1 Slope Ratio (Horizontal to Vertical)
- + HP High Point
- + LP Low Point
- + TW Top of Wall
- + BW Bottom of Wall
- + TS Top of Stone
- + BS Bottom of Stone
- + TC Top of Curb
- EMH/SSMH Existing Manhole; Refer to Site Preparation Plans
- MW Existing Monitoring Well; Refer to Site Preparation Plans
- S Proposed Manhole and Pipe; Refer to Civil Series

**GATEWAY
BRIDGE**

Tulsa, OK

Owner
River Parks Authority /
Gateway Bridge, LLC
7030 South Yale Avenue, Suite 600
Tulsa, OK 74136
Tel: 918.392.1612

DESIGN TEAM
LANDSCAPE ARCHITECT (TEAM LEAD)
Michael Van Valkenburgh Associates, Inc.
Tel: 718.243.2044

BRIDGE AND STRUCTURAL ENGINEER
Schlach Bergermann Partner

CIVIL ENGINEER
Wallace Engineering

LIGHTING CONSULTANT
Domingo Gonzalez Associates

SOILS CONSULTANT
Olsson Associates



ELECTRICAL ENGINEERING
Phillips + Gomez

SITE STRUCTURAL ENGINEERING
Wallace Engineering

GEOTECHNICAL ENGINEERING
Terracon Consultants, Inc.



06/18/2020

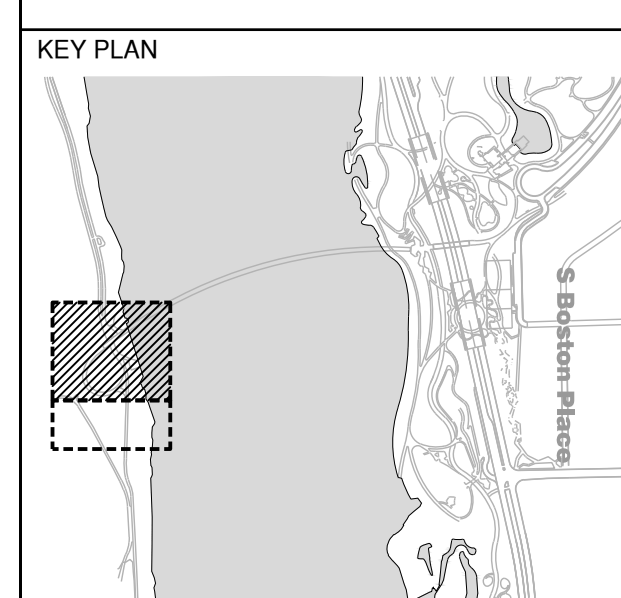

STATUS
Bid Documents
Issued for Permitting

REVISIONS

NO.	DATE	DESCRIPTION

DRAWING TITLE
Grading Plan-
North

JOB NUMBER 11003.06 **SHEET NO.** OF
DATE 06/18/2020
SCALE AS NOTED **L301**
DRAWN BY MVVA
CHECKED BY MVVA

S:\11003.06 Tulsa Zink Bridge\12 Civil Drawings\Sheet\301 Grading Plan-North.dwg - Friday, July 10, 2020 11:55:30 AM

MATCHLINE - SEE SHEET L 302

MATCHLINE - SEE SHEET L 302

MATCHLINE -SEE SHEET L 301

MATCHLINE -SEE SHEET L 301

PSO PROPERTY

COMPRESSOR BUILDING & ASSOCIATED WORK SHOWN FOR REFERENCE & COORDINATION PURPOSES ONLY (N.I.C)

ARKANSAS RIVER

GRADING LEGEND

- LOW** Limit of Work
- Bridge Deed and 200'-0" Right of Way
- OPDES Pipe Easement
- Bentonite Clay Barrier Wall
- (XX) — Existing Contour
- XX — Proposed Contour (Minor)
- XX — Proposed Contour (Major)
- XX.X — Proposed Contour (10')
- + (xx.xx) Existing Spot Elevation
- + xx.xx Proposed Spot Elevation
- MEX + Meet Existing Grade
- X.X% → Direction and Percentage of Slope
- X:1 → Slope Ratio (Horizontal to Vertical)
- + HP High Point
- + LP Low Point
- + TW Top of Wall
- + BW Bottom of Wall
- + TS Top of Stone
- + BS Bottom of Stone
- + TC Top of Curb
- EMH/SSMH Existing Manhole; Refer to Site Preparation Plans
- MW Existing Monitoring Well; Refer to Site Preparation Plans
- S Proposed Manhole and Pipe; Refer To Civil Series

GRADING NOTES

1. The Contractor shall layout and determine the elevations of all site elements and proposed utilities for approval by the Landscape Architect prior to the start of construction. The Contractor shall report any discrepancies in writing to the Construction Manager. The Contractor shall provide elevations simultaneously with layout.
2. The Contractor shall ensure that all erosion control measures are in place and functioning prior to the placement of fill material. Erosion control measures shall conform to the *Stormwater pollution prevention plan (SWPPP)* by Hydropower International Services Inter-National Consultancy, Inc.
3. The Contractor shall field verify grades and notify the Construction Manager of any discrepancies for resolution prior to starting construction operations. The Contractor shall not proceed under uncertainty and shall assume full responsibility of all costs for revisions due to failure to give such notifications.
4. The Contractor shall be responsible for positive surface drainage in all areas, unless otherwise noted. All newly graded ground surfaces shall be finished to uniform grades and sloped in such a manner as to drain properly and be free of depressions that cause areas of standing water. Where proposed grades meet existing, blend grades to provide a smooth transition between the new work and the existing work. Ponding at joints will not be accepted.
5. All grading shall be completed in a way to maintain positive drainage away from all structures. The Contractor shall report any conflicts with this requirement to the Construction Manager for resolution prior to final grading operations.
6. Grading within the drip lines of existing trees to remain and new trees shall be done by hand to avoid damage to tree roots. Refer to Specifications. Specifications to be submitted in a subsequent submission.
7. Refer to Specifications for compaction requirements under pavements and planted areas. Specifications to be submitted in a subsequent submission.
8. When rough grading of subgrade is complete, the Contractor must give Construction Manager and Landscape Architect notice for on-site review prior to and placement of planting soils and finish grading.
9. Fine grading: set sufficient grade stakes for review by Landscape Architects of finished grades. Stakes must be set at the bottom and top of slopes and as needed to review the proposed elevation. Grades shall be established which are accurate to 1/10 of a foot either way. Connect contours and spot elevations until an even slope is achieved. Refer to specifications.
10. During the review of rough grading and finish grade grading stakes, the Landscape Architect may make minor adjustments to rough grading without incurring additional cost to the project.
11. The Contractor shall adjust all utility elements or covers (including but not limited to: clean outs, manholes, catch basins, inlets, gate valves) to be flush with the final finish grade whether shown on the Drawings or not.

GATEWAY BRIDGE

Tulsa, OK

Owner
River Parks Authority / Gateway Bridge, LLC
7030 South Yale Avenue, Suite 600
Tulsa, OK 74136
Tel: 918.392.1612

DESIGN TEAM

LANDSCAPE ARCHITECT (TEAM LEAD)
Michael Van Valkenburgh Associates, Inc.
Tel: 718.243.2044

BRIDGE AND STRUCTURAL ENGINEER
Schlauch Bergemann Partner

CIVIL ENGINEER
Wallace Engineering

LIGHTING CONSULTANT
Domingo Gonzalez Associates

SOILS CONSULTANT
Olsson Associates

ELECTRICAL ENGINEERING
Phillips + Gomez



SITE STRUCTURAL ENGINEERING
Wallace Engineering

GEOTECHNICAL ENGINEERING
Terracon Consultants, Inc.



06/18/2020

KEY PLAN

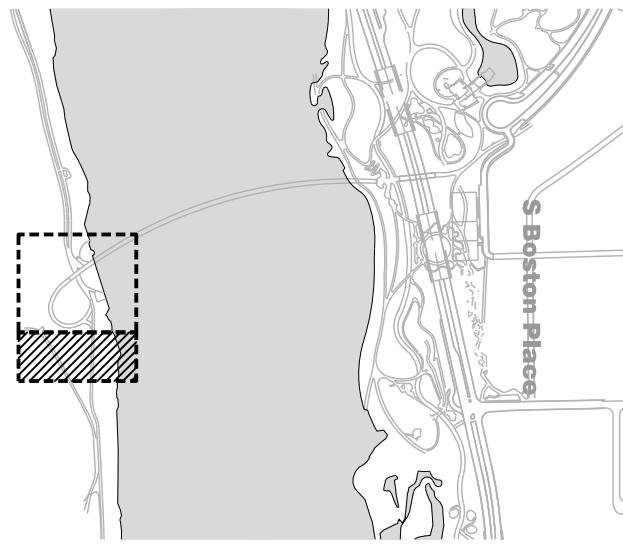

STATUS
Bid Documents Issued for Permitting

REVISIONS		
NO.	DATE	DESCRIPTION

DRAWING TITLE
Grading Plan-South

JOB NUMBER 11003.06 SHEET NO. OF
DATE 06/18/2020
SCALE AS NOTED **L302**
DRAWN BY MVVA
CHECKED BY MVVA

Public Safety and Economic Development

Attendees:

Paul McTighe
Kathy Sebert
Janae Bradford
Linda Jenkins
Ashley Webb
Karen O'Brien

**Report
To
Sales Tax Overview Committee
On
Public Safety, Urban Development
and Equipment**

TO: Public Safety, Urban Development and Equipment Subcommittee
Sales Tax Overview Committee

SUBMITTED BY: Marsha Hinds, Lead Engineer
Special Projects Design, Engineering Services Department

DATE: **March 11, 2021**

The status of projects managed by the Special Projects Design section of the Engineering Services Department as of **March 11, 2021**, is as follows:

2006 Sales Tax (6009)

Project No. SP 17-1

Budget: \$5,300,000.00

Project Description: Fire Station #33.

A New 4-Bay Fire Station located at E. 41st Street and S. 134th East Ave

Consultant: Kirkpatrick Architecture Studio

Contractor: Voy Construction

Status: Retaining wall pour complete. Grading should be completed this week. Ready to place first 2 manholes.

Project No. 067520 and 040430-7, Route 66 Xperience, TAC 1011

Budget \$5,000,000

Project Description: Interactive Route 66 Interpretive Center located at the northeast corner of Riverside Drive and Southwest Blvd.

Status: This project is now under the Mayor's office purview.

Project No. 065100, Contract 29, Misc. Electrical / Mechanical Services Citywide

Consultant: Cynergy

Status: Expired, **processing a new agreement.**

Project No. 065100, Contract 31, Misc. Structural Engineering Services Citywide

Consultant: Wallace Engineering – Structural Consultants, Inc.

Status: The consultant is providing services as requested by the City.
Used \$429.8K out of the \$456.5K agreement.

2014 Improve Our Tulsa (6014)

Project No. 145100, ADA Transition Plan – Building

Project Description: Improve accessibility for disabled citizens at various identified City facilities by improving to Americans with Disabilities Act (ADA) standards.

The 2016 Transition Plan Study included the following sites:

Municipal / Police Courts

BOK Center

Tulsa City Hall

23rd and Jackson Facilities

Tulsa Zoo, and Nature Center

Maxwell Convention Center = The Maxwell Convention Center items were taken care of in the Vision Tulsa Cox Business Center project.

Animal Shelter = The Animal Shelter items will be taken care of in the Improve Our Tulsa Animal Shelter expansion project.

Performing Arts Center = Performing Arts Center items were taken care of in the Improve Our Tulsa PAC renovations project.

Gilcrease Museum = The Gilcrease Museum items will no longer be valid with the new building.

Police- Gilcrease Division = The Police -Gilcrease Division some items will be addressed in the upcoming renovation project.

Consultant: TODD Architecture Group

Total Appropriations: \$1,275,000, Balance: \$825K

Status:

Received a request from the 911 Center of review of employee entry points.

Received a request from the Forensics Lab of review of employee entry points.

Consultant has investigated both requests and sites and has submitted recommendations.

Working with Facilities Maintenance and Security to install needed power assist door operators.

Project No. 145200, ADA Transition Plan – Parks

Project Description: Improve accessibility for disabled citizens at various identified City parks by improving to Americans with Disabilities Act (ADA) standards.

Consultant: Crafton Tull

Total Appropriations: \$1,140,000. **Balance \$367K**

Contractor: Builders Unlimited

Contract Amount: \$331,277.00

Status: Preconstruction mtg was held 1/27/21 for the Centennial, Hicks and Reed project.

The 2016 Transition plan also included the following sites:

Mohawk, Veterans, Lacy*, McClure*, Whiteside*, Hunter*

*Other capital improvement projects, i.e. Lacy Pool, McClure Pool, Whiteside Pool and Hunter playground have addressed some of the noted deficiencies at said locations.

Project No. 145300, Public Facilities – OTC City Hall

Project Description: Fire Alarm System upgrade, replace carpet on floors 3, 4, 5, 6, and 14
Contractor for Fire Alarm System Upgrade: Johnson Controls

Consultant for re-carpeting: Matrix

Contractor for re-carpeting: **Apparent low bidder L&M**

Total Appropriations: \$3,295,000. **Balance \$2.3M**

Status: Fire Alarm System upgrade complete

OTC City Hall 3rd, 4th and 6th floor Carpet is complete

Bids were open on 2/25/21 for the 14th and 15th floors carpet. Reviewing bids and preparing Award of Bid.

Project No. 145400, Public Facilities – Roofing

Project Description: Inspection, assessment, prioritization and repairs of roofing for various City facilities.

Consultants: Cyntergy, LLC & SGA Design Group, PC

Total Appropriations: \$3,000,000. **Balance \$375K**

Status:

Location	Project #	Status	Consultant
EMF Roof (Electronics Maintenance Facility)	SP 17-05	On hold consultant working on TMUA projects for us.	SGA
Tulsa Fire Department Field Ops (Old #9)(Which has been renamed FS#1)	SP 17-11	On hold consultant working on TMUA projects for us.	SGA

Consultant: Matrix

Project Description: Combined Project 145350; PAC Renovations, 145340; PAC Fire sprinklers, 145360; PAC Fan coil replacement and 145370; PAC HVAC motor replacement into one design agreement.

Contractor: CEI (Contract # 33312)

Contract Amount: \$1,861,694.12

Field Engineering and Legal are in contact with the Bonding Company.

Legal is the point of contact from this point forward on this project.

A walk-thru with the Bonding Company and various City personnel was held

December 6, 2019. City Legal is corresponding with the Bonding company.

The City has filed suit.

Project No. SP 21-1, PAC Renovations, Phase 2

Consultant: Beck Associates Architects

Project Description: Williams Theater stage floor replacement, renovations to office spaces.

Status: Negotiating design agreement; **awaiting fees and schedule.**

Project No. 145380, PAC Roof Replacement

Consultant: SGA

Project Description: Roof replacement

Contractor: Lowry (Contract # 135861)

Contract Amount: \$1,297,387.55

Status: Pre-construction meeting held 12/14/2020, NTP 4/2021

Project No. 145790, Thomas Gilcrease House Roof Replacement

Project Description: Replace the roof on the Thomas Gilcrease house.

Consultant: Selser Schaefer

Contractor: SE Tulsa Construction

Contract Amount: \$ 594,116.07

STATUS: Construction complete, working on close out documents.

• Funding

Improve Our Tulsa (145790)	\$ 175,000.00
Private Donations received	\$ 186,080.75
Residual funding from 145650 (savings from Grease Trap)	\$ 110,952.52
City match(to Gilcrease proposal)	\$ 62,500.00
Requested Council Transfer from 145660	\$ 90,446.67
6009 Funding 065320	\$ 29,237.02
Improve Our Tulsa (145780 Roof Replacement/Repair)	\$ 169,620.40
Improve Our Tulsa 145780	\$ 177,468.45
Design – Selser Schaefer	<\$ 29,237.02>
Design Amendment	<\$ 16,793.37>
Scoping Fees	<\$ 3,392.71>
Misc fees posted	<\$ 5,094.18>
Southwest Tulsa Construction	<\$ 594,116.07>
Supplement	<\$ 116,828.22>
Cost Placement Over-runs	<\$ 255,623.04>
Additional funding	\$ 19,776.80
	<hr/>
Balance / Contingency	\$ 0.00

Project No. 146110, Police Academy Renovation/Police Courts/Compstat Bldg

Project Description: Phase II: Police Courts and Compstat Bldg items to be worked on elevators, building envelope i.e. roof

Status: Facilities Maintenance is scheduling the following upgrades for the Police Courts and CompStat buildings:

Elevator work complete.

HVAC renovations which include but not limited to upgrading coils, valves and DD controls,

Plumbing upgrades-replacing galvanized pipe with pex,

Interior and Exterior lighting.

Project No. SP 16-10-1400XX, EMD Facilities Maintenance & Upgrades

Consultant: BKL, Inc.

Contractor: Voy

Phase I Construction Contact complete.

Project #140070. Available Balance: \$252,954.74

Project #140080. Available Balance: \$1,743,456.22

Status: EMD has requested concrete work to be completed at the Newblock location.

Concrete work complete.

Held a Teams meeting (8/20/2020) with EMD on additional work for various EMD sites.

EMD is preparing a priority listing for a future discussion meeting.

Held another Teams meeting (12-21-20) discussing project priorities.

Moving forward on concrete work requested at the Eastside Fuel Pump Island.

Moving forward on the West Yard Truck Wash repair.

Meeting to review status of requested work 2/10/2021.

Moving forward on Car Wash replacement at the Gilcrease Division.

**Tulsa Fire Department
Sales Tax/Bond Projects Report
3/9/2021**

Mike Mallory
Physical Resource Chief
Office 918-596-1230
Mobile 918-527-0262
mmallory@cityoftulsa.org

Ladder Order 2

Ladder 20 at 9827 East 59th Street

Ladder 24 at 3520 North Peoria

Both aerial ladders have been received and are in the process of being prepared for service. Stations are being prepared for receipt of the apparatus and station personnel are being trained on its operation.

Command Vehicles

District Chief Car 642 at Station 22, 7303 East 15th Street

Shift EMS Officer Car 835 Field Operations, Station 1, 1420 Charles Page

New specifications were created in response to the inability to acquire the Ford Police Responder pickup. The new specifications are based upon a Ford F-150 pickup but are open enough to allow other vehicle manufacturers to bid. The vehicles will be delivered in a near complete state with warning equipment, radios, and accessories installed. TFD will program radios and install lettering and door decals. A requisition was entered into the financial system on August 20, 2020. Specifications were approved by the Standards, Specifications and Awards (SSA) committee on February 25th and are currently out to bid.

Urban Search & Rescue Vehicles (Pickups)

USAR #2 and #3 @ 2819 North New Haven

Two USAR four door, four wheel drive, F-350 or equivalent, pickups were specified and approved by the Standards, Specifications and Awards (SSA) committee on February 25th and are currently out to bid. The pickups will replace the 2007 pickups that will be transferred to replace a 2008 pickup that has high miles and maintenance costs as well as replace a 1995 Ford flatbed four door, four wheel drive vehicle assigned to station 4.

Two additional Engines

Assignment to be determined

A requisition was entered into the Financial System for the purchase of two additional Engines on September 22, 2020. A Purchase order for the two Engines was issued on February 24th. The apparatus are expected to be delivered shortly after the first of the new calendar year of 2022.



INTEROFFICE CORRESPONDENCE

TO: Sales Tax Oversight Committee (STOC)
FROM: Deputy Chief Dennis L. Larsen
DATE: March 18, 2021
SUBJECT: Tulsa Police Fleet Activity



Fiscal Year 2020

105 – Total number of Police Utility Interceptors ordered on Purchase order 201133. All have been delivered. Of the delivered units, **92** have had their emergency equipment installed and have been issued to officers. The remaining **13** units are currently being completed at the Radio Shop.

5 – Total number of Ford Fusions ordered. **5** have been received and assigned to Investigations.

5 – Total number of Ford Escapes ordered all have been received and deployed.

1 - Ford F150 ordered and delivered and has been assigned to Property Room.

Status of Air Support Unit:

Police 1 (2013 Airbus AS350 B2) – Fully Operational

Police 2 (2019 Airbus H125) – Fully Operational

Fiscal Year 2021 Vehicles

93 - Total number of Police Utility Interceptors have been ordered. None have been received yet.

2 - Ford Transit Vans have been ordered. One is for a new Drone Unit, the other will be for a Bomb Tech. Both Units have been received and are in the process of being upfitted for service

3 - Ford F150's have been ordered, two will be for Special Investigation's undercover work, one will be a marked pickup for the TPD Academy.

3 - Harley Davidson Police Motorcycles have been requisitioned, the bid is still out.

1 - Ford Fusion has been ordered for Police Headquarters and has been delivered and deployed.

9 - Ford Escapes have been ordered for Police Detectives and all nine units have delivered and are in the process of being assigned to Detective Division.

Parks

Attendees:

Paul McTighe
Kathy Sebert
Janae Bradford
Linda Jenkins
Ashley Webb
Karen O'Brien

Parks STOC Report

3/11/21

Submitted To: Public Safety, Urban Development and Equipment Subcommittee Sales Tax Overview Committee

Submitted By: Gary Schellhorn, Resource and Facilities Coordinator, Special Projects Design, Engineering Services Dept.

1. TULSA PARKS – HILL SITE IMPROVEMENTS (017110-14, Contract 5)

- 210 East Latimer Place - District 1
- 2006 Sales Tax (6010-5451101-005011017110) and private funding
- Consultant: gh2 Architects
- Budget: \$68,000 (previously identified \$202,000 Private funding has not been provided.)
- Agreement between Private Partner (Reed Community Foundation) and Parks Department has been approved. Partner will make repairs to the interior of the building, City will make repairs to the exterior of the building which will include roofing repair, fascia repair, and sidewalk repairs.
- Funding for improvements: \$5,018.12 (6008-017110) + \$102,087.03 (6009-017110) + \$70,594.19 (6009-067120) = \$177,699.34.
- Parks Maintenance has replaced water line to building.
- Roofing repair - \$20,400: complete / repair of sidewalks and steps - \$20,040: complete.
- **Amount expended for original work = \$47,147.37 / Balance of funds = \$130,551.97**
- **Original work is complete. Design for roofing replacement has begun: design cost = \$29,640.00**

2. McCLURE PARK SLIDE / PLUNGE POOL (147500-1)

- 7440 E. 7th Street – District 3
- 2014 Sales Tax – part of McClure Pool Reconstruction Project (\$406,000)
- Design on the renovated plunge pool and flume slide is 10% complete. Mylars received 11/5/18.
- Advertising for bids began November 16, 2018 with bids opening December 14, 2018.
- 2 contractors provided bids of \$538,466 and \$794,999 which are 51% and 122% over the estimated cost.
- The bids were rejected.
- Redesign began November 12, 2019 and is complete. Mylars were submitted on April 16, 2020.
- Advertising for bids began April 24, 2020 with bids opening on June 5, 2020.
- One bid was received at bid opening in the amount of \$572,536 which is over the estimated amount of \$390,129.40. The bid was rejected.
- **Slide manufacturer provided actual costs for the slide and its installation. Evaluation of contractor's bid costs continues to determine where additional costs were added to bids. Bid item descriptions are being revised for clarity.**

3. ZEIGLER PARK WATER PLAYGROUND (147190a)

- 3903 West Fourth Street – District 1
- 2014 Sales Tax (6014-5451101-005011147190)
- Budget: \$500,000 (\$60k in FY2016 AND \$440k in FY2017)
- Consultant: Alaback Design Associates
- Design Fees: \$45,780.90
- Design is complete – Mylars were submitted September 26, 2019.
- Advertising for bids began October 18, 2019 with bids opening November 15, 2019.
- The bid has been awarded to Magnum Construction at a cost of \$470,986.00.
- Construction contract approved on January 15, 2020.
- Pre-construction conference was held January 28, 2020.
- Construction began February 24, 2020.
- Punch List Inspection was held July 9, 2020.
- Water Playground was opened on August 25, 2020. **Contractor is to make additional repairs to the project that was damaged by vandals during construction.**

Parks STOC Report

3/11/21

4. LANGENHEIM PARK PLAYGROUND AND SAFETY SURFACING (147520J)

- 4701 South Harvard Ave – District 9
- 2014 Sales Tax (6014-5455101-005011147520)
- Budget: \$275,000 (\$30k in FY2018 and \$245k in FY 2020)
- Consultant: LandPlan Consultants
- Design Fees: \$33,299.90 / **fees spent = \$23,661,90 / fees remaining balance = \$9,638.00**
- Design contract approved August 6, 2018.
- Design began on August 23, 2018 – Preliminary Design review meeting was held December 21, 2018.
- **A privately funded playground was installed in 2016.**
- **Park Director is coordinating with City Councilor to reallocate the funding to another park location within that district in need of a new playground.**
- **Funding balance remaining = \$251,338.10**

5. MINSHALL PARK PLAYGROUND AND SAFETY SURFACING (147520L)

- 7404 South Kingston Ave – District 8
- 2014 Sales Tax (6014-5451101-005011147520)
- Budget: \$275,000 (\$30k in FY2018 and \$245K in FY2020)
- Consultant: LandPlan Inc.
- Design Fees: \$33,299.90 / **fees spent = \$23,661,90 / fees remaining balance = \$9,638.00**
- Design began on August 23, 2018 – Preliminary Design review meeting was held December 21, 2018.
- **Neighborhood Association's desired improvements to the Park include trail repair, new benches along the trail, repairs to the gazebo floor slab, and dredging/cleanup of the pond. Stormwater Design is managing the design.**

6. PATRICK PARK PLAYGROUND AND SAFETY SURFACING (147520N)

- 5123 East Dawson Road – District 3
- 2014 Sales Tax (6014-5451101-005011147520)
- Budget: \$275,000 (\$30k in FY2018 and \$245K in FY2020)
- Consultant: LandPlan Inc.
- Design Fees: \$33,299.90
- Design began on August 23, 2018. Mylars were submitted December 4, 2019.
- Advertising for bids began December 27, 2019 and opened January 31, 2020.
- The bid has been awarded to Magnum Construction at a cost of \$479,999 for Patrick and Plaza playgrounds.
- Construction began on July 1, 2020.
- **Punch List Inspection was held on January 7, 2021.**
- **Completion of project is delayed from installing shade shelters that have been held up in the process due to COVID-19. Shelter scheduled to be delivered April 13, 2021.**

7. PLAZA PARK PLAYGROUND AND SAFETY SURFACING (147520P)

- 1404 South 145th East Ave – District 6
- 2014 Sales Tax (6014-5451101-005011147520)
- Budget: \$275,000 (\$30k in FY2018 and \$245K in FY2020)
- Consultant: LandPlan Inc.
- Design Fees: \$33,299.90
- Design began on August 23, 2018. Mylars were submitted December 4, 2019.
- Advertising for bids began December 27, 2019 and opened January 31, 2020.
- The bid has been awarded to Magnum Construction at a cost of \$479,999 for Patrick and Plaza playgrounds.
- Construction began on July 1, 2020.
- **Punch List Inspection was held on January 7, 2021.**
- **Completion of project is delayed from installing shade shelters that have been held up in the process due to COVID-19. Shelters scheduled to be delivered April 13, 2021.**

Parks STOC Report

3/11/21

- 8.. McCLURE PARK PLAYGROUND AND SAFETY SURFACING (147520M)
 - 7440 East 7th – District 3
 - 2014 Sales Tax (6014-5451101-005011147520)
 - Budget: \$275,000 (\$30k in FY2019 and \$245K in FY2021)
 - Consultant: LandPlan Inc.
 - Design Fees: \$33,299.90
 - Design began on August 23, 2018.
 - Design is complete – Mylars were submitted on July 25, 2002.
 - Advertising for bids began July 31, 2020 with bids opening September 11, 2020.
 - Contract has been awarded to Magnum Construction at a cost of \$427,747 for McClure and Penney
 - Pre-Construction Conference was held December 7, 2020.
 - **Construction began on December 28, 2020.**
 - **Construction Status = 73 calendar days / 150 calendar days = 48% time.**

9. PENNEY PARK PLAYGROUND AND SAFETY SURFACING (147520O)
 - 531 South 49th West Ave. – District 1
 - 2014 Sales Tax (6014-5451101-005011147520)
 - Budget: \$275,000 (\$30k in FY2019 and \$245K in FY2021)
 - Consultant: LandPlan Inc.
 - Design Fees: \$33,299.90
 - Design is complete – Mylars were submitted on July 25, 2002.
 - Advertising for bids began July 31, 2020 with bids opening September 11, 2020.
 - Contract has been awarded to Magnum Construction at a cost of \$427,747 for McClure and Penney
 - Pre-Construction Conference was held December 7, 2020.
 - **Construction began on December 28, 2020.**
 - **Construction Status = 73 calendar days / 150 calendar days = 48% time.**

10. REED PARK SWIMMING POOL RECONSTRUCTION (147120)
 - 4333 S. Yukon Ave. – District 2
 - 2014 Sales Tax (6014-5451101-005011147120)
 - Budget: \$2,410,000 (\$300k in FY2019 AND \$2,110K in FY2021)
 - Consultant: Alaback Design Associates
 - Design Fees: \$299,986.04
 - Design kick-off meeting held June 11, 2019.
 - Design is complete –Mylars submitted on August 17, 2020
 - Documents were submitted to State Health Department on Oct. 20, 2020, for approval.
 - Advertising for bids began December 11, 2020 and will open on January 29, 2021.
 - The bid is being awarded to Magnum Construction at a cost of \$2,650,000.00.
 - **Construction anticipated to begin March/April 2021 and be completed in March 2022.**

11. REED PARK WATER PLAYGROUND (147190)
 - 4333 S. Yukon Ave. – District 2
 - 2014 Sales Tax (6014-5451101-005011147190)
 - Budget: \$500,000 (\$60k in FY2019 AND \$440K in FY2021)
 - Consultant: Alaback Design Associates
 - Design Fees: \$57,347.87
 - Project is designed in conjunction with Reed Pool.
 - Design is complete – Mylars submitted on August 17, 2020
 - Advertising for bids with Reed Pool.
 - **Project construction in conjunction with Reed Pool.**

Parks STOC Report

3/11/21

12. CARL SMITH IMPROVEMENTS (147270)

- 17120 E. 21st Street – District 6
- 2014 Sales Tax
- Budget: \$185,000 (\$25,000 in FY2020 and \$160,000 in FY2021)
- Consultant: Method Architecture
- Design Fees: \$22,173.63
- Scope of work: HVAC improvements, flooring, painting, and roofing at Carl Smith Office, Concession, Restrooms, and Tournament Office.
- Design began October 30, 2019 – Mylars submitted on September 28, 2020.
- Project is designed in conjunction with Savage Improvements.
- Advertising for bids began October 23, 2020 with bids opening December 11, 2020.
- 3 Bids were received – the low bid was \$307,138 which was 20% over the project budget.
- The bids were rejected.
- **Value Engineering is being performed to reduce costs to re-bid this project.**

13. SAVAGE PARK IMPROVEMENTS (147230)

- 17800 E. 21st Street – District 6
- 2014 Sales Tax
- Budget: \$120,000 (\$15,000 in FY2019 and \$105,000 in FY2020)
- Consultant: Method Architecture
- Design Fees: \$22,173.63
- Scope of work: HVAC improvements, flooring, painting, and roofing at Savage Park Concession, Restrooms.
- Project is being designed in conjunction with Carl Smith Improvements.
- Design began October 30, 2019 – Mylars submitted on September 28, 2020.
- Advertising for bids began October 23, 2020 with bids opening December 11, 2020.
- 3 Bids were received – the low bid was \$307,138 which was 20% over the project budget.
- The bids were rejected.
- **Value Engineering is being performed to reduce costs to re-bid this project.**

14. WOODWARD PARK IMPROVEMENTS (147250)

- 2324 S. Rockford Ave. – District 4
- 2014 Sales Tax (147250.ArchEngr.)
- Budget: \$4,850,000 (\$870k in FY20 and \$3,980k in FY21)
- Consultant: LandPlan Consultants, Inc.
- Kick-off meeting was held June 10, 2020.
- **Programming / Master Planning continues and is scheduled to be complete in April 2021.**
- **Steering Committee meetings began on November 4, 2020. 3 community meetings are anticipated to begin in February.**
- **The design phase will begin in April 2021 after the completion of the Programming / Master Planning Phase is completed.**

15. BERRY PARK POOL RECONSTRUCTION (147300)

- 5002 N. Wheeling Ave. – District 1
- 2014 Sales Tax (147300.ArchEngr.)
- Budget: \$2,424,185
- Consultant: Alaback Design Associates
- **Design agreement scope of work continues being identified. City Councilor and Community outreach continues for the project.**

Parks STOC Report

3/11/21

16. TULSA ZOO CARNIVORES (147150)

- 5701 East 36th Street North. – District 1
- 2014 Sales Tax and Private Funding
- Budget: \$8,000,000 (2014) + \$17,000,000 (Private) = \$25,000,000
- Consultant: WDM (contract is being prepared with TZMI)
- **Construction Manager to be selected.**

17. GREENWOOD CULTURAL CENTER FACILITY REHABILITATIONS (147150)

- 322 North Greenwood Ave. – District 1
- 2020 Sales Tax
- Budget: \$5,340,000
- **Consultant Selection process is underway.**

18. TULSA PARKS – HILL SITE IMPROVEMENTS

- 210 East Latimer Place - District 1
- 2006 Sales Tax
- Balance of funds from Project 1 above = \$130,551.97
- Design for roofing replacement has begun: design cost = \$29,640.00

Sewer, Stormwater, and Transportation

Attendees:

Kathy Sebert
Mareo Johnson
Steve King
Paul McTighe

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Transportation Design Updates
 Design & Construction as of:
by [Signature] 3/9/21.

31/1/2021

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
FUND 401 - 2001 SALES TAX											
* 966120	Gilcrease Expressway Extension West - Tisdale Parkway to I-44 (Local Match) Tisdal to 41st St. West					95%	Dec-09	May-11	Plains/Tres/Unit	\$13,091	99%
TOTAL FUND 401 INCOMPLETE PROJECTS											

- + Remainder of Funding provided in 6010
- * Partial funding from other sources
- ~ Funded in Vision 2025 program
- ** Difference paid by Federal and State sources
- * Part of Becco's FY 04 street cuts contract
- † One contract for \$1,794,000
- †† Total contract with Becco is \$4,448,000 for stormwater project 993311 & street projects 6008-014180 & 6312-994526

FUNDS 402 - SALES TAX											
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
064101	41st Street South - Garnett Road to 129th East Avenue (Design)	Dec-15		BKL	\$465	90%	No construction funds currently scheduled				
064105	Peoria Avenue - 61st Street South to Riverside Parkway (Design)	Jan-14		BKL	\$800	70%	No construction funds currently scheduled				
064106	Garnett Road - 11th Street South to I-244 (Design)	Mar-15	Dec-16	C & K	\$500	100%	No construction funds currently scheduled				
064107	Mingo Road - 71st Street South to 81st Street South (Design)	Jun-14	Aug-16	Leidos	\$500	95%	Aug-19	Mar-21	APAC	\$7,431	72% 78%
064108	Pine Street - Memorial Drive to Mingo Road (Design)	May-14	Feb-20	Garver	\$449	80%	No construction funds currently scheduled				
064111	91st Street South - Memorial Drive to Mingo Road (Complete Design and Right-of-Way Acquisitions)	Design funded from other sources		Breisch		60%	Re-design funded through Vision Construction funded through IOT2				
966120	Gilcrease West Expressway from Tisdale Expressway to Edison			Tetra Tech		95%	Dec-09	May-11	Plains/Tres/Unit	\$13,091	99%
064093	City Match for Federal, State or County Projects			Various							
064004	Traffic Signal Synchronization			Various							
064003	Traffic Signalization, Lighting and Safety Improvements			Various							

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

31/1/2021

Budget Number	Project Description	DESIGN					CONSTRUCTION				
		Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
064002	Residential Streets - Major Rehabilitation										
i	Maintenance Zone 6140: Summerfield: E. 36th St. S. form S. 136th E. Ave. to S. 145th E. Ave. Phase II	May-09	Feb-10	COT	\$0	70%	Apr-21			\$500	
o	Sidewalks - Citywide			City							
q	Routine and Preventive Maintenance - Citywide										
r	Re-Inspection Pavement Management System (PMS) - Non-Arterial			Poe		100%					
064060	Bridge Replacement										
064062	Bridge Rehabilitation/Repair, Citywide										
914411	Trail System Improvements Matching Funds										
144104	Riverside Drive & Related Projects			HNTB		100%					
TOTAL FUND 402 INCOMPLETE PROJECTS											
FUND 403 - ADVANCE FUNDED SALES TAX											
014160	Arterial Street Rehab										
14K	81st - US 169 to Garnett										
	Traffic Signal Installation and Modification										
	Street Project Engineering and Inspection Intersections										
144104	Riverside Drive & Related Projects			HNTB		100%					
TOTAL FUND 403 INCOMPLETE PROJECTS											
FUND 404 - SPECIAL TEMPORARY SALES TAX FUND(2008)											
104010	Citywide - Arterial Sidewalk Repair and Construction										
104015	Citywide - Non-Arterial Rehabilitation and Reconstruction										
104016	Citywide - Non-Arterial Sidewalk Repair And Construction										
104017	Arterial Street Rehab										
i	Harvard Ave. - Admiral Blvd. to Pine St.	Jun-12	May-17	Meshek	\$390	95%	Mar-18	Dec-18	Becco	\$3,529	100%

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

31/1/2021

Budget Number	Project Description	DESIGN					CONSTRUCTION				
		Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
j	Lewis Ave. - 21st St. S. to 11th St. S.	Jun-12	Jul-14	C & K	\$353	95% 100%	Mar-18	Dec-18	Tri-Star	\$4,720	100%
l	Memorial Dr. - 21st St. S. to 11th St. S.	Aug-12	Dec-13	BKL	\$352	95%	Jul-19	Jul-21	Grade Line		65% 76%
o	Pine St. - Yale Ave. to Sheridan Rd.	Aug-12	Aug-17	Dewberry	\$467	95%	Aug-20	Jun-22	Becco		29% 38%
af	Pine St. - Yale Ave. Intersection	Jan-13	Aug-13	HRAOK	\$247	95%	Aug-20	Jun-22	Becco		23% 38%
104020	Citywide - Arterial Routine and Preventive Maintenance										
104021	Citywide - Non-Arterial Routine And Preventive Maintenance										
104022	Citywide - General Engineering / Testing / Inspection										
TOTAL FUND 404 INCOMPLETE PROJECTS											

FUND 405 - SALES TAX FUND (2014)

Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
144017	Arterial Street Rehab										
a	Charles Page Blvd. - 33rd W. Ave. to 25th W. Ave.	Jun-15	Sep-17	Tetra Tech	\$206	95%					
b	49th W. Ave. - Edison St. to Charles Page Blvd.	May-18	Apr-19	CEC	\$165	80%					
c	Utica Ave. - Pine St. to Admiral Blvd.	Nov-15	Apr-16	CEC	\$528	60% 80%					
d	Lewis Ave. - 36th St. N. to Apache St.	Jun-18	Dec-18	Cynergy	\$118	95%					
e	Southwest Blvd. - W. 23rd St. to W. 31st St.	Dec-16	Sep-17	Dewberry 100%	\$300	90%					
f	Southwest Blvd. - W. 31st St. to W. 40th St.	Dec-16	Sep-17	Dewberry 100%	\$315	90%					
g	Union Ave. - Southwest Blvd. to W. 41st St.	May-15	Sep-17	Dewberry	\$158	95%					
h	Union Ave. - W. 51st St. to W. 61st St	Jun-15	Aug-17	Garver	\$157	95%					
j	Pine St. - Harvard Ave. to Yale Ave.	May-18	Apr-19	Benham	\$289	90%	Jan-21	Jun-21	Ellsworth	\$1,598	9%
k	Admiral Pl. - Lewis Ave. to Harvard Ave.	Jan-18	Aug-18	BKL	\$253	90%					
l	Admiral Pl. - Harvard Ave. to Yale Ave.	Nov-16	Jul-17	Poe	\$325	95%					
m	Sheridan Rd. - Apache St. to Pine St.	Nov-15	Sep-17	AAB	\$156	95%	Feb-21	Jan-22	Ellsworth	\$4,177	1%
o	Mingo Rd. - 36th St. N. to Pine St.	Nov-16	Nov-17	McClelland	\$727	95%					
p	Mingo Rd. - Admiral Blvd. to 11th St.	Oct-18	Aug-09	Wallace	\$89	90%	Mar-19	Sep-21	Becco	\$8,435	85% 86%
q	11th St. - 89th E. Ave. to Mingo Rd.	Feb-15	Nov-15	CEC	\$162	100%	Apr-19	Oct-19	Ellsworth	\$1,631	100%
r	15th St. - Peoria Ave. to Lewis Ave.	May-15		Garver	\$248	95%	Sep-19	Nov-20	Crossland	\$3,094	100%
s	15th St. - Lewis Ave. to Harvard Ave.	Jan-17	Oct-17	Garver	\$302	90%					
t	Peoria Ave. - Admiral Blvd. to 11th St.	May-18	Feb-19	MARQUARDT	\$214	90%	Sep-20				
u	Peoria Ave. - 11th St. to 21st St.	Feb-16	Nov-16	MARQUARDT	\$252	90%					

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

31/1/2021

Budget Number	Project Description	DESIGN					CONSTRUCTION				
		Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
v	Utica Ave. - Admiral Blvd. to 11th St.	Nov-19	Aug-20	C&K	\$317	50% <i>65%</i>					
w	Utica Ave. - 11th St. to 15th St.	Dec-16	Jul-17	BKL	\$224	90%					
x	Harvard Ave. - 15th St. to 21st St.	Sep-19	Jul-20	Garver	\$245	80% <i>90%</i>	Oct-20				
y	Harvard Ave. - 21st St. to 31st St.	Apr-18	Apr-19	Poe	\$469	92%					
z	21st St. - Yale Ave. to Sheridan Rd.	May-18	Mar-19	CEC	\$259	90%					
aa	31st St. - Yale Ave. to Sheridan Rd.	Aug-19	May-20	HNTB	\$237	90%					
ac	41st St. - Sheridan Rd. to Memorial Dr.	Apr-18	Jan-19	CGA	\$262	90%					
ad	Memorial Dr. - 21st St. to 31st St.	Nov-15	Jun-16	BKL	\$289	98%					
ae	51st St. - Mingo Rd. to Garnett Rd.	Apr-18	Jun-19	Garver	\$234	90%	Jul-19	Jul-21	Grade Line	\$5,086	65%
af	71st St. - Memorial Dr. to Mingo Rd.			COT		85%					
ag	91st St. - Mingo Rd. to Hwy 169.			COT		100%	Nov-20		<i>Crossland</i>	<i>\$2,228</i>	
ah	Memorial Dr. - 81st St. to 91st St.	Sep-17	Mar-18	Marquardt	\$129	92%	May-20	Aug-20	Becco		100%
ai	Memorial Dr. - 91st St. to Creek Tpk.	Jun-15	Dec-15	Marquardt	\$58	95%	<i>Mar-21</i>		Crossland Heavy	\$2,987	<i>2%</i>
aj	Sheridan Rd. - 91st St. to 101st St.	Apr-18	Jun-19	HUB	\$84	95%	<i>Mar-21</i>		Crossland Heavy		<i>2%</i>
al	Harvard Ave. - 41st St. to 51st St.	Apr-18	Dec-18	PEC	\$236	65%					
am	36th St. N. - Mingo Rd. to Hwy 169	Jun-18	Apr-19	McClelland	\$301	90%					
an	Downtown Arterial Streets	May-15	Aug-15	Poe	\$923	70%					
	Phase 4 - Boulder/1ST to 10th		May-17	Poe		95%					
ao	Phase 5 - 6th Street / 7th Street		Jul-17	Poe		95%	Jan-19	Apr-20	Becco	\$4,415	100%
ao	Phase 6 - Detroit / 7th Street/ 8th Street		Aug-17	Poe		75%	Apr-20	Feb-21	Crossland	\$4,663	52% <i>62%</i>
ao	Phase 7 - Cheyenne		Jan-18	Poe		50%	<i>Apr-21</i>				
ap	Pine St. & MLK Jr. Blvd Intersection	May-08	Feb-19	CP&Y	\$117	98%					
aq	Pine St. & Peoria Ave. Intersection	Jun-17	Jun-18	Schemmer	\$135	90%					
ar	Pine St. & Lewis Ave. Intersection	Mar-17	Aug-17	Wallace	\$75	95%					
as	41st St. & Union Ave. Intersection	May-15	Sep-19	Dewberry	\$158	99%					
at	51st St. & Union Ave. Intersection			Garver		0%					
av	36th St. N. & Mingo Rd. Intersection	Nov-16	Nov-17	McClelland	\$727	95%					
aw	Admiral Blvd. & Lewis Ave. Intersection	Dec-17	Aug-18	BKL	\$250	90%	Aug-19	Sep-21	Becco		85% <i>86%</i>
ax	11th St. & Utica Ave. Intersection	Dec-16	Jul-17	BKL	\$224	90%					
ay	21st St. & Peoria Ave. Intersection						Oct-20				
az	21st St. & Memorial Dr. Intersection	Nov-15	Apr-16	MARQUARDT							
ba	51st St. & Mingo Rd. Intersection	Apr-18	Mar-19	BKL	\$289	98%	Jul-19	Jul-21	Gradeline		65% <i>76%</i>
bb	71st St. & Mingo Rd. Intersection	Apr-18	Mar-19	Garver	\$234	90%					
bd	71st St. & Sheridan Rd. Intersection	Mar-17	Nov-17	Cynergy	\$99	95%					
bd	71st St. & Memorial Dr. Intersection			COT		70%					
be	81st St. & Memorial Dr. Intersection	May-17	Dec-17	Benham		95%	Nov-20				
bf	61st St. & Yale Ave. Intersection	Dec-16	Aug-17	C&K	\$77	95%	Mar-21	<i>May-22</i>	Becco	\$13,875	
									Crossland	\$1,747	

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

31/1/2021

Budget Number	Project Description	DESIGN					CONSTRUCTION				
		Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
144020	Citywide Non-Arterial Routine and Preventive Maintenance										
144101	Widen Yale Avenue, 81st St. to 91st Street South	Jun-15	Jul-17	Benham	\$600	95%					
144102	Widen 81st Street South, Sheridan Road to Memorial Drive	Sep-16	May-18	Benham	\$950	95%	Mar-21		Becco	\$13,875	
144103	Widen Yale Avenue, 96th St. South to 101st St. South	Aug-16	Jul-17	CEC	\$200	95%	Mar-20	Dec-21	Becco	\$8,752	37%
144105	Widen 25th W. Ave., Edison to Apache (design)	Apr-21		Meshek Poe.							
144108	Widen Pine Street, Mingo to U.S. 169 (design)										
144120	Gilcrease Expressway Local Match										
144063	Bridges - Replacement and Rehabilitation Programs										
a	Bridge No. 275 - 10100 E. 36th St. N.	Jun-18	Dec-19	McClelland		80% 98%					
g	Bridge No. 250 - 11200 E. 11th St.	Jun-15	Dec-15	Cowen	\$39	95%			Becco	\$693	100%
h	Bridge No. 247 - 9200 E. 11th St.	Jun-15	Dec-15	Cowen	\$39	95%			Becco	\$693	100%
k	Bridge No. 401 - 3800 S. Memorial Dr.	Jun-15	Dec-15	Cowen	\$39	95%	Sep-19	Feb-20	Becco	\$693	100%
s	Bridge No. 333 - 1300 S. 177th E. Ave.	Jun-20	Oct-20	CP&Y		30%					
u	Bridge No. 209 - 3000 N. Mingo Rd.	Nov-16	Nov-17	McClelland	\$727	80% 90%					
x	Bridge No. 222 - 3200 S. Peoria Ave.	May-18	Jul-19	Garver	\$227	80%					
144094	ODOT Rehabilitation and Replacement Program										
144003	Citywide guardrail replacement										
144004	Citywide traffic signalization										
144005	Roadway, pedestrian, and decorative lighting replacement										
144006	Signing, pavement marking and delineation										
144007	Traffic calming										
144008	Traffic signal installation, modification, and safety improvements										
144009	Traffic signal pole replacement										
144010	Creek Turnpike Trail pedestrian bridge over Memorial Dr. (\$200,000 for study only)										
144011	GPS emergency vehicle preemption system (approx. 30 intersections)										

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

31/1/2021

Budget Number	Project Description	Estimated Start Date	DESIGN				CONSTRUCTION				
			Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
144109	Citywide ADA Transition Plan Implementation (Minimum for 30-Year Schedule - High and Medium Priority Needs)	Feb-16	Aug-18	BKL	\$639	90%					
	ADA Transition Plan - Package #1		Sep-17			95%	Mar-20	Nov-20	Daris	\$1,642	99%
	ADA Transition Plan - Package #2					90%					
	ADA Transition Plan - Package #3					70%					
144093	Citywide Matching Funds										
144018	Bicycle/Pedestrian Master Plan Implementation			Garver							
144019	IDL Entrance Rehabilitation (1st, 7th, and 8th Streets; signals at 1st and Greenwood)	see ao 144017		POE	\$1	60% <i>80%</i>					

TOTAL FUND 405 INCOMPLETE PROJECTS

FUNDS 4250-4255 2005 GENERAL OBLIGATION BOND ISSUES

054041	Citywide Routine/Preventive Maint										
	Arterial Streets Widening - Engineering and Partial ROW										
054050	51st - Garnett to BA Expr (Eng/Dsn)	Feb-08	Oct-08	C & K	\$300	65%	No construction funds currently scheduled.				
054051	61st - Peoria Int/Riverside Dr. to Peoria			DTA							
054052	81st - Memorial to Mingo; Sheridan to Memorial (Engr. & Design)	Jun-06	Apr-08	Benham	\$400	95%	Jun-09			See 064102	
054053	91st - Memorial to Mingo (Engr/Dsn)	Jan-08	Dec-08	Breisch	\$386	100%	ROW Acquisition				
054054	91st - Sheridan Inter (Final Design)	Mar-06	Apr-09	DDG	\$269	100%	Construction funded in 2006 S. T. See 064104				
054055	129th - 31st to 41st (Engr. & Design)	Feb-06	Feb-12	DTA	\$400	100%	Construction funded in 2006 S. T. See 064109				
054056	Delaware - 81st to 91st (Engr. & Dsn.)	Jan-08	Dec-08	BKL	\$456	100%	No construction funds currently scheduled.				
054057	Yale - 81st to 91st (Prelim Design)	Feb-06	Feb-07	Benham	\$300	100%	Advertised December 2020				
104023	Lewis Ave. - 11th to 21st	Jun-12		C&K	\$353	100%	Mar-18	Dec-18	TriStar	\$4,726	100%
054093	City Match for Federal/State projects.										
054002	Citywide Routine and Preventive Rehabilitation										
054003	Sidewalk Repair/Const (Citywide)										
054004	Traffic Calming Devices										
054001	Transportation Gen Eng/Insp Serv										

TOTAL FUNDS 4250-4255 INCOMPLETE PROJECTS

FUNDS 4260-4266 - 2008 STREETS GENERAL OBLIGATION BOND

Streets, Expressways, Sidewalks, Lighting, Traffic Calming

Arterial Street Rehabilitation and Citywide Projects:

104009	Citywide-Arterial Rehab & Reconstruction										
--------	--	--	--	--	--	--	--	--	--	--	--

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

31/1/2021

Budget Number	Project Description	DESIGN					CONSTRUCTION				
		Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
104010	Citywide-Arterial Sidewalk Repair & Construction										
104011	Citywide - Trails										
104012	Citywide - Railroad Crossings										
104013	Citywide - Local Match										
104014	Citywide-Gen.Engineering/Testing Inspection										
Non-Arterial Rehabilitaiton and Citywide Projects.											
104107	Maintenance Zone 1007	May-13	May-15	BKL	\$557	99%	Nov-18	Apr-21	Becco	\$7,500	98%
104944	Maintenance Zone 9044	Oct-19	Jan-20	Meshek	\$41	95%	Sep-20	May-21	Tri-Star	\$3,575	17% 47%
104015	Citywide Non-Arterial Rehab & Reconstruction										
104016	Citywide Non-Arterial Sidewalk Repair and Construction										
104000	Bond Issuance Costs										
104039	Harvard Ave. - Admiral Blvd. to Pine St.	Jun-12	May-13	Meshek	\$312	95%	Mar-18	May-19	Becco	\$3,529	100%
104041	Memorial Dr. - 21st St. S. to 11th St. S.	Aug-12	Dec-13	BKL	\$352	95%	Jul-19	Jul-21	Becco		85% 76%
104043	Pine St. - Yale Ave. to Sheridan Rd.	Aug-12	Mar-13	Dewberry	\$467	95%	Jul-20	Jun-22	Becco	\$4,587	23% 38%
144023	Citywide - Arterial Routine & Preventative Maintenance										
144022	Citywide-Art/Non-Art Routine & Preventative Maintenance										
104053	Pine St. - Yale Ave. Intersection	Jan-13	Aug-13	Dewberry	\$247	100%		2015			100%
104054	Citywide - General Engineering / Testing / Inspection										
TOTAL FUNDS 4260-4266 - 2008 Streets General Obligation Bond											
FUNDS 4270-4273 - 2014 STREETS GENERAL OBLIGATION BOND											
Streets, Expressways, Sidewalks, Traffic Calming											
Arterial Street Rehabilitation and Citywide Projects:											
144200	36th St. - N. MLK Jr. Blvd. to Peoria Ave.	Jun-15	Mar-20	PEC	\$232	75%	12/1/20				
144201	Apache St. - MLK Jr. Blvd. to Peoria Ave.	Nov-14	Aug-15	MESHEK	\$267	95%	Mar-19	Nov-19	Crossland	\$3,380	100%
144202	Apache St. - Peoria Ave. to Lewis Ave.	Aug-16	Mar-17	C&K	\$500	98%					
144203	W. 41st St. S. - 41st W. Ave. to S. 33rd W. Ave.	Sep-14	Aug-15	DEWBERRY	\$175	95%					
144204	S. 33rd W. Ave. - 41st St. to 51st St.	Sep-14	Aug-15	DEWBERRY	\$275	95%					
144205	Apache St. - Lewis Ave. to Harvard Ave.	Sep-14	Sep-15	GUY	\$210	80%	Feb-21				
144206	11th St. - Peoria Ave. to Utica Ave.	Nov-14	Nov-15	BKL	\$185	95%	Mar-20	Jan-21	Becco	\$2,343	54% 76%
144207	11th St. - Lewis Ave. to Harvard Ave.	Jun-16	Mar-17	BKL	\$205	85%					

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

31/1/2021

Budget Number	Project Description	DESIGN					CONSTRUCTION				
		Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
144208	11th St. - Sheridan Rd. to Memorial Dr.	Nov-14	Nov-15	BKL	\$180	95%					
144209	21st St. - Garnett Rd. to 129th E. Ave.	Dec-14	Jul-15	GARVER	\$235	95%	Apr-21				
144210	21st St. - 129TH East Ave. Intersection	Dec-14	Jul-15	GARVER	\$156	95%	Oct-20	Aug-21	Becco	\$4,079	6% 31%
144213	91st St. - Harvard Ave. to Yale Ave.		May-19	CEC	\$177	75%	Oct-20	Aug-21	Becco		6% 31%
144215	Peoria Ave. - 41st St. to 51st St.	Dec-16	Aug-17	MARQUARDT	\$340	90%					
144216	41st St. - Lewis Ave. to Harvard Ave.	Oct-14	Aug-15	CEC	\$275	95%	Apr-21		Crossland	\$5,653	
144217	Apache St. & Harvard Ave. Intersection	Sep-14	Sep-15	GUY	\$176	95%	Feb-21				
144218	41st St. & Lewis Ave. Intersection	Oct-14	Aug-15	CEC	\$210	95%	Feb-21				
144309	Citywide - Arterial Rehabilitation						Apr-21		Crossland		
144110	Citywide - Arterial Sidewalk Improvements										
144020	Citywide - Arterial Routine and Preventive Maintenance										
144093	Citywide Matching Funds										
144094	ODOT Rehabilitation and Replacement Program										
	Non-Arterial Rehabilitaiton and Citywide Projects.										
144111	Maintenance Zone 1001:	May-15	Feb-16	MAR / ARB	271 / 284	95%					
144106	Maintenance Zone 1006:	Sep-14	Jun-15	TETRA-TECH	\$356	95%			Gradeline	\$8,291	
144107	Maintenance Zone 1007:	Oct-14	Apr-15	Cyntergy	\$56	95%	Apr-19	Oct-19	Ellsworth	\$2,585	99% 100%
144168	Maintenance Zone 1068:	Sep-16	Sep-17	Nickle / Cowan	152./168.	95./95%	Nov-18	Nov-20	Becco		98%
144173	Maintenance Zone 1073:	Oct-14	Jul-15	COWAN	\$49	95%	Jul-17	Nov-17	PCSI	\$437	100%
144199	Maintenance Zone 1099:	Jun-15	Dec-15	CP&Y	\$259	95%			Crossland Heavy	\$2,343	
144153	Maintenance Zone 1153:	Sep-14	Jun-15	POE	\$334	95%					
144157	Maintenance Zone 1157 N:	Sep-14	Jun-15	BKL	\$302	95%					
144158	Maintenance Zone 1157 S:	Jun-15	Mar-16	SKW	\$210	95%	May-18	Feb-19	Ellsworth	\$3,195	100%
144225	Maintenance Zone 2125:	Nov-14	Aug-15	WALLACE	\$179	95%	Oct-19	May-20	Crossland	\$2,493	98%
144230	Maintenance Zone 2130:	Oct-14	Aug-15	MESHEK	\$270	95%	Apr-19	Jan-20	Becco	\$2,189	99%
144310	Maintenance Zone 3010:	May-15	Jan-16	MCCLELLAND	\$544	95%	Oct-20	Aug-21	Becco	\$3,485	6% 18%
144311	Maintenance Zone 3011:	Jun-16	Jun-17	POE	\$656	95%					
144317	Maintenance Zone 3017:	Oct-17	Jul-18	CGA	\$324	96%	Aug-20	Sep-21	Crossland Heavy	\$7,603	24% 45%
144320	Maintenance Zone 3020:	Aug-16	May-17	AAB	\$345	90%					
144413	Maintenance Zone 4013:	Sep-14	Apr-15	LEIDOS	\$512	95%	Jul-21				
144421	Maintenance Zone 4021:	Jul-16	Apr-17	CEC	\$343	96%					
144431	Maintenance Zone 4031:	May-15	Feb-16	GARVER	\$576	95%					

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

31/1/2021

Budget Number	Project Description	DESIGN				CONSTRUCTION					
		Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
144467	Maintenance Zone 4067 phase 1	Oct-14	Jun-15	GUY	\$344	95%	Jan-20	Aug-20	Crossland	\$3,127	99%
144467	Maintenance Zone 4067 phase 2										
144452	Maintenance Zone 4152:	Oct-17	Jul-18	HUB	\$373	97%					
144527	Maintenance Zone 5027:	Nov-14	May-15	CRAFTENTULL	\$115	95%	Sep-18	Jan-19	Paragon	\$1,144	100%
144533	Maintenance Zone 5033:	Oct-14	Jun-15	CGA	\$444	95%	Oct-18	Aug-19	Crossland	\$4,847	100%
144546	Maintenance Zone 5046:	Jun-16	Mar-17	MCCLELLAND	\$540	96%					
144547	Maintenance Zone 5047:	Aug-16	Jun-17	GARVER	\$584	90%	Jan-21				
144628	Maintenance Zone 6028:	Jan-18	Aug-19	MCCLELLAND	\$428	90%	Aug-21				
144635	Maintenance Zone 6035:	May-15	Apr-16	HUB	\$253	95%	Oct-19	Jul-19	Becco	\$2,768	100%
144642	Maintenance Zone 6142:	Oct-14	Jun-15	HOOD/COT	\$78	92% 95%	Jan-21		Ellsworth	\$1,313	
144645	Maintenance Zone 6145:	Oct-04	May-15	Cynergy	\$195	95%					
144740	Maintenance Zone 7040:	Jun-16	Apr-17	HUB	\$254	95%	Dec-20	Oct-21	Crossland Heavy	\$3,478	69%
144754	Maintenance Zone 7054:	Sep-17	Feb-19	POE	\$747	90%	Oct-21				
144857	Maintenance Zone 8057:	Apr-17	Jul-19	WALLACE	\$107	95%			Ellsworth	\$1,601	26% 30%
144863	Maintenance Zone 8063:	Oct-17	Sep-19	CraftonTull/pec	\$195	95%					
144944	Maintenance Zone 9044:	Oct-14	May-15		\$293	80%	Sep-20	Mag-21	Tri-Star	3,575	17% 47%
144945	Maintenance Zone 9045:	Oct-14	Jul-15	GARVER	\$200	95%	Jan-19	Nov-19	Crossland	\$3,557	100%
144949	Maintenance Zone 9049:	Sep-17	May-19	GARVER	\$770	85%					
144950	Maintenance Zone 9050:	Jul-16	Feb-17	CP&Y	\$255	95%					
144951	Maintenance Zone 9051:	Jul-16	Feb-17	SKW	\$130	95%	Jan-21				
144015	Citywide Non-Arterial Rehabilitation										
144021	Citywide Non-Arterial Routine and Preventive Maintenance										
144016	Citywide Non-Arterial Sidewalk Improvements										
144060	Bridge No. 189 - 4700 N. Iroquois Ave.	Nov-14	Jul-15	MEHLBURGER		90%					
144062	Bridge No. 323B - 12000 E. 21st	Dec-14		GARVER	\$10	95%					
TOTAL FUNDS 4270-4273 - 2014 Streets General Obligation Bond											
FUNDS 4281-4285 - 2020 STREETS GENERAL OBLIGATION BOND											
'Non-Arterial Street Rehabilitation Projects:											
2036N1007Z	Maintenance Zone 1007:			Cowan	\$81						
2036N1068Z	Maintenance Zone 1068:										
2036N1070Z	Maintenance Zone 1070:			CGA							
2036N1071Z	Maintenance Zone 1071:										
2036N1072Z	Maintenance Zone 1072:										
2036N1076Z	Maintenance Zone 1076:			McClelland	\$236	20% 30%					
2036N1078Z	Maintenance Zone 1078:	Oct-20	Jun-21	Olsson	\$253	30% 40%					

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

31/1/2021

Budget Number	Project Description	DESIGN					CONSTRUCTION				
		Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036N1097Z	Maintenance Zone 1097:										
2036N1098Z	Maintenance Zone 1098:										
2036N1153Z	Maintenance Zone 1153:										
2036N1155Z	Maintenance Zone 1155:										
2036N1157Z	Maintenance Zone 1157:										
2036N2056Z	Maintenance Zone 2056:										
2036N2065Z	Maintenance Zone 2065:	Jan-21	Sep-21	Garver	hold						
2036N2066Z	Maintenance Zone 2066:	Oct-20	Jul-21	Garver	\$218	10% 30%					
2036N2131Z	Maintenance Zone 2131:			C&K	\$101	20%					
2036N3004Z	Maintenance Zone 3004:										
2036N3005Z	Maintenance Zone 3005:										
2036N3008Z	Maintenance Zone 3008:										
2036N3010Z	Maintenance Zone 3010:										
2036N3011Z	Maintenance Zone 3011:										
2036N3017Z	Maintenance Zone 3017:										
2036N3075Z	Maintenance Zone 3075:										
2036N3080Z	Maintenance Zone 3080:										
2036N3081Z	Maintenance Zone 3081:										
2036N3082Z	Maintenance Zone 3082:			EST	\$58						
2036N4014Z	Maintenance Zone 4014:	Oct-20	May-21	Poe	\$136	20% 30%					
2036N4015Z	Maintenance Zone 4015:										
2036N4021Z	Maintenance Zone 4021:	Sep-20	Jul-21	CEC	\$256	20% 30%					
2036N4022Z	Maintenance Zone 4022:	Oct-20	Apr-21	BKL	\$322	30%					
2036N4023Z	Maintenance Zone 4023:										
2036N4029Z	Maintenance Zone 4029:										
2036N4030Z	Maintenance Zone 4030:	Dec-20	Jul-21	Marquandt	\$143	10%					
2036N4031Z	Maintenance Zone 4031:										
2036N4067Z	Maintenance Zone 4067:										
2036N4069Z	Maintenance Zone 4069:										
2036N5016Z	Maintenance Zone 5016:										
2036N5026Z	Maintenance Zone 5026:										
2036N5027Z	Maintenance Zone 5027:										
2036N5033Z	Maintenance Zone 5033:										
2036N5039Z	Maintenance Zone 5039:										
2036N5040Z	Maintenance Zone 5040:			TEP ✓							
2036N6035Z	Maintenance Zone 6035:			Benham	hold						
2036N6142Z	Maintenance Zone 6142:										

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

31/1/2021

Budget Number	Project Description	DESIGN					CONSTRUCTION				
		Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036N6144Z	Maintenance Zone 6144:										
2036N6148Z	Maintenance Zone 6148:										
2036N6149Z	Maintenance Zone 6149:										
2036N6150Z	Maintenance Zone 6150:										
2036N7048Z	Maintenance Zone 7048:	Nov-20	Oct-21	Benham	\$252	20%					
2036N7060Z	Maintenance Zone 7060:			HUB	\$73						
2036N7104Z	Maintenance Zone 7104:										
2036N7109Z	Maintenance Zone 7109:										
2036N7115Z	Maintenance Zone 7115:										
2036N8057Z	Maintenance Zone 8057:			Wallace	\$107						
2036N8102Z	Maintenance Zone 8102:	Oct-20		FNI	\$171	20%					
2036N8113Z	Maintenance Zone 8113:										
2036N8116Z	Maintenance Zone 8116:										
2036N9036Z	Maintenance Zone 9036:										
2036N9037Z	Maintenance Zone 9037:										
2036N9038Z	Maintenance Zone 9038:			CP&Y	\$183						
2036N9043Z	Maintenance Zone 9043:			PEC	\$71						
2036N9044Z	Maintenance Zone 9044:										
2036N9045Z	Maintenance Zone 9045:			POE	hold						
2036N9049Z	Maintenance Zone 9049:										
2036N9050Z	Maintenance Zone 9050:										
2036N9051Z	Maintenance Zone 9051:	Sep-20	Apr-21	Keithline	\$83	65%					
2036N9052Z	Maintenance Zone 9052:					80%					
Arterial Street Rehabilitation Projects:											
Arterial Street Projects:											
2036A0001Z	56th St N-MLK Blvd to 1500ft W of Peoria										
2036A0002Z	46th St N - Peoria Ave to Lewis Ave										
2036A0003Z	46th St N - Elwood Ave to MLK Jr Blvd										
2036A0004Z	36th St N - Peoria Ave to Lewis Ave										
2036A0005Z	36th St N - Osage Cnty Line to MLK Blvd										
2036A0006Z	31st St N - 53rd W Ave to 41st W Ave										
2036A0007Z	Apache St - Harvard Ave to Yale Ave			C&K							
2036A0008Z	Pine St - Gilcrease Museum Rd to Union			Benham							
2036A0009Z	Pine St - Peoria Ave to Lewis Ave										
2036A0010Z	Edison St - 33rd W Ave to Union Ave										
2036A0011Z	33rd W Ave - Apache St to Pine St										
2036A0012Z	33rd W Ave - Pine St to Edison St										

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

3/1/2021

Budget Number	Project Description	DESIGN					CONSTRUCTION				
		Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036A0013Z	Gilcrease Museum Rd - Apache to Pine			Benham							
2036A0014Z	MLK Jr Blvd - 56th St N to 46th St N										
2036A0015Z	MLK Jr Blvd - 36th St N to Apache St										
2036A0016Z	MLK Jr Blvd - Apache St to Pine St										
2036A0017Z	Peoria Ave - 56th St N to 46th St N										
2036A0018Z	Peoria Ave - 46th St N to 36th St N										
2036A0019Z	Peoria Ave - Pine St to Admiral Blvd										
2036A0020Z	Lewis Ave - Pine St to Admiral Pl										
2036A0021Z	Harvard Ave - Mohawk Blvd to 36th St N										
2036A0025Z	41st St S - Union Ave to Elwood Ave			BKL							
2036A0026Z	51st St S - 33rd W Ave to Union Ave										
2036A0027Z	61st St S - Lewis Ave to Harvard Ave										
2036A0028Z	Elwood Ave - 71st St S to 81st St S										
2036A0029Z	Lewis Ave - 61st St S to 71st St S										
2036A0030Z	Lewis Ave - 71st St S to 81st St S										
2036A0031Z	Delaware Ave - 81st St S to 91st St S										
2036A0032Z	Harvard Ave - 61st St S to 71st St S										
2036A0033Z	Harvard Ave - 71st St S to 81st St S										
2036A0034Z	Harvard Ave - 81st St S to 91st St S										
2036A0039Z	36th St N - Garnett Rd to 129th E Ave										
2036A0040Z	36th St N - 129th E Ave to 141st E Ave										
2036A0041Z	Apache St - Gilcrease Expy to Sheridan Rd										
2036A0042Z	Pine St - Lewis Ave to Harvard Ave			McClelland							
2036A0043Z	Pine St - State Hwy 11 to Mingo Rd			Poe							
2036A0044Z	Pine St - Mingo Rd to Garnett Rd										
2036A0045Z	Pine St - Garnett Rd to 129th E Ave										
2036A0046Z	Admiral Pl - Sheridan Rd to Memorial Dr										
2036A0047Z	Admiral Pl - Memorial Dr to Mingo Rd			CEC							
2036A0048Z	Admiral Pl - Garnett Rd to 129th E Ave										
2036A0049Z	11th St S - Memorial Dr to 89th E Ave										
2036A0050Z	Yale Ave - Apache St to Pine St			FNI							
2036A0051Z	Yale Ave - Pine St to Admiral Pl										
2036A0052Z	Sheridan Rd - 36th St N to Apache St										
2036A0053Z	Garnett Rd - Admiral Pl to 11th St S										
2036A0054Z	129th E Ave - 36th St N to Apache St										
2036A0055Z	129th E Ave - Apache St to Pine St			Olsson							
2036A0064Z	11th St S - Utica Ave to Lewis Ave			Wallace							

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

31/1/2021

Budget Number	Project Description	DESIGN					CONSTRUCTION				
		Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036A0065Z	11th St S - Harvard Ave to Yale Ave										
2036A0066Z	15th St S - Boston Ave to Denver Ave										
2036A0067Z	15th St S - Harvard Ave to Yale Ave										
2036A0068Z	21st St S - Lewis Ave to Harvard Ave										
2036A0069Z	21st St S - Harvard Ave to Yale Ave										
2036A0070Z	Peoria Ave - 21st St S to 31st St S										
2036A0077Z	15th St S - Sheridan Rd to 73rd E Ave										
2036A0078Z	41st St S - Yale Ave to Sheridan Ave										
2036A0079Z	Yale Ave - 31st St S to 36th St S										
2036A0080Z	Yale Ave - 41st St S to I-44										
2036A0081Z	Sheridan Rd - 21st St S to 31st St S										
2036A0082Z	Sheridan Rd - 31st St S to 41st St S										
2036A0083Z	Sheridan Rd - 41st St S to 51st St S										
2036A0086Z	Admiral Pl: 225th EA to 22200 Blk E Adm.										
2036A0087Z	11th St S - 145th E Ave to 161st E Ave										
2036A0088Z	11th St S - 161st E Ave to 177th E Ave										
2036A0089Z	11th St S - 177th E Ave to 193rd E Ave										
2036A0090Z	21st St S - 145th E Ave to 161st E Ave										
2036A0091Z	21st St S - 161st E Ave to 177th E Ave										
2036A0092Z	31st St S - Garnett Rd to 129th E Ave										
2036A0093Z	41st St S - 177th E Ave to 193rd E Ave			Marquardt							
2036A0094Z	129th E Ave - 51st St S to 61st St S										
2036A0095Z	145th E Ave - 11th St S to 21st St S										
2036A0096Z	145th E Ave - 21st St S to 31st St S										
2036A0097Z	161st E Ave - 11th St S to 21st St S										
2036A0108Z	61st St S - Sheridan Rd to Memorial Dr										
2036A0109Z	Memorial Dr - 51st St S 61st St S										
2036A0110Z	Mingo Rd - 61st St S to 71st St S										
2036A0111Z	Mingo Rd - 91st St S to 101st St S										
2036A0113Z	101st St S - Yale Ave to Sheridan Ave										
2036A0114Z	101st St S - Sheridan Rd to Memorial Dr										
2036A0115Z	111st St S - Yale Ave to Sheridan Rd										
2036A0116Z	121st St S - Yale Ave to Sheridan Rd										
2036A0117Z	Yale Ave - 61st St S to 71st St S										
2036A0118Z	Yale Ave - 111th St S to 121st St S										
2036A0119Z	Sheridan Rd - 71st St S to 81st St S			CGA							
2036A0122Z	41st St S - Riverside Dr to Peoria Ave										

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

31/1/2021

Budget Number	Project Description	DESIGN					CONSTRUCTION				
		Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036A0123Z	41st St S - Peoria Ave to Lewis Ave										
2036A0124Z	Peoria Ave - 31st St S to 41st St S										
2036A0125Z	Lewis Ave - 41st St S to I-44										
	Intersection Projects										
2036A0022Z	36th St N & Harvard Ave Intersection										
2036A0023Z	Apache St & MLK Jr Blvd Intersection										
2036A0024Z	Pine St & Gilcrease Museum Rd Intersection										
2036A0035Z	41st St S & Elwood Ave Intersection			BKL							
2036A0036Z	51st St S & 33rd W Ave Intersection										
2036A0037Z	71st St S & Union Ave Intersection										
2036A0038Z	81st St S & Union Ave Intersection										
2036A0056Z	36th St N & 129th E Ave Intersection										
2036A0057Z	Pine St & Sheridan Rd Intersection										
2036A0058Z	Pine St & Mingo Rd Intersection			Poe							
2036A0059Z	Pine St & Garnett Rd Intersection										
2036A0060Z	Admiral Pl & Sheridan Rd Intersection										
2036A0061Z	Admiral Pl & Garnett Rd Intersection										
2036A0062Z	11th St S & Sheridan Rd Intersection										
2036A0063Z	11th St S & Mingo Rd Intersection										
2036A0071Z	11th St S & Peoria Ave Intersection										
2036A0072Z	11th St S & Lewis Ave Intersection			Wallace							
2036A0073Z	11th St S & Harvard Ave Intersection										
2036A0074Z	15th St S & Harvard Ave Intersection										
2036A0075Z	21st St S & Harvard Ave Intersection										
2036A0076Z	31st St S & Peoria Ave Intersection										
2036A0084Z	15th St S & Sheridan Rd Intersection										
2036A0085Z	41st St S & Yale Ave Intersection										
2036A0098Z	11th St S & 145th E Ave Intersection										
2036A0099Z	11th St S & 161st E Ave Intersection										
2036A0100Z	11th St S & 177th E Ave Intersection										
2036A0101Z	11th St S & 193rd E Ave Intersection										
2036A0102Z	21st St S & 145th E Ave Intersection										
2036A0103Z	21st St S & 161st E Ave Intersection										
2036A0104Z	21st St S & 177th E Ave Intersection										
2036A0105Z	21st St S & 193rd E Ave Intersection										
2036A0106Z	31st St S & 145th E Ave Intersection										
2036A0107Z	41st St S & 177th E Ave Intersection										

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

3/1/2021

Budget Number	Project Description	DESIGN					CONSTRUCTION				
		Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2037B0425Z	Bridge #425										
2037B0225Z	Bridge #225										
2037B0167Z	Bridge #167										
2037B0173Z	Bridge #173			Garver							
2037B0236Z	Bridge #236			Poe							
2037B0241Z	Bridge #241										
2037B0261A	Bridge #261A			CP&Y							
2037B0261B	Bridge #261B			Garver							
2037B0269Z	Bridge #269			Garver							
2037B0474Z	Bridge #474			Benham							
2037B0482Z	Bridge #482										
2037B0153Z	Bridge #153										
2037B0183Z	Bridge #183										
2037B0252Z	Bridge #252										
2037B0271Z	Bridge #271										
2037B0322Z	Bridge #322										
2037B0329Z	Bridge #329			Benham							
2037B0478Z	Bridge #478										
2037B0204Z	Bridge #204										
2037B0315Z	Bridge #315			CP&Y							
2037B0336Z	Bridge #336										
2037B0404Z	Bridge #404										
2037B0346Z	Bridge #346										
2037B0423Z	Bridge #423										
2037B0424Z	Bridge #424			Benham							
2037B1000Z	Citywide Bridge Rehab and Inspection										
Citywide Projects											
	Citywide ADA Transition Plan Impl & Update (ROW)										
2036X0001Z	Transition Plan Update										
2036X0002Z	Transit Stops										
2036X0003Z	Signalized Intersections										
2036S0001Z	Sidewalk Corridors			BKL							
				BKL							
2036X0004Z	Citywide Infrastructure Partnership Funds										
2036N0001Z	Citywide Non-Arterial Routine & Preventive										
2036A1000Z	Citywide Arterial Routine and Preventive										
2036A1001Z	Pavement Reinspection										

CITY OF TULSA, OKLAHOMA
 SALES TAX OVERVIEW COMMITTEE
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

31/1/2021

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2035X0001Z	Transit-MTTA-Route 66 Bus Rapid Transit			HNTB							
	Traffic Engineering										
2036X0005Z	Signal Coordination & Communication										
2036X0006Z	Signal Installation, Repair and Replace										
2036X0007Z	Traffic Calming										
2036X0008Z	Lighting Repair and Replacement										
2036X0009Z	Pavement Markings and Signs										
2036X0010Z	Guardrail Repair and Replacement										
2039X0009Z	Traffic Studies										
	Bicycle-Pedestrian Infrastructure										
2036S0002Z	Go Plan Implementation - Engineering			Garver							
2036S0003Z	Go Plan Implementation-Traffic Operation			Traffic							
2036S0004Z	Arterial Sidewalk			Strt & Strmwtr							
2036S0005Z	Non Arterial Sidewalk			Strt & Strmwtr							
2036X0011Z	Arena District Mstr Plan Implementation										
TOTAL FUNDS 4281-4285 - 2020 STREETS GENERAL OBLIGATION BOND											

* Same design contract for \$35,000

** Same design contract for \$15,000

* Total contract with Becco is \$4,448,000 for stormwater project 993311 & street projects 6008-014180 & 6312-994526



Finance and Economic Indicators

STOC

SALES TAX OVERVIEW COMMITTEE

Ashley Webb
Chair

Ashley R. Webb
Riggs, Abney, Neal, Turpen, Orbison & Lewis Inc.
Attorney At Law
Tulsa, OK 74119
(918) 699-8905

To: City Council

Date: April 7th, 2021

Subject: March Report to City Council

Attached is the February 2021 Sales Tax Overview Committee (STOC) Status Report.

2006 Special Extended Sales Tax

February expenditures totaled \$172,498, almost all which was spent on the Performing Arts Center Rehabilitation project. Encumbrances and commitments total \$4,405,344. Current appropriations for the Special Extended Sales Tax Fund total \$271,344,933. There is a current appropriation balance of \$10,437,771.

2008 Sales Tax Special Temporary Streets Fund

Expenditures in February totaled \$2,737, almost all of which was spent on the Citywide Arterial Routine and Preventative project. To date, \$145,179,360 has been spent in this fund. Encumbrances and commitments total \$189,163. Life to date appropriations total \$145,493,500. There is a current appropriation balance of \$124,977.

2014 Sales Tax Fund

February expenditures totaled \$3,225,923, of which \$1.4 million was spent on the Citywide Arterial Rehabilitation project. To date, \$310,185,858 has been spent in this fund. Encumbrances and commitments total \$77,874,505. Total life-to-date appropriations for the 2014 Sales Tax Fund are \$567,377,764. There is a current appropriation balance of \$179,317,400.

2016 Sales Tax Fund

February expenditures totaled \$1,657,430 within the 2016 Tulsa Vision Sales Tax Fund, almost all of which was spent on the monthly transfer to service debt on the Tulsa Vision Advanced Sales Tax Revenue Bonds. To date, \$75,303,955 has been spent in this fund. Encumbrances and commitments total \$22,368,645. Total life-to-date appropriations for the 2016 Sales Tax Fund are \$127,143,645. There is a current appropriation balance of \$29,471,044.

2016 Revenue Bond Fund

February expenditures totaled \$3,449,921 within the 2016 Tulsa Vision Revenue Bond Program with \$1.6 million being spent on the BMX National Headquarters project. Total life to date appropriations within the fund are \$350,600,000. Encumbrances and commitments total \$114,355,641. There is a current appropriation balance of \$68,855,188.

STOC Chair Report to the City Council
April 7th, 2021

2020 General Obligation Bonds

February expenditures totaled \$251,707, of which \$83,000 was spent on the Maintenance Zone 4021 (13th St. from Peoria Ave. to Utica Ave., Quaker Ave., Quincy Ave., Rockford Ave., St. Louis Ave., Trenton Ave. and Troost Ave. from 13th St. to 13th Pl. and St. Louis Ave. from 13th Pl. to 15th St) project. To date, \$1,208,608 has been spent in this fund. Encumbrances and commitments total \$3,886,387. Life to date appropriations for the 2020 General Obligation Bond Fund total \$17,500,000. There is a current appropriation balance of \$12,405,005.

2014 General Obligation Bonds

February expenditures totaled \$1,800,702, with \$516,000 being spent on the Citywide Non-Arterial Routine and Preventative Maintenance. project. To date, \$165,735,482 has been spent in this fund. Encumbrances and commitments total \$37,399,848. Life to date appropriations for the 2014 General Obligation Bond Fund total \$277,500,000. There is a current appropriation balance of \$74,364,671.

2008 General Obligation Bonds


February expenditures totaled \$405,676, almost all of which was spent on the Maintenance Zone 1007 (North side Latimer St. / North side E. Haskell St. / West side N. Utica Ave.) project. To date, \$209,104,278 has been spent in this fund. Encumbrances and commitments total \$37,399,848. Life to date appropriations for the 2008 General Obligation Bond Fund total \$230,054,937. There is a current appropriation balance of \$9,232,100.

2005 General Obligation Bonds

There were \$0.00 expenditures in February. To date, \$74,004,600 has been spent in this fund. Encumbrances and commitments total \$3,126. Current appropriations for the 2005 General Obligation Bond Fund total \$74,919,257. There is a current appropriation balance of \$911,531.

Respectfully submitted,

Ashley Webb, Chair



Attachments

cc: James Wagner
Keith Eldridge
Gary Hamer



FINANCIAL REPORT TO CITY COUNCIL

Wednesday, April 7, 2021

I. Financial Report

Revenue: 2014 Extended 1.1 Percent and 2016 Vision 0.305 Percent Sales Tax Funds

	Fiscal Year to Date		
	March	Thru March	Actual vs Budget
Actual	\$ 8,584,471	\$ 81,253,906	\$ 3,676,105
Adopted Budget - Current Year	8,082,448	77,577,801	502,023

Expenditures

Fund	February	Fiscal Year to Date
		Thru February
4001, 4003-4004 - Tulsa Vision Rev Bonds	\$ 6,899,843	\$ 92,789,895
4000 - Tulsa Vision Sales Tax	3,314,860	30,907,584
405 - 2014 Sales Tax	6,451,846	72,105,052
404 - 2008 Streets Temporary Sales Tax	5,473	4,922,572
402 - 2006 Special Extended Sales Tax	344,996	2,223,029

II. Expenditures in Other Funds

Fund	February	Fiscal Year to Date
		Thru February
403 - 2006 Advance Funded Sales Tax	0	0
401 - 2001 Sales Tax	118,354	600,522
408 - 2020 GO Bond	503,415	2,383,736
427 - 2014 GO Bond	3,601,404	37,085,036
426 - 2008 GO Bond	811,351	3,186,582
425 - 2005 GO Bond	0	388,587
TOTAL \$	5,034,524	\$ 43,644,462

III. Items for the City Council's Attention

- A. Monthly Financial Reports
- B. STOC Committee and Subcommittee Minutes and Reports

IV. Attachments

- A. Attendance Record for the last 12 months
- B. STOC Committee and Subcommittee Minutes and Reports

Respectfully submitted,

Ashley R. Webb, Chair

Attachments

cc: James Wagner
Keith Eldridge
Gary Hamer

MAJOR CAPITAL IMPROVEMENTS CONSTRUCTION FUNDS SUMMARY
As of February, 2021

	CURRENT		EXPENDITURES		ENCUMBERED COMMITTED	PERCENT	BALANCE				
	APPROPRIATIONS		Current Month	To Date							
Fund 401 and Fund 403 2001 Third Penny Sales Tax and 2006 Advance Funded Sales Tax	\$	112,418,465	\$	59,177	\$	112,393,153	\$	14,589	100%	\$	10,723
Fund 402 2006 Third Penny Sales Tax Extension	\$	271,344,933	\$	172,498	\$	256,501,819	\$	4,405,344	96%	\$	10,437,771
Fund 404 2008 Sales Tax Special Temporary Streets Fund	\$	145,493,500	\$	2,737	\$	145,179,360	\$	189,163	100%	\$	124,977
Fund 405 2014 Sales Tax Fund	\$	567,377,764	\$	3,225,923	\$	310,185,858	\$	77,874,505	68%	\$	179,317,400
Fund 406: 4000 2016 Sales Tax Fund	\$	127,143,645	\$	1,657,430	\$	75,303,955	\$	22,368,645	77%	\$	29,471,044
Fund 406: 4001, 4003, 4004 2016 Revenue Bond Fund	\$	350,600,000	\$	3,449,921	\$	167,389,171	\$	114,355,641	80%	\$	68,855,188
Fund 428 2020 General Obligation Bonds	\$	17,500,000	\$	251,707	\$	1,208,608	\$	3,886,387	29%	\$	12,405,005
Fund 427 2014 General Obligation Bonds	\$	277,500,000	\$	1,800,702	\$	165,735,482	\$	37,399,848	73%	\$	74,364,671
Funds 426 2008 General Obligation Bonds	\$	230,054,937	\$	405,676	\$	209,104,278	\$	11,718,558	96%	\$	9,232,100
Funds 425 2005 General Obligation Bonds	\$	74,919,257	\$	-	\$	74,004,600	\$	3,126	99%	\$	911,531
Fund 740: 7401-7408 TMUA--Water Capital Fund	\$	380,354,697	\$	2,688,135	\$	265,006,652	\$	51,039,714	83%	\$	64,308,331
Funds 750: 7501-7520 TMUA-Sanitary Sewer Capital Funds	\$	484,713,375	\$	1,685,896	\$	345,060,370	\$	78,622,644	87%	\$	61,030,361

Report On Tulsa Economic Indicators January 2020

Economic Overview

Economic Overview will be updated at the end of every quarter. For the most recent update please refer to December – Tulsa Economic Indicators Report. The Next EO summary will be posted with the March 2021 Report.

Wage & Salary Employment Conditions

Labor force participation numbers from OESC has not been provided at the time of this report. The Total Employment survey reported by OESC has not been provided for January data. The area unemployment rate has also not been provided for January data from OESC. Total unemployment for the area was 3.2% this time last year. Regarding the second employment survey, Wage and Salary Employment numbers were also not available from OESC at the time for this report for January data. The Manufacturing, Service, and Trade sector numbers for TMSA were not reported by OESC for the month of January.

Construction Conditions

Single family residential construction activity in the metro area increased in January, reporting a total of 91 single family residential permits for the month. This was an increase of 75.0% over the previous month as well as a 355.0% increase over this time last year. There were 0 multi-family construction permits issued in January, increasing the year to date total at 0. Total commercial construction permits fell in January, reporting a decrease of \$-7.22 million for a total of \$ 7.5 million for the month. There was \$4.5 million in Retail sector permits issued in January. This was up from previous month of \$3.9M. Finally, there were \$3.0M in Office sector permits issued in January.

Freight Conditions

TIA reported January boarding at 45,885 passengers. Outgoing passenger counts fell by -11,631 over the previous month. This time last year, the airport reported a total 104,283 for the month. January cargo fell at the TIA, decreasing by -630 tons, and reporting a total of 4,715 tons shipped in January. Lastly, freight at the Port of Catoosa reported 139,697 of barge tonnage for the month. This is down vs. previous month by 34,473 in barge tonnage.

Enterprise Customers

Sewer customer totals decreased by -220 customers in January totaling 133,111. The current customer base is 0.4%, greater than this time last year. Water Customers also decreased by -225 customers in January totaling 141,065. The current customer base is 0.4%, greater than this time last year.

Price Indices

PPI was up in January at 210.2

MCI moved up 1.1% in January to 261.1

CPI-U moved up 0.3% in January to 249.2ⁱ

20 Year GO Bond rates moved up 6 basis points to 2.18% in January

Revenue Bond rates fell by 1 basis points to 2.56% in January

30-Day Treasury Bill rates remained stable at 0 basis point to 0.069% in January

ⁱ The annualized average for Fiscal year 2018 was 235.4. The annualized median for the last three Fiscal Years was 230.7

Tulsa Economic Indicators


Most Recent Twelve Months

(unless otherwise Indicated)


	February 20 to January 21	February 19 to January 20	Change
Wage & Salary			
Employment (TMSA 12 Mo. Avg.):	<u>Jan-21</u>	<u>Jan-20</u>	
Manufacturing	NA**	54,000	NA**
Services	NA**	227,400	NA**
Trade	NA**	86,000	NA**
Other	<u>NA**</u>	<u>88,300</u>	NA**
Total	NA**	455,700	NA**
Unemployment Rates (TMSA 12 Mo. Avg.):			
	<u>Jan-21</u>	<u>Jan-20</u>	
Tulsa MSA	NA**	3.3%	NA**
Oklahoma	6.6%	3.3%	3.3%
United States	8.4%	3.6%	4.8%
Tulsa City Construction (Calendar YTD): *			
	<u>Jan-21</u>	<u>Jan-20</u>	
Single Family Units	91	20	>100.00%
Multi-Family Units	0	0	(99.0%)
Value of :			
Retail Permits	\$4,540,000	\$1,060,000	>100.00%
Office Permits	\$3,000,000	\$100	>100.00%
Industrial Permits	\$0	\$170,000	(100.0%)
Air Passengers (Calendar YTD):			
	<u>Jan-21</u>	<u>Jan-20</u>	
Air Passengers (Calendar YTD):	45,900	104,300	(56.0%)
Barge Tonnage (Calendar YTD):			
	<u>Jan-21</u>	<u>Jan-20</u>	
Barge Tonnage (Calendar YTD):	139,700	146,300	(4.5%)
Price and Cost Indices:			
	<u>Jan-21</u>	<u>Jan-20</u>	
Consumer Price Index - Urban	249.2	245.5	1.5%
Producer Price Index	210.2	207.3	1.4%
Municipal Cost Index (Est.)	261.1	255.6	2.2%
(Indices are not adjusted for seasonality)			
Financial Rates (Monthly Avg.):			
	<u>Jan-21</u>	<u>Jan-20</u>	
30-Day Treasury Bill	0.069%	1.54%	(1.48)
Municipal General Obligation Bond			
Buyer 11 Bond Index (20 Yr. A-AAA)	2.18%	2.75%	(0.57)
Municipal Revenue Bond Buyer			
25 Bond Index (25 Yr. A-AA+)	2.56%	3.22%	(0.66)
Utilities:			
	<u>Jan-21</u>	<u>Jan-20</u>	
Water Customers	141,100	140,500	0.4%
Sewer Customers	133,100	132,500	0.5%

*Data unavailable at time of report. Therefore figure is a 12 month average forecast.


Rates on Municipal Investments and Cost of Financing**

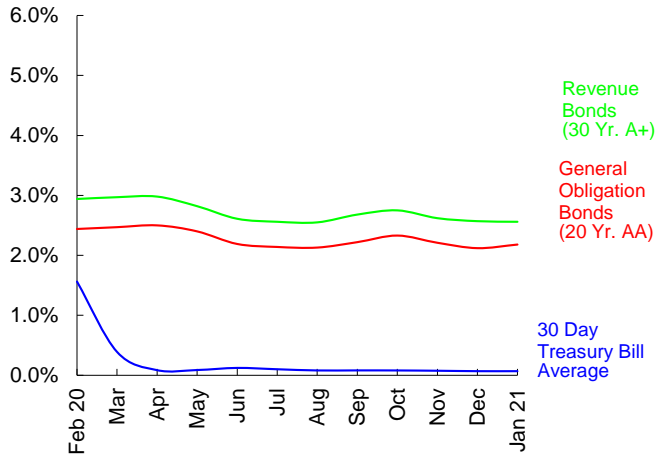


Consumers, Producers, and Municipal Price/Cost Indices

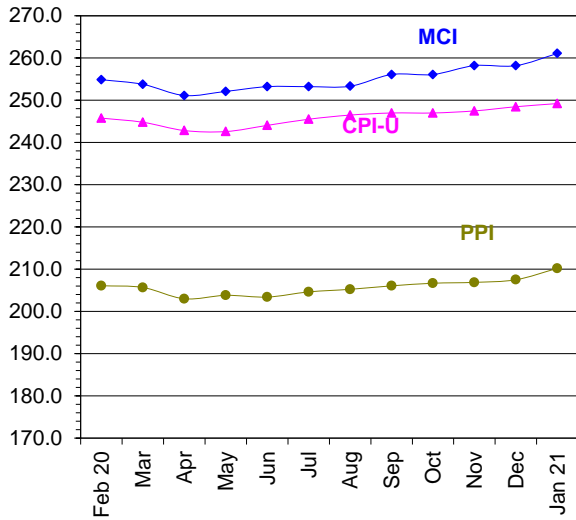

Monthly (- -) and Average (—) Unemployment Rates (Most Recent 12 Months)

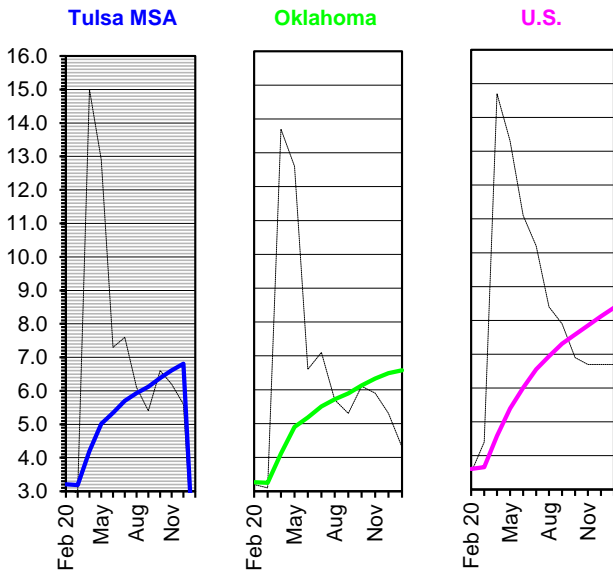

Tulsa MSA Wage & Salary Employment and 12 Month Moving Average (000's)

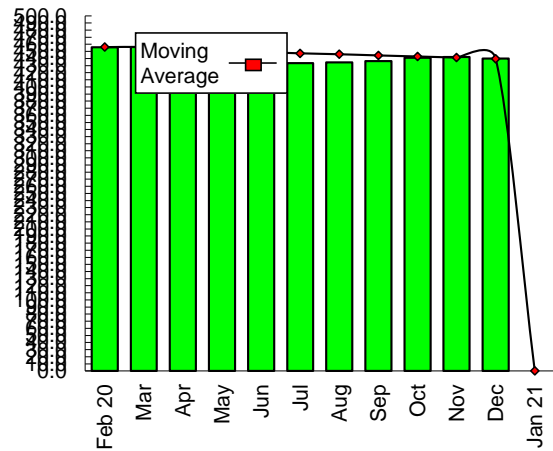

*Data unavailable at time of report. Therefore figure is a 12 month average forecast.

**Short Term Capital Purchases Summary (Fund 477) as of February 2021
2006 Sales Tax Capital Equipment Replacement Report**

Department/Entitiy	Appropriations	Month's Expenditures	Year to Date Expenditures	Encumbrances Commitments	Balance
Human Resources	\$ 41,504	\$ 8,849	\$ 8,849	\$ -	\$ 32,655
Finance	\$ 47,000	\$ -	\$ -	\$ 14,745	\$ 32,255
Legal	\$ 4,800	\$ -	\$ -	\$ -	\$ 4,800
Asset Management	\$ 498,823	\$ 45,243	\$ 90,745	\$ 46,773	\$ 361,305
Information Technology	\$ 5,637,641	\$ 108,474	\$ 2,554,840	\$ 1,594,488	\$ 1,488,313
Police	\$ 5,741,816	\$ 432,485	\$ 3,134,405	\$ 2,121,881	\$ 485,530
Fire	\$ 796,175	\$ -	\$ 14,141	\$ 356,046	\$ 425,988
Engineering Services	\$ 173,117	\$ -	\$ 787	\$ -	\$ 172,330
Streets & Stormwater	\$ 1,984,667	\$ 181,246	\$ 471,848	\$ 1,044,476	\$ 468,343
Parks & Recreation	\$ 577,189	\$ 16,472	\$ 186,319	\$ 175,713	\$ 215,157
WIN	\$ 314,746	\$ -	\$ 114,074	\$ 0	\$ 200,672
Development Services	\$ 181,438	\$ -	\$ 87,802	\$ -	\$ 93,636
City Council	\$ 5,000	\$ 4,033	\$ 4,033	\$ 967	\$ -
Transfer to Other Funds*	\$ 92,000	\$ -	\$ 92,000	\$ -	\$ -
Transfer to River Parks*	\$ 36,000	\$ -	\$ 36,000	\$ -	\$ -
Transportation Grants to MTTA*	\$ 92,000	\$ 92,000	\$ 92,000	\$ -	\$ -
	\$ 16,223,916.00	\$ 888,802.50	\$ 6,887,844.47	\$ 5,355,090.39	\$ 3,980,981.14

* Total appropriation is transferred to the agency in a lump sum during the year and incorporated into their budget.

City of Tulsa
Department of Finance
FINANCIAL REPORT



SALES TAX OVERVIEW COMMITTEE

PERIOD ENDING **February 28, 2021**

City of Tulsa
Department of Finance
FINANCIAL REPORT



G. T. Bynum
Mayor

James Wagner
Director of Finance

MAYOR

G. T. Bynum

CITY COUNCIL

VANESSA HALL-HARPER.....DISTRICT 1
JEANNIE CUEDISTRICT 2
CRISTA PATRICKDISTRICT 3
KARA JOY MCKEEDISTRICT 4
MYKEY ARTHRELL-KNEZEK.....DISTRICT 5
CONNIE DODSONDISTRICT 6
LORI DECTER WRIGHTDISTRICT 7
PHIL LARKIN JRDISTRICT 8
JAYME FOWLERDISTRICT 9

CITY AUDITOR

CATHY CRISWELL

SALES TAX OVERVIEW COMMITTEE

Ashley Webb, Chair
Linda Jenkins, Vice Chair
Rhonda Hinrichs, Secretary

Rhonda Hinrichs	Linda Jenkins
Paul McTighe	Sylvia Powell
Karen O'Brien	Renee Plocek
David Blatt	Ashley Webb
Kathy Sebert	Daryl Tannehill
Jesse Guardiola	Alex Gomez
Ellouise Cochran	Janae Bradford
Jonathan Hall	Steve King
Scott Grizzle	Steven Watts
Pamela Amburgy	Mareo Johnson
Marcia Bruno-Todd	

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
BALANCE SHEET
FEBRUARY 2021**

	FUND 402 2006 SPECIAL EXTENDED SALES TAX	FUND 404 2008 SPECIAL TEMPORARY SALES TAX	FUND 405 2014 EXTENDED 1.1% SALES TAX	FUND 4000 2016 LIMITED PURPOSE TEMPORARY SALES TAX	FUNDS 4260 through 4266 2008 GO BOND FUNDS	FUNDS 4270 through 4274 2014 GO BOND FUNDS	FUNDS 4281 through 4285 2020 GO BOND FUNDS	TOTAL
ASSETS:								
POOLED EQUITY WITH TREASURER	\$15,915,825.21	\$4,602,534.13	\$254,246,577.01	\$43,393,256.59	\$22,299,994.85	\$113,582,026.15	\$16,267,483.12	\$454,040,213.94
ACCRED INTERST RECEIVABLE	64,208.09	22,999.96	948,783.62	161,429.98				\$1,197,421.65
OTHER CURRENT RECEIVABLES				3,175,236.32				\$3,175,236.32
TAX RECEIVABLE			11,451,671.97	1,283,552.45				\$12,735,224.42
TOTAL ASSETS	\$15,980,033.30	\$4,625,534.09	\$266,647,032.60	\$48,013,475.34	\$22,299,994.85	\$113,582,026.15	\$16,267,483.12	\$471,148,096.33
LIABILITIES, RESERVES, AND FUND BALANCE:								
LIABILITIES AND RESERVE FOR ENC.:								
ACCOUNTS PAYABLE			52,562.39					52,562.39
CONTRACTS PAYABLE - RETAINAGE	115,660.54	338,285.77	1,557,206.81	238,865.82	639,164.33	1,948,238.76	1,883.27	4,837,422.03
CONTRACTS RETAINAGE CLEAR			20,413.40		294,095.52			314,508.92
PURCHASING CARD ESCROW DUE TO OTHER FUNDS								
ADVANCES FROM OTHER FUNDS								
RESERVE FOR ENCUMBRANCES	4,379,344.40	189,162.53	53,443,855.98	17,439,962.43	434,900.82	36,438,878.51	3,886,387.33	112,326,104.67
RESERVE FOR COMMITMENTS								
UNENCUMBERED FUND BALANCE:								
APPROPRIATED	10,437,770.50	124,977.17	179,317,400.36	29,471,044.48	9,232,100.48	74,364,670.56	12,379,212.52	302,947,963.55
UNAPPROPRIATED	1,047,257.86	3,973,108.62	32,255,593.66	863,602.61	11,699,733.70	830,238.32		50,669,534.77
RESERVED FOR ADVANCES								
TOTAL FUND BALANCE	11,485,028.36	4,098,085.79	211,572,994.02	30,334,647.09	20,931,834.18	75,194,908.88	12,379,212.52	353,617,498.32
TOTAL LIABILITIES, RESERVES, AND FUND BALANCE	\$15,980,033.30	\$4,625,534.09	\$266,647,032.60	\$48,013,475.34	\$22,299,994.85	\$113,582,026.15	\$16,267,483.12	\$471,148,096.33

CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
SCHEDULE OF SALES TAX REVENUE
February 2021

Month	COMPARISON TO BUDGET (2020-2021)			COMPARISON TO PRIOR YEAR				
	BUDGET	ACTUAL	DIFFERENCE	2019-2020	2020-2021	AMOUNT	PERCENT	
	AMOUNT	AMOUNT		ACTUAL	ACTUAL	INCREASE (DECREASE)	INCREASE/DECREASE ACTUAL BUDGET	
July	\$ 8,610,765.00	\$ 8,818,368.59	\$ 207,603.59	\$ 9,217,603.00	\$ 8,818,368.59	\$ (399,234.41)	-4.3%	-6.6%
August	\$ 8,698,132.00	\$ 9,272,936.78	574,804.78	\$ 9,263,735.00	\$ 9,272,936.78	9,201.78	0.1%	-6.1%
September	\$ 8,558,231.00	\$ 8,993,120.86	434,889.86	\$ 9,079,958.00	\$ 8,993,120.86	(86,837.14)	-1.0%	-5.7%
October	\$ 8,513,070.00	\$ 9,240,958.34	727,888.34	\$ 9,287,215.00	\$ 9,240,958.34	(46,256.66)	-0.5%	-8.3%
November	\$ 8,409,734.00	\$ 8,961,579.94	551,845.94	\$ 8,934,897.00	\$ 8,961,579.94	26,682.94	0.3%	-5.9%
December	\$ 8,540,060.00	\$ 8,742,413.11	202,353.11	\$ 9,124,882.00	\$ 8,742,413.11	(382,468.89)	-4.2%	-6.4%
January	\$ 9,026,643.00	\$ 9,279,328.26	252,685.26	\$ 9,749,388.00	\$ 9,279,328.26	(470,059.74)	-4.8%	-7.4%
February	\$ 9,138,718.00	\$ 9,360,728.24	222,010.24	\$ 10,050,199.00	\$ 9,360,728.24	(689,470.76)	-6.9%	-9.1%
March		\$ -	-		\$ -	-	#DIV/0!	#DIV/0!
April		\$ -	-		\$ -	-	#DIV/0!	#DIV/0!
May		\$ -	-		\$ -	-	#DIV/0!	#DIV/0!
June		\$ -	-		\$ -	-	#DIV/0!	#DIV/0!
TOTAL	\$ 69,495,353.00	\$ 72,669,434.12	\$ 3,174,081.12	\$ 74,707,877.00	\$ 72,669,434.12	\$ (2,038,442.88)	-2.7%	-7.0%

PERCENT INCREASE (DECREASE) 4.37%

2006 SPECIAL EXTENDED SALES TAX

FUND 402

(SIXTH THIRD PENNY SALES TAX PROGRAM)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 402 - 2006 SPECIAL EXTENDED SALES TAX**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE EIGHT MONTHS ENDED FEBRUARY 28, 2021**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
Revenue					
Sales Tax	\$	\$	\$	\$ 430,935,953.99	\$
Donations					
Interest on Investments	482,000.00	10,410.95	118,207.77	16,266,704.67	363,792.23
Intergovernmental Revenue Federal, State & Local grants Transfers from other funds					
Miscellaneous Revenue				1,424,225.61	
Total Revenue	482,000.00	10,410.95	118,207.77	448,626,884.27	363,792.23
Expenditures					
Project Expenditures	271,344,933.46	172,497.97	1,321,466.94	256,501,818.56	14,843,114.90
Total Expenditures	271,344,933.46	172,497.97	1,321,466.94	256,501,818.56	14,843,114.90
Excess (Deficiency) of Revenue Over Expenditures			(1,203,259.17)	192,125,065.71	
Completed Projects Encumbrances			4,405,344.40	174,416,586.99 4,405,344.40	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(5,608,603.57)	13,303,134.32	
June 30, 2018 Ending Fund Balance			18,829,685.06		
Prior year expenditures					
June 30, 2018 Encumbrances			82,052.83		
Adjusted Beginning Fund Balance			18,911,737.89		
Ending Fund Balance			\$ 13,303,134.32	\$ 13,303,134.32	

Fund 402
2006 SPECIAL EXTEND SALES TAX

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
402	016100	Forensic Lab Expansion	14,729,241.90	-	-	14,729,241.90	-	-	-
402	016130	Replace 2 Police Helicopters	4,344,475.00	-	-	4,344,475.00	-	-	-
402	016200	Apparatus Replacement	12,863,575.91	-	-	12,863,575.91	-	-	(0.00)
402	016240	Site Acq. For Addnl. Station	5,300,000.00	140.00	284,955.26	1,069,750.36	3,668,274.73	-	561,974.91
402	016310	Network System Replacement	1,402,150.04	-	-	1,402,150.04	-	-	-
402	017110	General Park Improvements	4,829,359.78	-	42,861.00	4,753,138.75	12,000.00	26,000.00	38,221.03
402	017120	Golf Course Development	459,640.57	-	-	459,640.57	-	-	-
402	017140	Tulsa Zoo Department	2,938,780.81	-	-	2,938,780.81	-	-	-
402	060020	Comprehensive Plan Update	649,253.49	-	-	649,253.49	-	-	-
402	060040	Equipment Mgmt Projects	2,242,000.00	-	-	2,242,000.00	-	-	0.00
402	062100	Unservd Area & Offsite Mns	7,200,000.00	-	-	7,200,000.00	-	-	-
402	062120	Sswwtp 71 Ls Expansion	400,000.00	-	-	400,000.00	-	-	-
402	062130	Spunky Crk Bsn Ms & Ls	9,497,696.77	-	-	9,497,696.77	(0.00)	-	(0.00)
402	062140	Lower Bird Creek Wwtp Expn	11,000,000.00	-	18,391.42	11,000,000.00	-	-	(0.00)
402	063101	Fred Creek Drainage Imprv	12,250,000.00	-	-	12,250,000.00	-	-	-
402	063106	Elm Crk 6th St Drainage	2,000,000.00	-	-	2,000,000.00	(0.00)	-	0.00
402	063107	Citywide Mdp Updates	450,000.00	-	-	450,000.00	-	-	-
402	063109	Engr And Insp Svc-Fc	500,000.00	-	-	500,000.00	-	-	-
402	064001	Arterial Streets Rehab	28,169,343.33	36,928.39	59,217.09	27,323,476.95	53,659.33	-	792,207.05
402	064002	Residential Streets Rehab	25,849,169.10	-	-	25,815,173.80	0.00	-	33,995.30
402	064003	Traffic Signals & Lighting	2,600,000.00	-	-	2,424,141.75	175,828.25	-	30.00
402	064004	TRAFFIC SIGNAL SYNCH	1,700,000.00	-	-	1,692,173.06	0.00	-	7,826.94
402	064005	St Surface Rpr & Crack Seal	10,000,000.00	-	-	10,000,000.00	0.00	-	(0.00)
402	064060	Bridge Replacement	2,500,000.00	-	7,586.86	2,499,613.73	385.00	-	1.27
402	064062	Bridge Rehab/Repair Cw	2,500,000.00	-	12,429.96	2,469,970.78	30,029.22	-	0.00
402	064093	City Match-Fed/St/Co Projs	1,500,000.00	-	-	1,410,000.00	90,000.00	-	-
402	064101	41St-Garnett To 129Th E Ave	500,000.00	-	16,664.10	498,500.00	1,500.00	-	0.00
402	064102	81St-Memorial To Mingo	7,402,272.09	-	-	7,402,272.09	-	-	0.00
402	064103	91St & Harvard Intersection	2,217,000.00	13,262.04	53,597.02	2,205,711.06	11,288.94	-	0.00
402	064104	91St And Sheridan Inters	4,417,718.54	-	-	4,414,613.00	-	-	3,105.54
402	064105	61St St Riverside To Peoria	800,000.00	-	143.31	705,528.20	23,660.27	-	70,811.53
402	064106	Garnett-11Th To I-244	500,000.00	-	-	499,555.00	-	-	445.00
402	064107	Mingo 71St To 81St	500,000.00	-	-	498,721.40	1,278.60	-	(0.00)
402	064108	Pine St-Memorial To Mingo	500,000.00	21,207.46	59,942.14	397,006.32	102,084.66	-	909.02
402	064109	129Th-31St To 41St	5,500,000.00	-	-	5,500,000.00	-	-	-
402	064110	61St-Riverside To Peoria	7,369,000.00	-	-	7,369,000.00	-	-	(0.00)
402	064111	91St-Memorial To Mingo	500,000.00	-	-	59,808.17	-	-	440,191.83
402	065100	Public Facilities Renov	7,080,000.00	207.63	10,339.89	6,669,432.56	135,462.01	-	275,105.43
402	065300	Energy Efficiency Facil Impr	1,600,000.00	-	-	1,134,165.67	70,052.83	-	395,781.50
402	065320	Gilcrease Museum Renovation	3,342,500.00	-	-	3,342,089.45	410.55	-	0.00
402	065330	Performing Arts Ctr Renova	1,560,000.00	100,752.45	100,752.45	1,560,000.00	-	-	-
402	066210	New Fs 11-11Th/177Th	-	-	-	-	-	-	-
402	066220	Homeland Sec Equip Facil	2,708,852.22	-	-	2,708,852.22	-	-	0.00
402	066310	Weather Alert Sirens Repl	1,694,929.61	-	-	1,694,929.61	-	-	-

Fund 402
2006 SPECIAL EXTEND SALES TAX

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
402	066320	61St Twr Comm Shelter Repl	299,964.04	-	-	299,964.04	-	-	-
402	066330	Pwr Prtct Bok Comm Site Bok	104,569.00	-	-	104,569.00	-	-	-
402	066340	Log Sys 800 Mhz Radio Sys	118,787.61	-	-	118,787.61	-	-	-
402	066350	Computer Sys Repl/Enhance	511,449.95	-	-	511,449.95	-	-	-
402	067120	Plgnd Splashpad Park Surfs	3,095,280.61	-	-	3,024,686.42	-	-	70,594.19
402	067130	Playground Equip Repl/Renov	1,063,517.00	-	-	1,054,597.78	-	-	8,919.22
402	067170	Carl Smith Facil Devel	235,421.96	-	-	231,991.95	3,430.01	-	0.00
402	067510	Trails Resurf And Widening	2,924,423.01	-	-	2,924,423.01	-	-	-
402	067520	EST BANK IMPR 11TH-21STS	5,250,000.00	-	-	346,031.29	-	-	4,903,968.71
402	067530	RVR WST FESTIVAL PRK RENOV	7,491,683.05	-	-	7,491,683.05	-	-	-
402	067540	RIVER PRKS FACIL REHAB/REPL	345,186.15	-	-	345,186.15	-	-	-
402	068100	Tda Downtown Prop Acq	1,720,000.00	-	-	1,720,000.00	-	-	-
402	068110	Kendall Whittier Plan Impl	5,000,000.00	-	-	5,000,000.00	-	-	-
402	068120	Dirty Butter Crk Acq Ph2	2,096,066.28	-	-	2,096,066.28	0.00	-	(0.00)
402	068130	Downtown Signage	1,813,710.24	-	-	1,813,710.24	-	-	-
402	068140	Econ Devel Infrastructure	3,000,000.00	-	-	3,000,000.00	-	-	-
402	068160	New Parking Garage	5,000,000.00	-	-	2,301,726.39	-	-	2,698,273.61
402	069100	Mtta System Projects	2,410,000.00	-	-	2,402,136.89	-	-	7,863.11
402	096005	Electronic Ticketing Equip	182,707.40	-	-	182,707.40	-	-	-
402	144104	Riverside Dr & Rltd Infrstr	250,252.64	-	-	250,252.64	-	-	-
402	146200	Fire - SCBA	94,389.51	-	-	94,389.51	-	-	-
402	156000	Radio Sys Upgrd & Assc Equip	3,545,000.00	-	-	3,545,000.00	-	-	-
402	170101	Capital Equipment	172,000.00	-	-	172,000.00	-	-	0.00
402	203400001Z	Tulsa Zoo Department	561,065.85	-	444,633.76	451,650.93	-	-	109,414.92
402	914411	Tulsa Trails	1,492,500.00	-	-	1,492,500.00	0.00	-	(0.00)
402	962301	Tulsa Convention Center Impr	2,000,000.00	-	-	1,981,869.61	-	-	18,130.39
402	966120	Gilcrease Exp Osage Exp-41st	4,500,000.00	-	-	4,500,000.00	-	-	-
			\$ 271,344,933.46	\$ 172,497.97	\$ 1,111,514.26	\$ 256,501,818.56	\$ 4,379,344.40	\$ 26,000.00	\$ 10,437,770.50

2008 TEMPORARY SALES TAX

FUND 404

(2008 SPECIAL TEMPORARY SALES TAX FUND)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 404 - 2008 SPECIAL TEMPORARY SALES TAX**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE EIGHT MONTHS ENDED FEBRUARY 28, 2021**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
Revenue					
Sales Tax	\$	\$	\$	\$ 144,577,118.55	\$
Donations					
Interest on Investments	257,000.00	2,991.99	43,262.53	4,025,908.52	213,737.47
Intergovernmental Revenue					
Federal, State & Local grants					
Transfers from other funds					
Miscellaneous Revenue					
Total Revenue	<u>257,000.00</u>	<u>2,991.99</u>	<u>43,262.53</u>	<u>148,603,027.07</u>	<u>213,737.47</u>
Expenditures					
Project Expenditures	145,493,500.00	2,736.50	2,958,549.74	145,179,360.30	314,139.70
Total Expenditures	<u>145,493,500.00</u>	<u>2,736.50</u>	<u>2,958,549.74</u>	<u>145,179,360.30</u>	<u>314,139.70</u>
Excess (Deficiency) of Revenue Over Expenditures			(2,915,287.21)	3,423,666.77	
Completed Projects Encumbrances			<u>189,162.53</u>	<u>189,162.53</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(3,104,449.74)	3,234,504.24	
June 30, 2018 Ending Fund Balance			6,338,953.98		
Prior year expenditures					
June 30, 2018 Encumbrances					
Adjusted Beginning Fund Balance			<u>6,338,953.98</u>		
Ending Fund Balance			<u>\$ 3,234,504.24</u>	<u>\$ 3,234,504.24</u>	

Fund 404
2008 SPECIAL TEMP SALES TAX

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
404	104009	Citywide-Arterial Rehab&Cons	4,200,000.00	-	-	4,200,000.00	-	-	-
404	104010	Citywide-Arterial Sidewalk R	1,600,000.00	-	-	1,600,000.00	-	-	-
404	104015	Citywide Nonarterial Reh&Re	100,000.00	-	-	100,000.00	-	-	-
404	104016	Citywide Nonarterial Sidewlk	702,500.00	-	-	702,500.00	-	-	-
404	104017	Art Rehab Citywide	81,942,000.00	2,622.50	4,129.31	81,854,680.85	87,010.41	-	308.74
404	104020	Citywide Nonarterial Sidewlk	15,894,000.00	-	-	15,894,000.00	-	-	(0.00)
404	104021	Citywide Non-arterial RTPV	34,082,000.00	-	2,433,738.26	33,983,662.53	16,368.66	-	81,968.81
404	104022	Citywide General Engineering	1,383,000.00	-	23,304.52	1,297,374.54	85,625.46	-	0.00
404	104023	Bridge Repair and Rehab	90,000.00	-	-	87,261.95	-	-	2,738.05
404	144104	Riverside Dr & Rltd Infrstr	5,500,000.00	114.00	114.00	5,459,880.43	158.00	-	39,961.57
			\$ 145,493,500.00	\$ 2,736.50	\$ 2,461,286.09	\$ 145,179,360.30	\$ 189,162.53	\$ -	\$ 124,977.17

2014 EXTENDED 1.1% SALES TAX

FUND 405

(2014 EXTENDED 1.1% SALES TAX FUND)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 405 - 2014 EXTENDED 1.1% SALES TAX**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE EIGHT MONTHS ENDED FEBRUARY 28, 2021**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
Revenue					
Sales Tax	\$ 80,716,900.00	\$ 7,328,684.03	\$ 56,894,218.87	\$ 546,811,060.00	\$ 23,822,681.13
Donations					
Interest on Investments	3,641,000.00	165,303.59	1,746,879.85	14,481,619.66	1,894,120.15
Intergovernmental Revenue					
Federal, State & Local grants					
Transfers from other funds					
Miscellaneous Revenue				98,580.75	
Total Revenue	<u>84,357,900.00</u>	<u>7,493,987.62</u>	<u>58,641,098.72</u>	<u>561,391,260.41</u>	<u>25,716,801.28</u>
Expenditures					
Project Expenditures	<u>567,377,763.82</u>	<u>3,225,923.23</u>	<u>43,483,178.28</u>	<u>310,183,579.82</u>	<u>257,194,184.00</u>
Total Expenditures	<u>567,377,763.82</u>	<u>3,225,923.23</u>	<u>43,483,178.28</u>	<u>310,183,579.82</u>	<u>257,194,184.00</u>
Excess (Deficiency) of Revenue					
Over Expenditures			15,157,920.44	251,207,680.59	
Completed Projects					
Encumbrances			<u>77,874,505.35</u>	<u>77,874,505.35</u>	
Excess (Deficiency) of Revenue Over					
Expenditures and Encumbrances			(62,716,584.91)	173,333,175.24	
June 30, 2018 Ending Fund Balance			227,243,786.37		
Prior year expenditures					
June 30, 2018 Encumbrances			<u>8,805,973.78</u>		
Adjusted Beginning Fund Balance			236,049,760.15		
Ending Fund Balance			<u>\$ 173,333,175.24</u>	<u>\$ 173,333,175.24</u>	

Fund 405

2014 SALES TAX

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
405	140040	Cng Fuel Expansion	1,800,000.00	-	-	1,787,810.17	-	-	12,189.83
405	140050	Radio Frequency ID Devices	750,000.00	-	-	-	-	-	750,000.00
405	140060	Emd Emergency Generators	200,000.00	-	-	191,890.18	(0.00)	-	8,109.82
405	140070	Emd Facilities Maintenance	1,000,000.00	22,829.00	85,975.20	833,020.46	(0.00)	-	166,979.54
405	140080	Emd Lights, Hvac, Plumbing	2,300,000.00	-	-	556,543.78	(0.00)	-	1,743,456.22
405	140100	Capital Equipment	46,235,000.00	636,250.00	5,090,000.00	43,689,996.00	-	-	2,545,004.00
405	143001	Levee District #12 Rehab	3,400,000.00	1,023.86	8,842.41	332,628.80	16,575.85	-	3,050,795.35
405	144003	Citywide Guardrail Repl	1,000,000.00	24,626.13	321,940.04	416,963.78	27,492.87	-	555,543.35
405	144004	CW Traffic Signalization	2,000,000.00	1,233.61	20,239.99	1,127,987.00	340,923.78	-	531,089.22
405	144005	Roadway & Pedestrian Lights	1,000,000.00	-	-	853,014.30	(0.00)	-	146,985.70
405	144006	Signing Pvmt Mark Dlintion	2,510,000.00	-	70,006.70	1,400,370.25	3,530.00	-	1,106,099.75
405	144007	Traffic Calming & Safety	1,000,000.00	2,406.96	32,706.52	936,231.85	63,768.15	-	(0.00)
405	144008	TRAFFIC SIGNAL INSTALLATION	3,000,000.00	-	713,074.16	1,829,493.79	566,161.41	-	604,344.80
405	144009	TRAFFIC SIGNAL POLE RPL	1,000,000.00	7,500.20	41,798.35	744,596.23	32,622.72	-	222,781.05
405	144010	Creek Turnpike Trail Bridge	200,000.00	-	-	-	-	-	200,000.00
405	144011	GPS Emgency Vehicle Preemp Sys	400,000.00	-	-	-	-	-	400,000.00
405	144017	Art Street Rehab & Citywide	127,340,000.00	1,392,364.33	9,821,627.10	48,124,332.60	15,382,780.15	62,500.00	63,770,387.25
405	144018	Bike Ped Master Plan Improv	4,200,000.00	612.80	876,462.95	3,899,532.03	147,212.02	-	153,255.95
405	144019	IDL Entrance Rehab	3,000,000.00	-	677,248.00	2,277,251.20	722,748.80	-	0.00
405	144020	Citywide-Arterial Rt&Pv Main	3,120,000.00	1,724.00	490,093.94	490,093.94	-	-	2,629,906.06
405	144063	Bridge Replacement And Rehab	14,685,000.00	4,831.50	940,395.00	4,717,473.68	560,915.18	-	9,406,611.14
405	144093	Citywide Matching Funds	3,429,500.00	-	52,535.19	3,429,500.00	(0.00)	-	0.00
405	144094	ODOT Rehab & Replacement	3,800,000.00	-	366,642.69	2,718,690.77	1,069,477.61	-	11,831.62
405	144101	Yale Ave 81St - 91St Wdn	35,250,000.00	58,566.61	1,102,757.04	4,950,871.05	17,597,368.33	-	12,701,760.62
405	144102	81St St Sheridan - Meml Wdn	12,000,000.00	15.00	41,225.77	1,213,024.96	8,994,680.36	-	1,792,294.68
405	144103	Yale 96th - 101st St Wdn	13,000,000.00	340,255.88	3,453,991.21	5,893,273.09	5,333,782.49	-	1,772,944.42
405	144104	Riverside Dr & Rltd Infrstr	19,000,000.00	6,044.35	43,356.45	18,127,809.44	40,646.55	-	831,544.01
405	144105	25 W Ave: Edison-Apache (DS-W)	750,000.00	5,517.69	5,517.69	5,517.69	-	-	744,482.31
405	144108	Pine St: Mingo-U.S. 169 (DS-W)	500,000.00	-	-	-	-	-	500,000.00
405	144109	Ada Transition Plan - Street	10,200,000.00	5,222.42	981,013.23	3,279,128.18	625,164.28	-	6,295,707.54
405	144120	Gilcrease Exp Local Match	7,500,000.00	67.00	14,470.42	3,395,159.09	1,034,000.00	-	3,070,840.91
405	145100	Ada Transition Plan - Bldgs	1,275,000.00	-	1,768.75	425,268.04	23,014.10	-	826,717.86
405	145200	Ada Transition Plan - Parks	1,140,000.00	-	3,791.98	372,393.93	400,237.18	-	367,368.89
405	145300	Public Facilities, Otc	3,295,000.00	-	-	507,066.10	14,446.72	473,458.62	2,300,028.56
405	145330	Pac - Fire Alarm System	520,000.00	-	-	279,088.07	-	-	240,911.93
405	145340	Pac - Fire Sprinklers	1,140,000.00	8,171.63	8,171.63	536,750.40	7,795.85	-	595,453.75
405	145350	Pac - Renovations	1,840,000.00	-	22,854.03	942,854.03	62,132.25	-	835,013.72
405	145360	Pac - Fan Coil Replacement	555,000.00	-	-	548,127.45	6,872.55	-	0.00
405	145370	Pac - Hvac Motor Replacement	175,000.00	-	-	20,000.00	155,000.00	-	-
405	145380	PAC: Roof Replacement	1,300,000.00	-	5,445.50	24,574.95	1,275,425.05	-	-
405	145400	Public Facilities, Roofing	3,000,000.00	56,108.83	1,312,815.44	2,420,143.75	204,776.51	-	375,079.74
405	145500	Animal Shelter Exprn Ph 1	2,750,000.00	-	-	89,980.00	428,529.41	-	2,231,490.59
405	145600	Animal Shelter Facility Imp	750,000.00	-	-	705,467.71	-	-	44,532.29
405	145610	Gm - Cctv Camera Upgrade	491,854.46	-	-	491,854.46	-	-	-
405	145620	Gilcrease Lib/Arch Storage	300,000.00	-	-	300,000.00	-	-	-

Fund 405

2014 SALES TAX

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
405	145630	Helmerich Hall Floor Repl	1,374.12	-	-	1,374.12	-	-	(0.00)
405	145640	Gilcrease: Gallery wood floor	-	-	-	-	-	-	-
405	145650	GM - Grease Trap & Sewer	54,047.48	-	-	54,047.48	-	-	-
405	145660	GM - Gallery Lighting Cntrls	218,393.61	-	-	218,393.61	(0.00)	-	0.00
405	145670	GM - Fire Suppression	43,119.58	-	-	43,119.51	-	-	0.07
405	145680	Gilcrease: Kitchen renovation	-	-	-	-	0.00	-	(0.00)
405	145690	GM - Perimeter Fence	30,595.39	-	-	30,595.39	-	-	0.00
405	145700	GM - Public Restroom	11,553.31	-	-	11,553.31	-	-	(0.00)
405	145710	Gilcrease: Restore N Park	-	-	-	-	-	-	-
405	145710A	Gilcrease: Restore N Park	-	-	-	-	-	-	-
405	145720	GM HVAC Humidification	1,078,145.54	-	-	976,129.11	-	-	102,016.43
405	145730	Gilcrease: Chromatic Glass	-	-	-	-	-	-	-
405	145740	GM Chilled Water Drive	155,000.00	-	-	155,000.00	-	-	-
405	145750	GM HVAC Controls	400,000.00	-	-	400,000.00	-	-	-
405	145760	GM - Halon Fire Suppression	632,623.06	-	-	632,623.06	0.00	-	(0.00)
405	145770	Gilcrease: Parking Expansion	-	-	-	-	-	-	-
405	145780	GM - Roof Replacement	1,322,531.58	-	-	1,322,531.58	(0.00)	-	0.00
405	145790	GM - Thoms Gilcrease Roof	518,324.73	-	-	518,324.73	(0.00)	-	(0.00)
405	145800	Tulsa Centrl Library Project	10,000,000.00	-	-	10,000,000.00	-	-	-
405	146100	Helicopter Replacement	2,802,000.00	-	-	2,802,000.00	-	-	-
405	146110	Police Academy-Crt-Compstat	4,040,000.00	-	231,463.02	2,874,212.92	(0.00)	-	1,165,787.08
405	146120	Uniform Division Renovations	3,000,000.00	31,781.05	148,020.07	173,508.70	205,154.30	-	2,621,337.00
405	146130	Police Capital Equipment	22,265,000.00	250,000.00	2,000,000.00	21,265,000.00	-	-	1,000,000.00
405	146200	Fire - SCBA	2,600,000.00	-	-	2,600,000.00	-	-	-
405	146210	Apparatus Replacement	17,000,000.00	-	761,375.76	11,712,285.81	4,492,948.83	294,000.00	500,765.36
405	146220	Fire Station Rehabilitation	7,250,000.00	37,544.62	577,556.40	5,411,330.80	495,815.43	-	1,342,853.77
405	146230	Fire Station Generators	1,500,000.00	-	-	942,068.86	557,931.14	-	-
405	146240	Fire Department Facilities	2,000,000.00	10,535.93	80,668.22	132,604.22	107,357.78	-	1,760,038.00
405	146300	Financial Sys Replacement	10,000,000.00	-	110,786.00	8,645,799.86	754,875.63	-	599,324.51
405	146310	Law Enforcement Records Mgmt	6,530,000.00	48,240.23	334,920.49	4,065,847.21	2,088,604.31	-	375,548.48
405	147100	Rp - Park Facilities Refurb	4,000,000.00	-	122,074.90	2,948,235.21	-	-	1,051,764.79
405	147120	Reed - Pool Reconstruction	2,410,000.00	7,131.25	35,071.62	209,969.39	2,200,030.61	-	-
405	147130	Security System Upgrades	160,000.00	-	3,213.46	85,708.45	4,000.00	-	70,291.55
405	147140	Tiger & Snow Leopard Exhibit	3,165,497.09	-	-	3,165,497.09	-	-	0.00
405	147150	Carnivores Exhibits	8,000,000.00	-	-	619.32	-	-	7,999,380.68
405	147160	Hicks Park Improvements	635,000.00	-	5,300.00	483,214.70	1,686.55	-	150,098.75
405	147170	Hunter: Restroom (Exp & Repr)	400,000.00	-	-	-	-	-	400,000.00
405	147180	Lacy Park Master Plan - Ph 1	3,600,000.00	-	-	3,583,825.97	11,000.00	-	5,174.03
405	147190	Water Playgrounds	1,580,000.00	-	12,651.60	1,076,896.75	503,103.25	-	(0.00)
405	147200	Rp - Pedestrian Bridge Imp	7,760,000.00	-	-	7,743,717.33	16,281.67	-	1.00
405	147210	Mohawk Golf Club House	265,000.00	-	35,918.75	178,395.34	-	-	86,604.66
405	147220	Page Belcher Improvements	400,000.00	-	27,865.00	176,814.20	135.70	-	223,050.10
405	147230	Savage Park Improvements	120,000.00	-	5,139.02	13,298.59	9,617.02	-	97,084.39
405	147240	Whiteside Plumbing Repairs	355,000.00	-	5,241.32	251,097.34	0.00	-	103,902.66
405	147250	Woodward: Comp Landscaping	4,850,000.00	30,981.00	81,688.41	81,688.41	765,846.32	-	4,002,465.27

Fund 405

2014 SALES TAX

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
405	147260	Cousins Park Improvements	1,975,000.00	-	-	-	-	-	1,975,000.00
405	147270	Carl Smith Improvements	185,000.00	-	5,224.57	14,837.35	7,388.98	-	162,773.67
405	147300	Berry - Pool Reconstruction	2,424,185.98	-	-	-	-	-	2,424,185.98
405	147400	Lacy - Pool	2,640,000.00	-	-	2,608,738.87	19,904.73	-	11,356.40
405	147500	Mcclure - Pool	4,725,000.00	-	16,963.11	4,487,848.77	10,372.73	-	226,778.50
405	147510	Whiteside Pool	1,350,000.00	-	6,416.98	1,342,501.62	0.00	-	7,498.38
405	147520	Playground Safety Surfaces	7,300,000.00	110,336.38	426,443.81	2,141,896.65	1,420,695.09	-	3,737,408.26
405	148100	Annual Economic Development	6,675,000.00	-	126,368.12	2,877,537.00	2,820,000.00	-	977,463.00
405	148110	Op Ser - Strategic Mobility	1,500,000.00	67,865.72	103,988.42	498,918.67	49,760.33	-	951,321.00
405	148120	Op Ser - Corridor & Small Ar	2,000,000.00	-	20,985.00	566,868.24	277.34	499,245.00	933,609.42
405	148130	Op Ser - Northland Str. Acq	5,000,000.00	480.15	77,297.10	503,316.05	13,699.46	-	4,482,984.49
405	148140	Retail and Res Development	4,000,000.00	-	-	3,998,400.00	-	-	1,600.00
405	148150	Pearl District Flood Control	5,000,000.00	13.00	27,847.95	2,707,651.13	122,847.86	-	2,169,501.01
405	148160	Charles Page Boulevard - Plan	445,000.00	-	-	-	-	-	445,000.00
405	148170	Eugene Field Redevelopment	10,900,000.00	55,591.10	3,170,842.99	4,166,932.56	4,178,926.45	-	2,554,140.99
405	148180	Route 66 Restrooms & Parking	550,000.00	-	(24,589.18)	524,394.54	1,016.28	-	24,589.18
405	149100	Transit Coach & Lift Match	14,750,000.00	-	619,936.80	8,552,272.80	-	-	6,197,727.20
405	149200	Peoria (Brt) Project	14,052,005.06	51.00	211.00	13,576,471.11	151,761.32	1,137.45	322,635.18
405	193400000Z	Zoo Playground	1,650,000.00	-	-	1,451,728.18	-	-	198,271.82
405	2059FR0046	Consulting Services - Match	70,500.00	-	23,913.00	27,488.00	-	-	43,012.00
405	2125X0001Z	Computer Aided Dispatch (CAD)	660,000.00	-	264,955.00	264,955.00	395,045.00	-	-
405	2132X0001Z	MTTA Parking Lot	947,994.94	-	-	-	-	-	947,994.94
405	2134B0001Z	Gilcrease Museum Facility Imp	3,323,517.89	-	-	-	-	-	3,323,517.89
			\$ 567,377,763.82	\$ 3,225,923.23	\$ 36,052,526.09	\$ 310,185,858.11	\$ 76,544,164.28	\$ 1,330,341.07	\$ 179,317,400.36

**2016 VISION TULSA ECONOMIC
DEVELOPMENT SALES FUND**

FUND 4000

(2016 LIMITED PURPOSE TEMPORARY SALES TAX FUND)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 4000 - 2016 VISION TULSA ECONOMIC DEVELOPMENT**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE EIGHT MONTHS ENDED FEBRUARY 28, 2021**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
Revenue					
Sales Tax	\$ 28,903,500.00	\$ 2,839,439.40	\$ 21,173,454.92	\$ 118,026,745.55	\$ 7,730,045.08
Donations					
Interest on Investments	659,000.00	26,519.26	240,010.19	1,812,839.25	418,989.81
Intergovernmental Revenue					
Federal, State & Local grants					
Transfers from other funds					
Miscellaneous Revenue					
Total Revenue	<u>29,562,500.00</u>	<u>2,865,958.66</u>	<u>21,413,465.11</u>	<u>119,839,584.80</u>	<u>8,149,034.89</u>
Expenditures					
Project Expenditures	<u>127,143,644.98</u>	<u>1,657,429.86</u>	<u>16,931,237.98</u>	<u>76,739,484.86</u>	<u>50,404,160.12</u>
Total Expenditures	<u>127,143,644.98</u>	<u>1,657,429.86</u>	<u>16,931,237.98</u>	<u>76,739,484.86</u>	<u>50,404,160.12</u>
Excess (Deficiency) of Revenue Over Expenditures			4,482,227.13	43,100,099.94	
Completed Projects Encumbrances			<u>22,368,645.28</u>	<u>22,368,645.28</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(17,886,418.15)	20,731,454.66	
June 30, 2018 Ending Fund Balance			38,496,944.74		
Prior year expenditures					
June 30, 2018 Encumbrances			<u>120,928.07</u>		
Adjusted Beginning Fund Balance			38,617,872.81		
Ending Fund Balance			<u>\$ 20,731,454.66</u>	<u>\$ 20,731,454.66</u>	

Fund 4000
2016 VISION ED CAPITAL PROJ

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4000	170000	Zink Lake and Related Improvem	21,690,000.00	-	167,031.83	178,355.40	18,036,408.39	3,475,236.21	0.00
4000	170010	Turkey Mountain Urban Wilderne	1,000,000.00	-	490,928.25	490,928.25	-	-	509,071.75
4000	170015	Levee Dist #12 Rehab (Match)	2,500,000.00	-	-	-	-	-	2,500,000.00
4000	170020	Trail E Bank 101 Cousins Park	2,000,000.00	-	-	69,165.48	19.59	-	1,930,814.93
4000	170025	23rd Jackson Redevelop Study	1,000,000.00	550.00	319,019.91	760,310.95	610.71	-	239,078.34
4000	170035	Cox Center & Dist Master Plan	14,100,000.00	-	-	14,100,000.00	(0.00)	-	(0.00)
4000	170060	BMX National Headquarters	5,801.19	-	-	-	-	-	5,801.19
4000	170065	South Mingo Corridor	1,000,000.00	-	-	1,935.00	-	-	998,065.00
4000	170080ENGR	CW & Rt 66 Beaut Rvst_ENGR	637,500.00	-	-	-	-	-	637,500.00
4000	170080MOED	CW & Rt 66 Beaut Rvst_MOED	3,550,000.00	-	100,000.00	1,325,000.00	750,000.00	-	1,475,000.00
4000	170080PLAN	CW & Rt 66 Beaut Rvst_PLAN	826,343.79	7,613.19	65,235.50	290,670.52	88,453.38	-	447,219.89
4000	170085	Peoria - Mohawk: Business Park	3,264,000.00	-	109.02	1,817,410.02	0.00	-	1,446,589.98
4000	170090	Public School Partnership	4,300,000.00	-	510,135.93	2,409,250.65	-	-	1,890,749.35
4000	170095	Community Health Connection	4,570,000.00	-	-	4,570,000.00	-	-	-
4000	170105	Discovery Lab Site	-	-	-	-	-	-	-
4000	170125	McCullough Park	1,000,000.00	-	-	-	-	-	1,000,000.00
4000	170145	Tulsa Arts Commission	600,000.00	-	282,087.00	282,087.00	17,917.00	-	299,996.00
4000	170155	PAC Improvement Master Plan	1,000,000.00	-	16,311.23	1,000,000.00	0.00	-	(0.00)
4000	170160	Transfer to TPFA 2017	64,100,000.00	1,649,266.67	13,502,933.35	48,008,841.95	-	-	16,091,158.05
			\$ 127,143,644.98	\$ 1,657,429.86	\$ 15,453,792.02	\$ 75,303,955.22	\$ 18,893,409.07	\$ 3,475,236.21	\$ 29,471,044.48

**2016 VISION ADVANCE FUNDED
REVENUE BOND FUND**

FUND 4001

(2016 ADVANCE FUNDED BOND FUND)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 4001 - 2017 VISION ECONOMIC DEVELOPMENT BOND FUND ISSUE 1**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE EIGHT MONTHS ENDED FEBRUARY 28, 2021**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
Revenue					
Bond Sale Receipts	\$	\$	\$	\$ 115,300,000.00	\$
Donations					
Miscellaneous Revenue				3,175,000.00	
Total Revenue				<u>118,475,000.00</u>	
Expenditures					
Project Expenditures	118,475,000.00	249,463.03	8,976,480.02	91,688,939.26	26,786,060.74
Total Expenditures	<u>118,475,000.00</u>	<u>249,463.03</u>	<u>8,976,480.02</u>	<u>91,688,939.26</u>	<u>26,786,060.74</u>
Excess (Deficiency) of Revenue Over Expenditures			(8,976,480.02)	26,786,060.74	
Completed Projects Encumbrances			<u>24,518,676.10</u>	<u>24,518,676.10</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(33,495,156.12)	2,267,384.64	
June 30, 2018 Ending Fund Balance			26,267,715.84		
Prior year expenditures					
June 30, 2018 Encumbrances			<u>9,494,824.92</u>		
Adjusted Beginning Fund Balance			<u>35,762,540.76</u>		
Ending Fund Balance	\$		<u><u>2,267,384.64</u></u>	\$	<u><u>2,267,384.64</u></u>

Fund 4001
2017 VISION ED ISSUE 1

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4001	170000	Zink Lake and Related Improve	24,425,000.00	-	87,441.34	5,492,431.16	15,128,605.05	3,803,963.79	0.00
4001	170030	Gilcrease Museum Expansion	1,000,000.00	-	202,328.58	1,000,000.00	-	-	0.00
4001	170035	Cox Center & Dist Master Plan	13,250,000.00	-	23,891.18	13,133,195.27	107,304.73	-	9,500.00
4001	170040	Tulsa Fairgrounds	26,325,000.00	-	-	26,325,000.00	0.00	-	(0.00)
4001	170045	Airport Infrastructure	9,100,000.00	6,154.63	937,098.19	6,374,495.06	2,725,504.94	-	0.00
4001	170055	Langston Health Complex Exp	1,800,000.00	-	28,727.35	1,800,000.00	0.00	-	(0.00)
4001	170060	BMX National Headquarters	1,350,000.00	-	-	1,350,000.00	(0.00)	-	0.00
4001	170065	South Mingo Corridor	11,000,000.00	214,528.88	1,768,330.21	6,393,177.01	2,672,301.75	-	1,934,521.24
4001	170070	Public School Safety First	5,000,000.00	28,779.52	1,226,562.05	4,718,958.96	0.00	-	281,041.04
4001	170095	Community Health Connection	5,405,000.00	-	-	5,405,000.00	-	-	-
4001	170100	Air National Guard Training Ce	9,400,000.00	-	166.95	9,358,127.35	2,129.86	-	39,742.79
4001	170110	N Peoria Conn 56-Mohawk	900,000.00	-	-	871,987.17	28,012.83	-	(0.00)
4001	170115	TCC Career Placement	5,320,000.00	-	-	5,320,000.00	0.00	-	(0.00)
4001	170120	UCAT Auth OSU Tulsa	-	-	-	-	-	-	-
4001	170130	Mohawk Sports Complex	3,500,000.00	-	-	3,468,440.74	31,559.26	-	(0.00)
4001	170135	Go Plan Priority Projects	-	-	-	-	-	-	-
4001	170140	Rt 66 Village Train Depot	400,000.00	-	110,765.66	380,706.11	19,293.89	-	0.00
4001	170150A	2017 Vision ED Issue Costs_1	300,000.00	-	-	226,339.38	-	-	73,660.62
			\$ 118,475,000.00	\$ 249,463.03	\$ 4,385,311.51	\$ 91,617,858.21	\$ 20,714,712.31	\$ 3,803,963.79	\$ 2,338,465.69

**2016 VISION ADVANCE FUNDED
REVENUE BOND FUND**

FUND 4003

(2016 ADVANCE FUNDED BOND FUND)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 4003 - 2017 VISION ECONOMIC DEVELOPMENT BOND FUND ISSUE 2**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE EIGHT MONTHS ENDED FEBRUARY 28, 2021**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
Revenue					
Bond Sale Receipts	\$	\$	\$	\$ 118,100,000.00	\$
Donations					
Miscellaneous Revenue					
Total Revenue				<u>118,100,000.00</u>	
Expenditures					
Project Expenditures	118,100,000.00	2,342,860.62	35,718,951.14	66,387,964.95	51,712,035.05
Total Expenditures	<u>118,100,000.00</u>	<u>2,342,860.62</u>	<u>35,718,951.14</u>	<u>66,387,964.95</u>	<u>51,712,035.05</u>
Excess (Deficiency) of Revenue Over Expenditures			(35,718,951.14)	51,712,035.05	
Completed Projects Encumbrances			<u>37,922,058.32</u>	<u>37,922,058.32</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(73,641,009.46)	13,789,976.73	
June 30, 2018 Ending Fund Balance			87,430,986.19		
Prior year expenditures					
June 30, 2018 Encumbrances					
Adjusted Beginning Fund Balance			<u>87,430,986.19</u>		
Ending Fund Balance			<u>\$ 13,789,976.73</u>	<u>\$ 13,789,976.73</u>	

Fund 4003
2017 VISION ED ISSUE 2

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4003	170000	Zink Lake and Related Improvem	16,885,000.00	-	992,330.28	992,330.28	13,446,559.01	-	2,446,110.71
4003	170005	Low-Water Dam and Pedestrian B	-	-	-	-	-	-	-
4003	170010	Turkey Mountain Urban Wilderne	5,000,000.00	-	4,951,568.75	5,000,000.00	-	-	-
4003	170030	Gilcrease Museum Expansion	6,000,000.00	3,789.74	1,501,053.67	2,656,597.02	3,343,402.98	-	0.00
4003	170035	Cox Center & Dist Master Plan	27,650,000.00	98,764.39	5,322,915.07	26,696,126.86	705,836.58	-	248,036.56
4003	170040	Tulsa Fairgrounds	3,675,000.00	-	1,170.40	2,151,454.28	1,519,216.12	-	4,329.60
4003	170045	Airport Infrastructure	9,100,000.00	-	-	-	9,100,000.00	-	-
4003	170050	Tulsa Zoo & Living Museum	3,000,000.00	69,107.00	1,194,165.66	1,274,064.56	689,467.17	-	1,036,468.27
4003	170055	Langston Health Complex Exp	11,450,000.00	-	11,450,000.00	11,450,000.00	-	-	-
4003	170060	BMX National Headquarters	13,650,000.00	1,632,890.82	5,693,426.26	6,565,089.22	6,846,030.03	-	238,880.75
4003	170070	Public School Safety First	4,750,000.00	-	348,208.38	3,887,487.72	405,495.28	-	457,017.00
4003	170085	Peoria - Mohawk: Business Park	2,500,000.00	-	387,323.31	2,112,020.84	387,979.16	-	0.00
4003	170105	Discovery Lab Site	8,000,000.00	-	550.00	8,750.00	-	-	7,991,250.00
4003	170110	N Peoria Conn 56-Mohawk	3,000,000.00	-	7,822.00	1,761,075.06	0.00	-	1,238,924.94
4003	170125	McCullough Park	540,000.00	22,652.37	211,744.29	419,015.80	120,984.20	-	(0.00)
4003	170140	Rt 66 Village Train Depot	2,600,000.00	515,656.30	1,102,432.21	1,147,782.22	1,357,087.79	-	95,129.99
4003	170150B	2017 Vision ED Issue Bond Cost	300,000.00	-	-	266,171.09	-	-	33,828.91
			\$ 118,100,000.00	\$ 2,342,860.62	\$ 33,164,710.28	\$ 66,387,964.95	\$ 37,922,058.32	\$ -	\$ 13,789,976.73

**2016 VISION ADVANCE FUNDED
REVENUE BOND FUND**

FUND 4004

(2016 ADVANCE FUNDED BOND FUND)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 4004 - 2017 VISION ECONOMIC DEVELOPMENT BOND FUND ISSUE 3**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE EIGHT MONTHS ENDED FEBRUARY 28, 2021**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
Revenue					
Bond Sale Receipts	\$	\$	\$	\$ 114,025,000.00	\$
Donations					
Miscellaneous Revenue					
Total Revenue				<u>114,025,000.00</u>	
Expenditures					
Project Expenditures	114,025,000.00	857,597.79	8,844,925.60	9,383,348.11	104,641,651.89
Total Expenditures	<u>114,025,000.00</u>	<u>857,597.79</u>	<u>8,844,925.60</u>	<u>9,383,348.11</u>	<u>104,641,651.89</u>
Excess (Deficiency) of Revenue Over Expenditures			(8,844,925.60)	104,641,651.89	
Completed Projects Encumbrances			<u>51,914,906.25</u>	<u>51,914,906.25</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(60,759,831.85)	52,726,745.64	
June 30, 2018 Ending Fund Balance			113,486,577.49		
Prior year expenditures					
June 30, 2018 Encumbrances					
Adjusted Beginning Fund Balance			<u>113,486,577.49</u>		
Ending Fund Balance			<u>\$ 52,726,745.64</u>	<u>\$ 52,726,745.64</u>	

Fund 4004
2017 VISION ED ISSUE 3

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4004	170005	Low-Water Dam and Pedestrian B	2,800,000.00	47.05	47.05	47.05	-	-	2,799,952.95
4004	170030	Gilcrease Museum Expansion	58,000,000.00	23,704.00	2,106,243.64	2,106,243.64	45,818,428.89	-	10,075,327.47
4004	170045	Airport Infrastructure	9,100,000.00	317,572.40	317,572.40	317,572.40	1,312,414.92	-	7,470,012.68
4004	170050	Tulsa Zoo & Living Museum	22,000,000.00	-	-	-	30,000.00	-	21,970,000.00
4004	170055	Langston Health Complex Exp	3,000,000.00	-	3,000,000.00	3,000,000.00	-	-	-
4004	170060	BMX National Headquarters	3,600,000.00	-	-	-	3,600,000.00	-	-
4004	170065	South Mingo Corridor	3,000,000.00	-	-	-	-	-	3,000,000.00
4004	170070	Public School Safety First	4,750,000.00	-	-	-	-	-	4,750,000.00
4004	170080MOED	CW & Rt 66 Beaut Reinvestment_	150,000.00	-	-	-	-	-	150,000.00
4004	170085	Peoria - Mohawk Business Park	4,200,000.00	255,422.74	848,198.24	848,198.24	888,602.26	-	2,463,199.50
4004	170135	Go Plan Priority Projects	3,125,000.00	260,851.60	2,572,864.27	2,859,539.82	265,460.18	-	0.00
4004	170150C	2017 Vision ED Issue Bond Cost	300,000.00	-	-	251,746.96	-	-	48,253.04
			\$ 114,025,000.00	\$ 857,597.79	\$ 8,844,925.60	\$ 9,383,348.11	\$ 51,914,906.25	\$ -	\$ 52,726,745.64

2008 GO BOND FUNDS

FUNDS 4260~4266 COMBINED

(2008 GENERAL OBLIGATION BOND FUNDS)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 4260-4266 - 2008 GO BOND FUNDS**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE EIGHT MONTHS ENDED FEBRUARY 28, 2021**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
Revenue					
Bond Sale Receipts	\$	\$	\$	\$ 285,000,000.00	\$
Donations					
Miscellaneous Revenue					
Total Revenue				<u>285,000,000.00</u>	
Expenditures					
Project Expenditures	230,054,936.55	405,675.73	1,979,544.05	209,104,278.17	20,950,658.38
Total Expenditures	<u>230,054,936.55</u>	<u>405,675.73</u>	<u>1,979,544.05</u>	<u>209,104,278.17</u>	<u>20,950,658.38</u>
Excess (Deficiency) of Revenue Over Expenditures			(1,979,544.05)	75,895,721.83	
Completed Projects				54,945,063.45	
Encumbrances			<u>11,718,557.90</u>	<u>11,718,557.90</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(13,698,101.95)	9,232,100.48	
June 30, 2018 Ending Fund Balance			22,930,202.43		
Prior year expenditures					
June 30, 2018 Encumbrances					
Adjusted Beginning Fund Balance			<u>22,930,202.43</u>		
Ending Fund Balance			<u>\$ 9,232,100.48</u>	<u>\$ 9,232,100.48</u>	

Fund

426

2008 GO BOND PROGRAM

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4261	104003	61st S-33rd W Ave to Union	232,000.00	-	-	72,145.64	159,854.36	-	-
4263	104003	61st S-33rd W Ave to Union	1,324,527.90	-	-	1,324,527.90	-	-	-
4261	104004	71st S-Hwy 75 to Arkansas Rive	343,000.00	-	-	343,000.00	-	-	0.00
4263	104004	71st S-Hwy 75 to Arkansas Rive	3,617,048.74	-	-	3,617,048.74	-	-	-
4263	104005	81ST S-YALE AVE TO SHERIDAN	923,488.36	-	-	923,488.36	-	-	-
4260	104006	101St S-Harvard Ave To Yale	58,155.21	-	-	58,155.21	-	-	-
4261	104006	101St S-Harvard Ave To Yale	1,066,494.63	-	-	1,066,494.63	0.00	-	(0.00)
4262	104006	101St S-Harvard Ave To Yale	1,131,141.85	-	-	1,131,141.85	(0.00)	-	0.00
4263	104006	101St S-Harvard Ave To Yale	3,074,799.31	-	-	2,446,327.87	(0.00)	-	628,471.44
4261	104008	129th E Ave-21st S to 11th	252,739.33	-	-	252,739.33	-	-	-
4263	104008	129th E Ave-21st S to 11th	772,254.96	-	-	772,254.96	-	-	-
4261	104009	Citywide-Arterial Rehab&Cons	150,000.00	-	-	150,000.00	-	-	-
4263	104009	Citywide-Arterial Rehab&Cons	25,000.00	-	-	25,000.00	-	-	-
4264	104009	Citywide-Arterial Rehab&Cons	60,000.00	-	-	60,000.00	-	-	-
4265	104009	Citywide-Arterial Rehab&Cons	10,000.00	-	-	10,000.00	-	-	-
4261	104010	Citywide-Arterial Sidewalk R	120,000.00	-	-	120,000.00	-	-	-
4262	104010	Citywide-Arterial Sidewalk R	40,000.00	-	-	40,000.00	-	-	-
4263	104010	Citywide-Arterial Sidewalk R	80,000.00	-	-	80,000.00	-	-	-
4264	104010	Citywide-Arterial Sidewalk R	80,000.00	-	-	80,000.00	-	-	-
4265	104010	Citywide-Arterial Sidewalk R	80,000.00	-	-	80,000.00	-	-	-
4261	104011	Citywide - Trails	365,000.00	-	-	365,000.00	-	-	(0.00)
4262	104011	Citywide - Trails	100,000.00	-	-	100,000.00	-	-	-
4263	104011	Citywide - Trails	250,000.00	-	-	240,572.63	-	-	9,427.37
4264	104011	Citywide - Trails	133,000.00	-	-	133,000.00	-	-	-
4265	104011	Citywide - Trails	152,000.00	-	-	152,000.00	-	-	-
4261	104012	Citywide-Railroad Crossings	125,000.00	-	2,604.20	125,000.00	-	-	-
4262	104012	Citywide-Railroad Crossings	50,000.00	-	-	50,000.00	-	-	-
4263	104012	Citywide-Railroad Crossings	75,000.00	-	-	75,000.00	-	-	-
4264	104012	Citywide-Railroad Crossings	125,000.00	-	403.65	125,000.00	-	-	-
4266	104012	Citywide-Railroad Crossings	125,000.00	-	476.22	125,000.00	-	-	0.00
4261	104013	Citywide - Local Match	2,996,000.00	-	-	2,813,486.95	182,513.05	-	(0.00)
4262	104013	Citywide - Local Match	1,000.00	-	-	1,000.00	-	-	-
4263	104013	Citywide - Local Match	1,000.00	-	-	1,000.00	-	-	-
4264	104013	Citywide - Local Match	1,000.00	-	-	1,000.00	-	-	-
4265	104013	Citywide - Local Match	1,000.00	-	-	1,000.00	-	-	-
4261	104014	Citywide General Eng/Test/In	47,140.00	-	-	47,140.00	-	-	-
4262	104014	Citywide General Eng/Test/In	33,113.00	-	-	33,113.00	-	-	-
4263	104014	Citywide General Eng/Test/In	30,887.00	-	-	15,491.47	15,395.53	-	(0.00)
4264	104014	Citywide General Eng/Test/In	25,000.00	-	-	25,000.00	-	-	0.00
4265	104014	Citywide General Eng/Test/In	26,000.00	-	2,988.26	20,645.90	(0.00)	-	5,354.10
4266	104014	Citywide General Eng/Test/In	2,000.00	-	-	2,000.00	-	-	-
4260	104015	Citywide Nonarterial Reh&Re	1,500,000.00	-	-	-	-	-	1,500,000.00
4261	104015	Citywide Nonarterial Reh&Re	80,000.00	-	-	80,000.00	-	-	-
4262	104015	Citywide Nonarterial Reh&Re	1,180,000.00	-	-	1,180,000.00	-	-	-

Fund

426

2008 GO BOND PROGRAM

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4263	104015	Citywide Nonarterial Reh&Re	20,000.00	-	-	20,000.00	-	-	-
4264	104015	Citywide Nonarterial Reh&Re	90,000.00	-	-	89,999.00	-	-	1.00
4261	104016	Citywide Nonarterial Sidewlk	60,000.00	-	-	60,000.00	-	-	-
4262	104016	Citywide Nonarterial Sidewlk	60,000.00	-	-	60,000.00	-	-	-
4263	104016	Citywide Nonarterial Sidewlk	60,000.00	-	-	60,000.00	-	-	-
4264	104016	Citywide Nonarterial Sidewlk	90,000.00	-	-	90,000.00	-	-	-
4265	104016	Citywide Nonarterial Sidewlk	30,000.00	-	-	4,492.22	-	-	25,507.78
4260	104018	129th E Ave Admiral to Pine	1,289,339.05	-	-	1,289,339.05	0.00	-	(0.00)
4261	104018	129th E Ave Admiral to Pine	459,443.82	-	-	459,443.82	-	-	-
4263	104018	129th E Ave Admiral to Pine	517,997.83	-	-	517,997.83	-	-	-
4260	104020	Citywide-Arterial Rt&Pv Main	693,869.00	-	-	693,869.00	-	-	-
4261	104020	Citywide-Arterial Rt&Pv Main	3,000,315.00	-	-	3,000,315.00	(0.00)	-	0.00
4262	104023	Lewis Ave 21st to 11th	-	-	-	-	-	-	-
4261	104024	Memorial Ave 11Th To Admiral	-	-	-	-	-	-	-
4262	104024	Memorial Ave 11Th To Admiral	-	-	-	-	-	-	-
4261	104032	River Road - 111th to 101st	665,320.12	-	-	665,320.12	-	-	-
4263	104032	River Road - 111th to 101st	219,509.96	-	-	219,509.96	-	-	-
4261	104033	61St & Memorial Intersection	817,595.75	-	-	817,595.75	-	-	-
4260	104035	Pine St 129th E Ave Intersec	883,614.80	-	-	883,614.80	(0.00)	-	(0.00)
4262	104035	Pine St 129th E Ave Intersec	200,000.00	-	-	200,000.00	-	-	-
4261	104036	Harvard Ave - 61St S To 51St	4,124,138.14	-	-	4,124,138.14	-	-	-
4261	104037	Apache St-Yale To Sheridan	395,997.45	-	-	395,997.45	-	-	-
4261	104038	Cinci/Detroit-l244 To Jasper	710,000.00	-	-	710,000.00	-	-	-
4261	104039	Harvard Ave-Admiral To Pine	426,655.29	-	-	426,655.29	-	-	-
4261	104040	Lewis Ave-36Th St N To 46Th	450,400.19	-	-	450,400.19	-	-	(0.00)
4261	104041	Memorial Dr-21St St S To 11Th	1,067,161.62	-	529.42	1,066,589.14	572.48	-	0.00
4261	104043	PINE ST-YALE TO SHERIDAN RD	411,176.00	-	-	398,067.35	13,108.65	-	0.00
4262	104045	River Rd-111Th St S To 101St	297,000.00	-	-	297,000.00	-	-	-
4262	104046	Riverside Dr-41St St S To 31	472,541.00	-	-	472,541.00	-	-	-
4262	104047	Union Ave-51St St S To 41St	700,000.00	-	-	700,000.00	-	-	-
4262	104049	21st St S Utica Ave Intersect	200,000.00	-	-	200,000.00	-	-	-
4262	104050	31St St S-Harvard Intersect	300,000.00	-	-	300,000.00	-	-	-
4262	104051	36TH ST N-LEWIS AVE INTERSEC	248,140.69	-	-	248,140.69	-	-	-
4262	104052	41St St S-Harvard Intersect	413,881.00	-	-	413,881.00	-	-	-
4262	104053	Pine St- Yale Ave Intersect	500,000.00	-	259,932.84	500,000.00	-	-	-
4262	104054	Citywide-Gen Engr/Test/Inspe	451,860.00	-	-	451,860.00	0.00	-	(0.00)
4264	104060	Bridge 160-5400 E. Apache St	560,000.00	-	-	560,000.00	-	-	-
4265	104060	Bridge 160-5400 E. Apache St	2,884,992.49	-	-	2,884,992.49	-	-	0.00
4261	104061	Bridge 163-100 S Boulder Ave	730,000.00	-	-	730,000.00	-	-	-
4262	104061	Bridge 163-100 S Boulder Ave	6,554,170.84	-	-	6,554,170.84	-	-	-
4264	104062	Bridge 228-3200 S. Riverside	280,000.00	-	-	280,000.00	-	-	-
4265	104062	Bridge 228-3200 S. Riverside	8,476.00	-	-	8,476.00	-	-	(0.00)
4264	104063	Bridge 234-4200 S. Union Ave	315,516.00	-	-	315,516.00	0.00	-	(0.00)
4265	104063	Bridge 234-4200 S. Union Ave	181,496.27	-	-	181,496.27	-	-	0.00

Fund

426

2008 GO BOND PROGRAM

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4264	104064	Bridge 290-200 N 49th W Ave	210,000.00	-	-	210,000.00	-	-	-
4266	104064	Bridge 290-200 N 49th W Ave	1,477,083.90	-	-	1,477,083.90	-	-	(0.00)
4261	104065	Bridge 318A 10100 S 72nd E A	1,000,000.00	-	-	1,000,000.00	-	-	-
4262	104065	Bridge 318A 10100 S 72nd E A	2,837,026.52	-	-	2,837,026.52	-	-	(0.00)
4261	104102	Maintenance Zone 1001 (Sw)	251,628.29	-	-	251,628.29	-	-	-
4263	104102	Maintenance Zone 1001 (Sw)	1,772,604.35	-	-	1,772,604.35	-	-	-
4263	104106	Maintenance Zone 1006	349,872.76	-	-	349,872.76	-	-	-
4264	104106	Maintenance Zone 1006	2,805,465.62	-	-	2,805,465.62	-	-	-
4263	104107	Maintenance Zone 1007	404,424.66	404,424.66	404,424.66	404,424.66	-	-	-
4264	104107	Maintenance Zone 1007	774,971.00	690.00	139,731.89	770,626.57	4,344.43	-	(0.00)
4266	104107	Maintenance Zone 1007	6,971,000.00	-	-	6,971,000.00	0.00	-	0.00
4263	104171	Maintenance Zone 1071	231,965.00	-	-	223,482.91	8,482.09	-	(0.00)
4264	104171	Maintenance Zone 1071	1,438,711.50	-	-	1,438,711.50	-	-	-
4263	104230	Maintenance Zone 2130	757,539.81	-	-	757,539.81	-	-	-
4264	104231	Maintenance Zone 2131	245,563.00	-	-	241,015.56	4,547.44	-	0.00
4265	104231	Maintenance Zone 2131	2,210,000.00	-	-	2,210,000.00	-	-	-
4260	104266	Maintenance Zone 2065 C	457,291.81	-	-	-	-	-	457,291.81
4261	104266	Maintenance Zone 2065 C	336,957.69	-	-	-	-	-	336,957.69
4262	104266	Maintenance Zone 2065 C	545,992.63	-	-	-	-	-	545,992.63
4263	104266	Maintenance Zone 2065 C	599,734.88	-	-	543,660.00	-	-	56,074.88
4264	104266	Maintenance Zone 2065 C	4,911,619.99	561.07	561.07	4,884,730.26	23,206.74	-	3,682.99
4261	104303	Maintenance Zone 3003	1,715,018.19	-	-	1,715,018.19	-	-	-
4264	104307	Maintenance Zone 3007	181,593.20	-	17,140.80	198,734.00	-	-	(17,140.80)
4265	104307	Maintenance Zone 3007	1,503,547.42	-	227,329.58	1,730,877.00	-	-	(227,329.58)
4264	104309	Maintenance Zone 3009	361,880.46	-	-	361,880.46	-	-	-
4265	104309	Maintenance Zone 3009	3,302,497.13	-	-	3,302,497.13	-	-	-
4263	104310	Maintenance Zone 3010	3,825,661.04	-	-	3,825,661.04	-	-	-
4263	104311	Maintenance Zone 3011	113,466.78	-	-	113,466.78	-	-	-
4264	104311	Maintenance Zone 3011	564,833.33	-	-	564,833.33	-	-	-
4263	104317	Maintenance Zone 3017	249,959.46	-	-	241,598.61	-	-	8,360.85
4264	104317	Maintenance Zone 3017	1,430,502.09	-	-	1,430,502.09	-	-	(0.00)
4264	104413	Maintenance Zone 4013	616,845.00	-	-	596,968.95	19,876.05	-	0.00
4265	104413	Maintenance Zone 4013	4,128,283.27	-	-	4,128,283.27	-	-	(0.00)
4263	104415	Maintenance Zone 4015	383,418.92	-	-	383,418.92	-	-	(0.00)
4264	104415	Maintenance Zone 4015	2,653,769.73	-	-	2,653,769.73	-	-	-
4261	104416	Maintenance Zone 4016	1,012,270.00	-	-	1,012,270.00	-	-	-
4262	104416	Maintenance Zone 4016	6,292,219.05	-	-	6,292,219.05	-	-	(0.00)
4261	104467	Maintenance Zone 4067 (A)	289,771.38	-	-	289,771.38	-	-	-
4263	104467	Maintenance Zone 4067 (A)	2,710,368.84	-	-	2,710,368.84	-	-	-
4264	104525	Maintenance Zone 5025	5,142,414.45	-	-	5,027,770.95	(0.00)	-	114,643.50
4261	104533	Maintenance Zone 5033	340,572.92	-	-	340,572.92	-	-	-
4263	104533	Maintenance Zone 5033	2,187,078.89	-	-	2,187,078.89	-	-	(0.00)
4264	104534	Maintenance Zone 5034	549,761.20	-	-	549,761.20	-	-	(0.00)
4265	104534	Maintenance Zone 5034	4,985,771.51	-	-	4,985,771.51	-	-	-

Fund

426

2008 GO BOND PROGRAM

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4261	104541	Maintenance Zone 5041	676,125.51	-	-	676,125.51	-	-	-
4262	104541	Maintenance Zone 5041	4,778,618.79	-	-	4,778,618.79	-	-	-
4263	104619	Maintenance Zone 6019	1,769,054.10	-	-	1,769,054.10	-	-	-
4262	104628	Maintenance Zone 6028	6,365,510.34	-	-	6,365,510.34	-	-	-
4263	104642	Maintenance Zone 6042	368,304.86	-	-	368,304.86	-	-	-
4264	104642	Maintenance Zone 6042	3,180,683.21	-	-	3,180,683.21	-	-	-
4264	104651	Maintenance Zone 6151	508,498.00	-	-	508,498.00	-	-	0.00
4266	104651	Maintenance Zone 6151	4,582,000.00	-	-	4,582,000.00	-	-	-
4264	104747	Maintenance Zone 7046	199,990.98	-	-	199,990.98	-	-	-
4265	104747	Maintenance Zone 7046	2,085,970.73	-	-	2,085,970.73	-	-	-
4261	104753	Maintenance Zone 7053	902,005.68	-	-	902,005.68	-	-	-
4262	104753	Maintenance Zone 7053	5,864,985.14	-	-	5,864,985.14	-	-	0.00
4263	104759	Maintenance Zone 7059	199,994.85	-	-	199,994.85	-	-	-
4264	104759	Maintenance Zone 7059	1,980,033.02	-	-	1,980,033.02	-	-	-
4261	104760	Maintenance Zone 7060	1,404,314.01	-	-	1,404,314.01	-	-	-
4261	104803	Maintenance Zone 8103	279,000.00	-	-	279,000.00	-	-	-
4263	104803	Maintenance Zone 8103	3,604,263.82	-	-	3,604,263.82	-	-	(0.00)
4264	104807	Maintenance Zone 8107	214,651.00	-	-	214,651.00	-	-	-
4265	104807	Maintenance Zone 8107	1,651,085.82	-	-	1,651,085.82	-	-	-
4263	104813	Maintenance Zone 8113	292,626.95	-	-	292,626.95	-	-	-
4264	104813	Maintenance Zone 8113	3,158,681.59	-	-	3,158,681.59	-	-	-
4261	104863	Maintenance Zone 8063	514,195.00	-	-	514,195.00	-	-	-
4262	104863	Maintenance Zone 8063	4,230,579.00	-	-	4,230,579.00	-	-	-
4263	104928	Maintenance Zone 9029 (W)	713,226.00	-	-	713,226.00	-	-	-
4264	104928	Maintenance Zone 9029 (W)	7,388,380.56	-	-	7,388,380.56	-	-	(0.00)
4261	104930	Maintenance Zone 9030	354,516.00	-	-	354,516.00	-	-	-
4262	104930	Maintenance Zone 9030	3,032,690.36	-	-	3,032,690.36	-	-	-
4264	104931	Maintenance Zone 9031	13,500.00	-	-	13,500.00	-	-	-
4265	104931	Maintenance Zone 9031	135,355.68	-	-	135,355.68	-	-	-
4261	104936	Maintenance Zone 9036	278,000.00	-	-	278,000.00	-	-	-
4263	104936	Maintenance Zone 9036	2,082,756.60	-	-	2,082,756.60	-	-	-
4264	104937	Maintenance Zone 9037	85,951.95	-	-	85,951.95	-	-	-
4266	104937	Maintenance Zone 9037	901,000.00	-	-	901,000.00	-	-	-
4264	104944	Maintenance Zone 9044	50,000.00	-	8,168.17	50,000.00	-	-	-
4266	104944	Maintenance Zone 9044	529,000.00	-	529,000.00	529,000.00	-	-	-
4261	134001	5th Street Frisco to Denver	52,260.67	-	-	52,260.67	-	-	-
4262	134001	5th Street Frisco to Denver	2,397,671.00	-	-	2,397,671.00	-	-	(0.00)
4263	134001	5th Street Frisco to Denver	3,817,935.33	-	-	3,817,935.33	-	-	-
4264	134001	5th Street Frisco to Denver	468,355.03	-	-	468,355.03	-	-	0.00
4265	134001	5th Street Frisco to Denver	485,772.10	-	-	485,772.10	-	-	-
4260	144022	Art/NonArt Routine & Preventio	3,195.19	-	-	3,195.19	-	-	-
4261	144022	Art/NonArt Routine & Preventio	1,938,060.85	-	-	1,938,059.85	-	-	1.00
4262	144022	Art/NonArt Routine & Preventio	1,179,441.50	-	-	1,179,441.50	-	-	-
4263	144022	Art/NonArt Routine & Preventio	1,129,302.46	-	-	1,129,250.93	0.00	-	51.53

Fund

426

2008 GO BOND PROGRAM

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4260	144023	CW - Arterial Rt & Pv Main	19,903.44	-	-	19,903.44	-	-	(0.00)
4261	144023	CW - Arterial Rt & Pv Main	821,260.42	-	-	821,260.42	0.00	-	0.00
4262	144023	CW - Arterial Rt & Pv Main	2,589,129.91	-	-	2,589,129.91	(0.00)	-	0.00
4263	144023	CW - Arterial Rt & Pv Main	3,494,979.57	-	-	3,494,979.57	-	-	(0.00)
4264	144023	CW - Arterial Rt & Pv Main	1,928,632.59	-	-	1,928,632.59	-	-	-
4265	144063	Bridge Replacement And Rehab	1,787,083.90	-	-	-	-	-	1,787,083.90
4266	144063	Bridge Replacement And Rehab	412,916.10	-	-	-	-	-	412,916.10
4263	144101	Yale Ave 81st - 91st Wdn	1,923,304.15	-	-	-	1,923,304.15	-	-
4264	144101	Yale Ave 81st - 91st Wdn	1,967,195.50	-	-	-	1,967,195.50	-	-
4265	144101	Yale Ave 81st - 91st Wdn	6,996,157.43	-	-	-	6,996,157.43	-	-
4265	144467	Maintenance Zone 4067	1,336,220.25	-	-	-	-	-	1,336,220.25
4263	144642	Maintenance Zone 6142	400,000.00	-	-	-	400,000.00	-	-
4262	147200	RP - Pedestrian Bridge Imp	978,381.71	-	-	-	-	-	978,381.71
4263	147200	RP - Pedestrian Bridge Imp	1,270,150.33	-	-	-	-	-	1,270,150.33
4263	1040316324	Admiral & Memorial Intersect	445,721.30	-	-	445,721.30	-	-	-
			\$ 230,054,936.55	\$ 405,675.73	\$ 1,593,290.76	\$ 209,104,278.17	\$ 11,718,557.90	\$ -	\$ 9,232,100.48

2014 GO BOND FUNDS

FUND 4270~4273 COMBINED

(2014 GENERAL OBLIGATION BOND FUNDS)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 4270-4274 - 2008 GO BOND FUNDS**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE EIGHT MONTHS ENDED FEBRUARY 28, 2021**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<u>Revenue</u>					
Bond Sale Receipts	\$	\$	\$	\$ 277,500,000.00	\$
Donations					
Miscellaneous Revenue					
Total Revenue				<u>277,500,000.00</u>	
<u>Expenditures</u>					
Project Expenditures	<u>277,500,000.00</u>	<u>1,800,702.02</u>	<u>24,108,873.66</u>	<u>165,735,481.65</u>	<u>111,764,518.35</u>
Total Expenditures	<u>277,500,000.00</u>	<u>1,800,702.02</u>	<u>24,108,873.66</u>	<u>165,735,481.65</u>	<u>111,764,518.35</u>
Excess (Deficiency) of Revenue Over Expenditures			(24,108,873.66)	111,764,518.35	
Completed Projects Encumbrances			<u>37,399,847.79</u>	<u>37,399,847.79</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(61,508,721.45)	74,364,670.56	
June 30, 2018 Ending Fund Balance			135,863,399.89		
Prior year expenditures					
June 30, 2018 Encumbrances			<u>9,992.12</u>		
Adjusted Beginning Fund Balance			<u>135,873,392.01</u>		
Ending Fund Balance			<u>\$ 74,364,670.56</u>	<u>\$ 74,364,670.56</u>	

Fund

427

2014 GO BOND PROGRAM

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4270	144000	Bond Issuance Costs	20,000.00	-	-	20,000.00	-	-	-
4271	144000	Bond Issuance Costs	80,000.00	-	-	79,999.78	-	-	0.22
4272	144000	Bond Issuance Costs	150,000.00	-	-	150,000.00	-	-	-
4273	144000	Bond Issuance Costs	150,000.00	-	-	150,000.00	-	-	-
4274	144000	Bond Issuance Costs	132,000.00	-	-	-	-	-	132,000.00
4270	144015	Citywide Nonarterial Reh&Re	200,000.00	-	-	200,000.00	-	-	-
4271	144015	Citywide Nonarterial Reh&Re	400,000.00	-	-	400,000.00	-	-	-
4272	144015	Citywide Nonarterial Reh&Re	540,000.00	-	-	540,000.00	-	-	-
4273	144015	Citywide Nonarterial Reh&Re	539,950.00	-	127,723.29	177,630.75	-	-	362,319.25
4274	144015	Citywide Nonarterial Reh&Re	1,320,000.00	-	-	-	-	-	1,320,000.00
4271	144016	Citywide Non-Art Sidewalks	100,000.00	-	-	100,000.00	-	-	-
4272	144016	Citywide Non-Art Sidewalks	300,000.00	-	89,936.20	273,467.83	-	-	26,532.17
4273	144016	Citywide Non-Art Sidewalks	100,000.00	-	-	100,000.00	-	-	-
4270	144020	Citywide-Arterial Rt&Pv Main	355,000.00	-	-	355,000.00	-	-	-
4271	144020	Citywide-Arterial Rt&Pv Main	3,745,000.00	-	-	3,745,000.00	(0.00)	-	0.00
4272	144020	Citywide-Arterial Rt&Pv Main	6,260,000.00	212.75	1,241,867.91	5,214,085.64	480,484.32	-	565,430.04
4273	144020	Citywide-Arterial Rt&Pv Main	9,140,000.00	-	298,569.18	7,979,246.50	1,160,753.49	-	0.01
4270	144021	Citywide-Nonarterial Rt&Pv M	1,973,927.51	-	174,801.42	1,000,819.74	-	-	973,107.77
4271	144021	Citywide-Nonarterial Rt&Pv M	9,000,000.00	6,769.06	940,673.02	8,544,070.00	455,930.00	-	(0.00)
4272	144021	Citywide-Nonarterial Rt&Pv M	16,880,000.00	515,684.59	3,482,714.40	14,335,941.49	2,381,495.13	-	162,563.38
4273	144021	Citywide-Nonarterial Rt&Pv M	22,000,000.00	29,619.97	858,052.83	20,493,180.57	523,651.99	-	983,167.44
4270	144060	Bridge189 - 4700 N. Iroquois	20,000.00	-	7,228.32	11,321.19	-	-	8,678.81
4271	144060	Bridge189 - 4700 N. Iroquois	180,000.00	-	-	180,000.00	-	-	-
4270	144061	Bridge298 - 2100 E. 61St St	100,000.00	-	-	66,650.26	-	-	33,349.74
4271	144061	Bridge298 - 2100 E. 61St St	900,000.00	-	-	543,739.50	-	-	356,260.50
4270	144062	Bridge323B - 12000 E. 21St	10,000.00	-	-	10,000.00	-	-	-
4272	144062	Bridge323B - 12000 E. 21St	50,000.00	-	50,000.00	50,000.00	-	-	-
4270	144093	Citywide Matching Funds	250,000.00	-	-	250,000.00	-	-	-
4271	144093	Citywide Matching Funds	450,000.00	-	-	450,000.00	-	-	-
4272	144093	Citywide Matching Funds	650,000.00	-	-	650,000.00	(0.00)	-	0.00
4273	144093	Citywide Matching Funds	1,753,170.00	15,000.00	735,983.93	1,322,651.32	193,694.93	-	236,823.75
4271	144094	ODOT Rehab & Replacement	1,640,000.00	-	-	1,620,383.08	9,627.80	-	9,989.12
4272	144094	ODOT Rehab & Replacement	1,640,000.00	-	-	1,640,000.00	(0.00)	-	0.00
4273	144094	ODOT Rehab & Replacement	1,640,000.00	-	-	1,640,000.00	(0.00)	-	(0.00)
4274	144094	ODOT Rehab & Replacement	3,280,000.00	-	129,140.50	129,140.50	-	-	3,150,859.50
4270	144106	Maintenance Zone 1006	400,000.00	-	1,588.54	369,685.14	30,314.86	-	(0.00)
4272	144106	Maintenance Zone 1006	2,210,000.00	-	166,466.44	2,008,802.62	96,058.96	-	105,138.42
4274	144106	Maintenance Zone 1006	1,340,000.00	-	-	-	-	-	1,340,000.00
4270	144107	Maintenance Zone 1007	55,000.00	-	2,260.00	55,000.00	-	-	-
4271	144107	Maintenance Zone 1007	475,000.00	-	-	475,000.00	-	-	-
4271	144110	Citywide-Arterial Sidewalks	300,000.00	-	-	300,000.00	-	-	-
4272	144110	Citywide-Arterial Sidewalks	900,000.00	1,556.87	75,651.47	900,000.00	(0.00)	-	(0.00)
4273	144110	Citywide-Arterial Sidewalks	300,000.00	-	-	300,000.00	(0.00)	-	0.00
4271	144111	Maintenance Zone 1001	830,000.00	-	-	536,387.82	293,612.18	-	0.00

Fund

427

2014 GO BOND PROGRAM

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4273	144111	Maintenance Zone 1001	-	-	-	-	-	-	-
4274	144111	Maintenance Zone 1001	7,445,000.00	-	-	-	7,101,598.47	-	343,401.53
4270	144153	Maintenance Zone 1153	410,000.00	-	-	349,257.75	3,913.97	-	56,828.28
4272	144153	Maintenance Zone 1153	-	-	-	-	-	-	-
4274	144153	Maintenance Zone 1153	1,243,000.00	-	-	-	-	-	1,243,000.00
4270	144157	Maintenance Zone 1157	419,944.69	-	-	419,944.69	-	-	-
4272	144157	Maintenance Zone 1157	3,635,000.00	-	-	3,192,879.00	(0.00)	-	442,121.00
4271	144158	Maintenance Zone 1157	260,000.00	-	-	211,448.65	8,194.81	-	40,356.54
4273	144158	Maintenance Zone 1157	2,275,000.00	-	4,980.06	2,107,199.83	-	-	167,800.17
4272	144168	Maintenance Zone 1068	400,000.00	-	31,974.79	309,525.83	67,841.98	-	22,632.19
4270	144173	Maintenance Zone 1073	55,000.00	-	-	54,000.00	-	-	1,000.00
4271	144173	Maintenance Zone 1073	480,000.00	-	-	404,552.85	-	-	75,447.15
4270	144176	Maintenance Zone 1076	260,000.00	-	7,895.58	260,000.00	-	-	-
4273	144176	Maintenance Zone 1076	2,330,000.00	-	-	1,418,019.41	0.00	-	911,980.59
4271	144199	Maintenance Zone 1099	320,000.00	2,925.66	2,928.83	255,047.71	64,952.29	-	0.00
4274	144199	Maintenance Zone 1099	2,800,000.00	-	-	-	2,129,753.17	-	670,246.83
4271	144200	Architect and Engineering Serv	330,000.00	718.00	15,641.19	274,011.97	(0.00)	-	55,988.03
4274	144200	36 St: N MLK - Peoria Ave	2,920,000.00	-	-	-	-	-	2,920,000.00
4270	144201	Apache St: Mlk - Peoria	282,774.79	-	-	282,774.79	-	-	-
4271	144201	Apache St: Mlk - Peoria	2,410,000.00	42,726.10	45,855.33	2,407,208.85	2,791.15	-	0.00
4272	144202	Apachee: Peoria - Lewis Ave	300,000.00	-	-	300,000.00	-	-	-
4270	144203	W 41st St S 41st W - S 33rd W	175,000.00	-	-	175,000.00	-	-	-
4271	144203	W 41st St S 41st W - S 33rd W	1,510,000.00	-	-	-	-	-	1,510,000.00
4270	144204	S33rd W: 41st St to 51st St	275,000.00	-	-	275,000.00	(0.00)	-	0.00
4271	144204	S33rd W: 41st St to 51st St	2,455,000.00	-	-	164,357.24	21,186.18	-	2,269,456.58
4270	144205	Apache St: Lewis To Harvard	210,000.00	-	-	210,000.00	-	-	-
4274	144205	Apache St: Lewis To Harvard	1,860,000.00	3,351.42	57,160.40	72,922.49	27,172.05	-	1,759,905.46
4270	144206	11th St: Peoria to Utica	185,000.00	-	-	185,000.00	-	-	-
4271	144206	11th St: Peoria to Utica	1,635,000.00	-	945,821.53	1,635,000.00	(0.00)	-	0.00
4272	144207	11Th St: Lewis Ave - Harvard	200,000.00	-	-	200,000.00	-	-	-
4270	144208	11th St: Sheridan - Memorial	180,000.00	-	-	180,000.00	-	-	-
4271	144208	11th St: Sheridan - Memorial	1,600,000.00	-	31,707.44	80,896.72	3,147.63	-	1,515,955.65
4270	144209	21St St: Garnett To 129Th E	300,000.00	-	10,720.17	300,000.00	-	-	(0.00)
4273	144209	21st St: Garnett to 129th E	50.00	-	-	50.00	-	-	-
4274	144209	21st St: Garnett to 129th E	2,435,000.00	394,480.91	1,140,682.16	1,140,682.16	840,159.67	-	454,158.17
4270	144210	21St St-129Th East Ave Inter	250,000.00	-	94,000.00	243,280.10	6,719.90	-	-
4273	144210	21st St-129th East Ave Inter	-	-	-	-	-	-	-
4274	144210	21st St-129th East Ave INTERSC	1,965,000.00	-	-	-	1,965,000.00	-	-
4272	144211	41St: Garnett - 129 E Ave	102,199.23	-	-	102,199.23	-	-	0.00
4273	144211	41St: Garnett - 129 E Ave	1,707,301.15	-	58.40	1,496,415.87	2,997.71	-	207,887.57
4270	144212	51st St Sheridan to Memorial	140,000.00	-	-	140,000.00	-	-	-
4271	144212	51st St Sheridan to Memorial	1,215,000.00	-	-	907,661.29	7,990.00	-	299,348.71
4273	144213	91st Harvard - Yale	285,000.00	-	7,869.34	170,477.43	24,429.04	-	90,093.53
4270	144214	Sheridan 81st to 91st	200,000.00	-	-	199,928.84	(0.00)	-	71.16

Fund

427

2014 GO BOND PROGRAM

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4272	144214	Sheridan 81st to 91st	1,715,000.00	-	-	1,326,022.15	-	-	388,977.85
4272	144215	Peoria: 41St St - 51St St.	300,000.00	-	1,330.00	296,394.50	3,605.50	-	-
4270	144216	41st St: Lewis to Harvard	275,000.00	-	-	275,000.00	-	-	-
4271	144216	41st St: Lewis to Harvard	2,455,000.00	15.00	15.00	92,055.93	2,342,111.61	-	20,832.46
4270	144217	Apache & Harvard Intersectio	200,000.00	-	-	196,823.70	-	-	3,176.30
4273	144217	Apache & Harvard Intersect	785,000.00	-	-	35.00	-	-	784,965.00
4274	144217	Apache & Harvard INTERSCTN	990,000.00	-	-	-	-	-	990,000.00
4270	144218	41st St & Lewis Intersection	210,000.00	-	-	210,000.00	-	-	-
4271	144218	41st St & Lewis Intersection	1,845,000.00	-	-	169,954.38	1,675,045.62	-	-
4270	144219	Maintenance Zone 2119	40,000.00	-	-	38,500.00	1,500.00	-	-
4271	144219	Maintenance Zone 2119	360,000.00	-	-	327,980.36	-	-	32,019.64
4270	144225	Maintenance Zone 2125	264,462.36	-	-	264,462.36	-	-	0.00
4273	144225	Maintenance Zone 2125	2,310,000.00	-	492,405.15	2,303,496.81	6,503.19	-	0.00
4270	144226	Maintenance Zone 2126	45,000.00	-	-	44,710.26	-	-	289.74
4271	144226	Maintenance Zone 2126	305,000.00	-	-	305,000.00	-	-	-
4270	144230	Maintenance Zone 2130	406,919.00	-	124,153.93	403,521.21	3,397.79	-	(0.00)
4273	144230	Maintenance Zone 2130	-	-	-	-	-	-	-
4274	144230	Maintenance Zone 2130	3,488,081.00	132,080.47	393,382.24	394,057.16	2,863,318.83	-	230,705.01
4270	144255	Maintenance Zone 2055	150,000.00	-	-	148,972.24	1,027.76	-	0.00
4271	144255	Maintenance Zone 2055	1,285,000.00	-	-	1,119,095.86	-	-	165,904.14
4270	144256	Maintenance Zone 2056	130,000.00	-	-	130,000.00	-	-	0.00
4271	144256	Maintenance Zone 2056	1,160,000.00	-	(15,000.00)	1,138,393.91	(0.00)	-	21,606.09
4270	144264	Maintenance Zone 2064	190,000.00	-	-	143,436.25	-	-	46,563.75
4272	144264	Maintenance Zone 2064	1,660,499.62	-	-	1,123,073.63	0.00	-	537,425.99
4270	144265	Maintenance Zone 2065	100,000.00	-	313.41	98,741.93	-	-	1,258.07
4271	144265	Maintenance Zone 2065	895,000.00	-	(2,813.22)	859,200.67	-	-	35,799.33
4270	144303	Maintenance Zone 3003	100,000.00	-	-	100,000.00	-	-	-
4271	144303	Maintenance Zone 3003	775,000.00	-	-	525,681.40	-	-	249,318.60
4270	144304	Maintenance Zone 3004	185,000.00	-	-	180,914.87	-	-	4,085.13
4272	144304	Maintenance Zone 3004	1,655,000.00	-	-	1,231,358.67	(0.00)	-	423,641.33
4271	144309	Citywide - Arterial Rehab	898,403.59	118,593.45	118,593.45	559,268.42	339,135.17	-	(0.00)
4272	144309	Citywide - Arterial Rehab	900,000.00	256,249.62	256,249.62	256,249.62	-	-	643,750.38
4273	144309	Citywide - Arterial Rehab	900,000.00	-	-	-	-	-	900,000.00
4274	144309	Citywide - Arterial Rehab	1,800,000.00	-	-	-	-	-	1,800,000.00
4271	144310	Maintenance Zone 3010	800,000.00	-	-	561,391.79	(0.00)	-	238,608.21
4274	144310	Maintenance Zone 3010	7,130,000.00	-	-	-	-	-	7,130,000.00
4272	144311	Maintenance Zone 3011	1,000,000.00	-	288,137.67	970,329.23	29,670.77	-	0.00
4274	144311	Maintenance Zone 3011	8,485,000.00	4,786.50	3,114,706.92	3,115,367.48	3,385,525.71	-	1,984,106.81
4273	144317	Maintenance Zone 3017	750,000.00	-	-	456,529.83	22,176.76	-	271,293.41
4270	144318	Maintenance Zone 3018	50,000.00	-	-	50,000.00	-	-	-
4271	144318	Maintenance Zone 3018	395,000.00	-	-	365,498.17	1,558.55	-	27,943.28
4272	144320	Maintenance Zone 3020	480,000.00	-	-	320,726.04	24,611.29	-	134,662.67
4274	144320	Maintenance Zone 3020	4,020,000.00	-	-	-	-	-	4,020,000.00
4270	144380	Maintenance Zone 3080	20,000.00	-	-	19,047.02	-	-	952.98

Fund

427

2014 GO BOND PROGRAM

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4271	144380	Maintenance Zone 3080	170,000.00	-	-	170,000.00	-	-	-
4270	144413	Maintenance Zone 4013	670,000.00	-	-	511,528.37	23,530.58	-	134,941.05
4272	144413	Maintenance Zone 4013	-	-	-	-	-	-	-
4270	144415	Maintenance Zone 4015	100,000.00	-	-	100,000.00	-	-	(0.00)
4271	144415	Maintenance Zone 4015	895,000.00	-	-	537,042.77	-	-	357,957.23
4272	144421	Maintenance Zone 4021	375,000.00	-	-	331,229.87	11,557.46	-	32,212.67
4270	144430	Maintenance Zone 4030	175,000.00	-	-	169,422.12	-	-	5,577.88
4272	144430	Maintenance Zone 4030	1,550,000.00	-	4,446.25	1,517,287.45	0.00	-	32,712.55
4271	144431	Maintenance Zone 4031	1,200,000.00	-	1,775.21	562,881.25	20,867.95	-	616,250.80
4274	144431	Maintenance Zone 4031	10,480,000.00	-	-	-	-	-	10,480,000.00
4273	144452	Maintenance Zone 4152	600,000.00	-	-	380,196.06	21,806.79	-	197,997.15
4270	144467	Maintenance Zone 4067	485,000.00	-	34,999.35	485,000.00	(0.00)	-	(0.00)
4273	144467	Maintenance Zone 4067	4,370,000.00	461.85	1,362,943.68	2,833,730.84	18,345.71	-	1,517,923.45
4270	144527	Maintenance Zone 5027	150,000.00	-	-	129,524.39	-	-	20,475.61
4271	144527	Maintenance Zone 5027	1,265,000.00	-	-	1,258,372.62	-	-	6,627.38
4270	144533	Maintenance Zone 5033	500,000.00	-	-	498,257.02	1,742.98	-	(0.00)
4273	144533	Maintenance Zone 5033	4,380,000.00	-	-	4,380,000.00	(0.00)	-	0.00
4270	144539	Maintenance Zone 5039	400,000.00	-	-	400,000.00	-	-	0.00
4272	144539	Maintenance Zone 5039	3,525,000.00	-	(57,500.00)	2,982,395.92	0.00	-	542,604.08
4272	144546	Maintenance Zone 5046	600,000.00	-	627.66	563,071.83	26,910.14	-	10,018.03
4272	144547	Maintenance Zone 5047	1,100,000.00	-	3,242.84	772,587.07	71,040.96	-	256,371.97
4274	144547	Maintenance Zone 5047	2,905,000.00	-	-	-	-	-	2,905,000.00
4270	144627	Maintenance Zone 6027	120,000.00	-	-	120,000.00	-	-	(0.00)
4271	144627	Maintenance Zone 6027	1,040,000.00	-	-	886,165.51	-	-	153,834.49
4273	144628	Maintenance Zone 6028	1,000,000.00	1,208.75	20,498.00	913,879.84	37,651.01	-	48,469.15
4271	144635	Maintenance Zone 6035	400,000.00	-	-	269,740.18	2,267.58	-	127,992.24
4273	144635	Maintenance Zone 6035	3,645,000.00	-	17,164.56	3,034,358.21	(0.00)	-	610,641.79
4270	144642	Maintenance Zone 6142	100,000.00	-	861.59	92,828.82	7,171.18	-	(0.00)
4271	144642	Maintenance Zone 6142	800,000.00	4,468.55	10,598.51	15,278.74	671,969.36	-	112,751.90
4270	144645	Maintenance Zone 6145	265,000.00	-	550.00	207,564.20	57,435.80	-	0.00
4273	144645	Maintenance Zone 6145	2,375,000.00	-	425.00	425.00	2,249,564.20	-	125,010.80
4270	144647	Maintenance Zone 6147	101,060.09	-	-	101,060.09	(0.00)	-	0.00
4271	144647	Maintenance Zone 6147	890,000.00	-	-	890,000.00	0.00	-	(0.00)
4271	144700	Maintenance Zone 7100	301,596.41	-	-	301,596.41	(0.00)	-	0.00
4273	144700	Maintenance Zone 7100	2,440,000.00	-	-	1,012,395.47	(0.00)	-	1,427,604.53
4270	144733	Maintenance Zone 7133	200,000.00	-	-	198,500.00	-	-	1,500.00
4271	144733	Maintenance Zone 7133	1,740,000.00	-	-	751,870.76	-	-	988,129.24
4272	144740	Maintenance Zone 7040	350,000.00	-	94,614.47	348,434.84	1,565.16	-	0.00
4274	144740	Maintenance Zone 7040	2,925,000.00	-	119,814.99	119,814.99	2,416,773.69	-	388,411.32
4270	144748	Maintenance Zone 7048	230,000.00	-	-	226,454.43	-	-	3,545.57
4273	144748	Maintenance Zone 7048	1,920,000.00	-	-	955,111.36	(0.00)	-	964,888.64
4273	144754	Maintenance Zone 7054	1,000,000.00	-	-	726,908.15	19,591.85	-	253,500.00
4270	144760	Maintenance Zone 7060	340,000.00	-	-	335,526.95	-	-	4,473.05
4272	144760	Maintenance Zone 7060	3,055,000.00	-	-	2,985,401.38	-	-	69,598.62

Fund

427

2014 GO BOND PROGRAM

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4270	144803	Maintenance Zone 8103	190,000.00	-	-	182,481.92	-	-	7,518.08
4271	144803	Maintenance Zone 8103	1,685,000.00	-	-	1,592,680.53	-	-	92,319.47
4270	144812	Maintenance Zone 8112	200,000.00	-	-	200,000.00	-	-	-
4271	144812	Maintenance Zone 8112	1,800,000.00	-	-	1,578,077.06	-	-	221,922.94
4270	144857	Maintenance Zone 8057	275,000.00	-	1,751.10	272,355.48	2,644.52	-	0.00
4273	144857	Maintenance Zone 8057	1,453,081.00	227,264.50	479,257.64	479,361.69	973,719.31	-	-
4274	144857	Maintenance Zone 8057	841,919.00	-	-	674.92	-	-	841,244.08
4273	144863	Maintenance Zone 8063	800,000.00	-	-	677,105.58	49,632.35	-	73,262.07
4270	144931	Maintenance Zone 9031	60,000.00	-	-	58,793.31	-	-	1,206.69
4271	144931	Maintenance Zone 9031	485,000.00	-	-	459,660.26	-	-	25,339.74
4270	144943	Maintenance Zone 9043	450,000.00	-	-	450,000.00	(0.00)	-	0.00
4272	144943	Maintenance Zone 9043	3,900,000.00	-	-	2,165,462.22	-	-	1,734,537.78
4270	144944	Maintenance Zone 9044	400,000.00	-	-	340,782.70	59,217.30	-	0.00
4273	144944	Maintenance Zone 9044	2,295,000.00	-	258,880.93	361,338.42	1,933,661.58	-	0.00
4274	144944	Maintenance Zone 9044	1,305,000.00	42,528.00	634,136.85	639,620.01	1,986.10	-	663,393.89
4270	144945	Maintenance Zone 9045	400,000.00	-	2,002.57	369,279.62	30,720.38	-	(0.00)
4273	144945	Maintenance Zone 9045	3,460,000.00	-	-	3,011,446.11	(0.00)	-	448,553.89
4273	144949	Maintenance Zone 9049	1,200,000.00	-	-	692,193.50	78,461.84	-	429,344.66
4272	144950	Maintenance Zone 9050	350,000.00	-	-	252,682.54	2,288.62	-	95,028.84
4272	144951	Maintenance Zone 9051	160,000.00	-	-	129,184.92	5,063.16	-	25,751.92
4274	144951	Maintenance Zone 9051	1,390,000.00	-	-	-	-	-	1,390,000.00
4270	144958	Maintenance Zone 9058	102,830.56	-	-	102,830.56	-	-	-
4271	144958	Maintenance Zone 9058	840,000.00	-	-	833,560.11	0.00	-	6,439.89
4273	193140000Z	Mingo Creek Trail - 41st to 51	196,830.00	-	-	196,830.00	-	-	-
			\$ 277,500,000.00	\$ 1,800,702.02	\$ 18,542,518.04	\$ 165,735,481.65	\$ 37,399,847.79	\$ -	\$ 74,364,670.56

2020 GO BOND FUNDS

FUNDS 4281-428x COMBINED

(2020 GENERAL OBLIGATION BOND FUND)

**CITY OF TULSA, OKLAHOMA
SALES TAX OVERVIEW COMMITTEE REPORT
FUND 4281-428x - 2020 GO BOND FUNDS**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES
FOR THE EIGHT MONTHS ENDED FEBRUARY 28, 2021**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
Revenue					
Bond Sale Receipts	\$ 17,500,000.00		\$ 17,500,000.00	\$ 17,500,000.00	
Donations					
Miscellaneous Revenue					
Total Revenue	<u>17,500,000.00</u>		<u>17,500,000.00</u>	<u>17,500,000.00</u>	
Expenditures					
Project Expenditures	17,500,000.00	251,707.33	1,208,608.15	1,208,608.15	16,291,391.85
Total Expenditures	<u>17,500,000.00</u>	<u>251,707.33</u>	<u>1,208,608.15</u>	<u>1,208,608.15</u>	<u>16,291,391.85</u>
Excess (Deficiency) of Revenue Over Expenditures			16,291,391.85	16,291,391.85	
Completed Projects Encumbrances			<u>3,886,387.33</u>	<u>3,886,387.33</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			12,405,004.52	12,405,004.52	
June 30, 2018 Ending Fund Balance					
Prior year expenditures					
June 30, 2018 Encumbrances					
Adjusted Beginning Fund Balance					
Ending Fund Balance			<u>\$ 12,405,004.52</u>	<u>\$ 12,405,004.52</u>	

Fund

428

2020 GO BOND PROGRAM

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4281	2019X0000Z	Bond Issuance Cost	27,542.00	-	-	-	-	-	27,542.00
4281	2035X0001Z	Transit-MTTA - Route 66 BRT	1,000,000.00	-	82,724.82	82,724.82	467,280.43	-	449,994.75
4281	2036A0007Z	Apache St: Harvard Ave - Yale	100,000.00	-	-	-	-	-	100,000.00
4281	2036A0013Z	Gilcrease Rd: Apache St - Pine	100,000.00	-	-	-	-	-	100,000.00
4281	2036A0025Z	41st St S: Union Ave - Elwood	250,000.00	-	-	-	-	-	250,000.00
4281	2036A0035Z	41st St S & Elwood Ave INTERSC	50,000.00	-	-	-	-	-	50,000.00
4281	2036A0042Z	Pine St: Lewis Ave - Harvard A	200,000.00	-	-	-	-	-	200,000.00
4281	2036A0043Z	Pine St: State Hwy 11 - Mingo	175,000.00	-	-	-	-	-	175,000.00
4281	2036A0047Z	Admiral Pl: Memorial Dr - Ming	240,000.00	-	-	-	-	-	240,000.00
4281	2036A0050Z	Yale Ave: Apache St - Pine St	150,000.00	-	-	-	-	-	150,000.00
4281	2036A0055Z	129th E Ave: Apache St - Pine	150,000.00	-	-	-	-	-	150,000.00
4281	2036A0058Z	Pine St & Mingo Rd INTERSCTN	200,000.00	-	-	-	-	-	200,000.00
4281	2036A0064Z	11th St S: Utica Ave - Lewis A	75,000.00	-	-	-	-	-	75,000.00
4281	2036A0072Z	11th St S & Lewis Ave INTERSCT	50,000.00	-	-	-	-	-	50,000.00
4281	2036A0092Z	31st St S: Garnett Rd - 129th	200,000.00	-	-	-	-	-	200,000.00
4281	2036A0119Z	Sheridan Rd: 71st St S - 81st	200,000.00	-	-	-	-	-	200,000.00
4281	2036A1000Z	CW Arterial Routine & Preventi	1,760,000.00	-	-	-	-	-	1,760,000.00
4281	2036A1001Z	R&P: Pavement Reinspection	500,000.00	5,418.00	108,647.07	108,647.07	391,352.93	-	-
4281	2036D0002Z	CBD: MLK & Detroit north of BN	170,000.00	2,208.10	71,394.93	88,135.23	80,405.48	-	1,459.29
4281	2036D0004Z	CBD: Detroit Ave south of BNSF	140,000.00	22,285.22	94,515.75	94,515.75	35,583.65	-	9,900.60
4281	2036D0005Z	CBD: Reconciliation Way	75,000.00	-	75,000.00	75,000.00	-	-	-
4281	2036D0007Z	CBD: Alleyways	365,000.00	-	38,298.05	38,298.05	-	-	326,701.95
4281	2036N0001Z	CW NonArterial Routine & Preve	1,500,000.00	-	-	-	-	-	1,500,000.00
4281	2036N1007Z	Maintenance Zone 1007	120,000.00	24,557.03	25,505.84	25,505.84	94,494.16	-	-
4281	2036N1070Z	Maintenance Zone 1070	250,000.00	-	416.95	416.95	218,483.05	-	31,100.00
4281	2036N1076Z	Maintenance Zone 1076	250,000.00	747.56	89,292.26	89,292.26	158,963.95	-	1,743.79
4281	2036N1078Z	Maintenance Zone 1078	300,000.00	5,273.80	89,850.85	89,850.85	163,080.72	-	47,068.43
4281	2036N2056Z	Maintenance Zone 2056	200,000.00	-	-	-	-	-	200,000.00
4281	2036N2065Z	Maintenance Zone 2065	400,000.00	12,538.61	12,538.61	12,538.61	205,071.39	-	182,390.00
4281	2036N2066Z	Maintenance Zone 2066	150,000.00	1,770.35	38,383.83	38,383.83	73,783.17	-	37,833.00
4281	2036N3081Z	Maintenance Zone 3081	100,000.00	-	80.48	80.48	70,106.80	-	29,812.72
4281	2036N4014Z	Maintenance Zone 4014	200,000.00	-	73,948.46	73,948.46	61,285.54	-	64,766.00
4281	2036N4021Z	Maintenance Zone 4021	330,000.00	82,855.41	92,293.01	92,293.01	163,616.05	-	74,090.94
4281	2036N4022Z	Maintenance Zone 4022	350,000.00	-	87,559.86	87,559.86	243,944.99	-	18,495.15
4281	2036N4030Z	Maintenance Zone 4030	150,000.00	30,701.75	59,873.80	59,873.80	90,126.20	-	0.00
4281	2036N5040Z	Maintenance Zone 5040	100,000.00	-	-	-	-	-	100,000.00
4281	2036N6035Z	Maintenance Zone 6035	120,000.00	-	-	-	-	-	120,000.00
4281	2036N7048Z	Maintenance Zone 7048	400,000.00	-	-	-	251,630.00	-	148,370.00
4281	2036N7060Z	Maintenance Zone 7060	100,000.00	-	-	-	72,602.00	-	27,398.00
4281	2036N8057Z	Maintenance Zone 8057	200,000.00	-	521.19	521.19	121,130.47	-	78,348.34
4281	2036N8102Z	Maintenance Zone 8102	260,000.00	47,794.27	47,794.27	47,794.27	123,439.73	-	88,766.00
4281	2036N9037Z	Maintenance Zone 9037	250,000.00	-	-	-	145,531.32	-	104,468.68
4281	2036N9038Z	Maintenance Zone 9038	90,000.00	-	-	-	82,635.84	-	7,364.16
4281	2036N9044Z	Maintenance Zone 9044	350,000.00	-	-	-	-	-	350,000.00
4281	2036N9050Z	Maintenance Zone 9050	150,000.00	-	-	-	97,756.66	-	52,243.34

Fund

428

2020 GO BOND PROGRAM

as of: 2/28/2021

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4281	2036N9051Z	Maintenance Zone 9051	110,000.00	2,129.55	53,869.48	53,869.48	41,238.23	-	14,892.29
4281	2036S0001Z	ADA: Sidewalk Corridors	140,000.00	-	-	-	-	-	140,000.00
4281	2036S0002Z	BPI: Go Plan Implement - ENG	165,000.00	-	-	-	165,000.00	-	-
4281	2036S0003Z	BPI: Go Plan Implement - Traff	10,000.00	-	-	-	-	-	10,000.00
4281	2036S0004Z	BPI: Arterial Sidewalk	250,000.00	96.13	96.13	96.13	-	-	249,903.87
4281	2036S0005Z	BPI: Non Arterial Sidewalk	75,000.00	-	-	-	-	-	75,000.00
4281	2036W0004Z	91 St S: Memorial - Mingo Rd W	1,200,000.00	-	-	-	-	-	1,200,000.00
4281	2036X0001Z	ADA: Transition Plan Update	250,000.00	-	-	-	-	-	250,000.00
4281	2036X0002Z	ADA: Transit Stops	60,000.00	-	-	-	-	-	60,000.00
4281	2036X0003Z	ADA: Signalized Intersections	50,000.00	-	-	-	-	-	50,000.00
4281	2036X0005Z	TE: Signal Coord and Communica	100,000.00	-	-	-	-	-	100,000.00
4281	2036X0006Z	TE: Signal Instal, Repair and	300,000.00	-	-	-	-	-	300,000.00
4281	2036X0007Z	TE: Traffic Calming	50,000.00	-	-	-	-	-	50,000.00
4281	2036X0008Z	TE: Lighting Repair and Replac	100,000.00	-	-	-	-	-	100,000.00
4281	2036X0009Z	TE: Pavement Markings and Sign	375,000.00	-	-	-	-	-	375,000.00
4281	2036X0010Z	TE: Guardrail Repair and Repl	50,000.00	-	-	-	-	-	50,000.00
4281	2036X0011Z	Arena District Master Pln Impl	582,458.00	-	-	-	-	-	582,458.00
4281	2037B0167Z	Bridge #167	30,000.00	-	-	-	-	-	30,000.00
4281	2037B0173Z	Bridge #173	50,000.00	-	-	-	-	-	50,000.00
4281	2037B0201C	Bridge #201C	20,000.00	-	-	-	-	-	20,000.00
4281	2037B0204Z	Bridge #204	145,000.00	-	-	-	82,759.78	-	62,240.22
4281	2037B0232A	Bridge #232A	100,000.00	-	-	-	22,300.00	-	77,700.00
4281	2037B0241Z	Bridge #241	150,000.00	-	-	-	-	-	150,000.00
4281	2037B0245Z	Bridge #245	100,000.00	-	-	-	88,700.00	-	11,300.00
4281	2037B0258Z	Bridge #258	35,000.00	-	-	-	35,000.00	-	-
4281	2037B0261A	Bridge #261A	35,000.00	-	-	-	-	-	35,000.00
4281	2037B0261B	Bridge #261B	35,000.00	-	-	-	-	-	35,000.00
4281	2037B0263Z	Bridge #263	65,000.00	-	-	-	-	-	65,000.00
4281	2037B0269Z	Bridge #269	50,000.00	-	-	-	-	-	50,000.00
4281	2037B0286Z	Bridge #286	30,000.00	-	-	-	-	-	30,000.00
4281	2037B0301A	Bridge #301A	40,000.00	-	-	-	-	-	40,000.00
4281	2037B0301Z	Bridge #301	30,000.00	-	-	-	-	-	30,000.00
4281	2037B0343Z	Bridge #343	10,000.00	-	-	-	-	-	10,000.00
4281	2037B0359Z	Bridge #359	15,000.00	-	-	-	-	-	15,000.00
4281	2037B0423Z	Bridge #423	20,000.00	-	-	-	-	-	20,000.00
4281	2037B1000Z	CW Bridge Rehab and Inspection	150,000.00	13,331.55	24,262.21	24,262.21	39,084.79	-	86,653.00
4281	2039X0009Z	TE: Traffic Studies	25,000.00	-	25,000.00	25,000.00	-	-	-
			\$ 17,500,000.00	\$ 251,707.33	\$ 1,191,867.85	\$ 1,208,608.15	\$ 3,886,387.33	\$ -	\$ 12,405,004.52

COMBINED STATEMENT OF OTHER FUND ACTIVITY

FUNDS 400, 401, 403, 425

SALES TAX OVERVIEW COMMITTEE REPORT
(FUNDS 400, 401, 403, 425)
 Combined Statement of Fund Activity
 February 28, 2021

FUND	LIFE-TO-DATE APPROPRIATIONS	EXPEDITURES			ENCUMBERED/ COMMITTED	BALANCE
		CURRENT MONTH	FISCAL YEAR-TO-DATE	LIFE-TO-DATE		
FUND 400 - 1985 SALES TAX ECONOMIC DEVEL.	\$ 773,571.70	\$ -	\$ -	\$ 575,503.56	\$ -	\$ 198,068.14
017110 General Park Improvements	248,000.00	0.00	0.00	49,931.86	0.00	198,068.14
FUND 401 - 2001 SALES TAX FUND	\$ 84,712,542.85	\$ 59,176.87	\$ 300,260.88	\$ 84,687,475.98	\$ 14,589.32	\$ 10,477.55
012110 Northslope Wwtp Impr.	365,000.00	0.00	0.00	365,000.00	0.00	0.00
013110 Crow Creek Channel Rehab.	1,656,764.36	0.00	0.00	1,656,764.36	0.00	0.00
013120 Citywide Flood Control	7,598,000.00	0.00	0.00	7,598,000.00	0.00	0.00
013140 Fred Creek Guier Wd Drainage	451,854.00	0.00	0.00	451,854.00	0.00	0.00
017110 General Park Improvements	4,611,018.12	44,817.30	247,338.92	4,585,951.25	14,589.32	10,477.55
203400001Z Tulsa Zoo Department	37,773.32	0.00	37,668.17	37,773.32	0.00	0.00
912222 Utility Relocation For I-44	63,226.68	0.00	832.59	63,226.68	0.00	0.00
914411 Tulsa Trails	3,857,231.30	14,359.57	14,421.20	3,857,231.30	0.00	0.00
FUND 403 - 2006 EXT SALES TAX ADVANCE FUND	27,705,922.61	0.00	0.00	27,705,676.78	0.00	245.83
017150 Woodward & Forestry Impr.	470,000.00	0.00	0.00	469,754.17	0.00	245.83
FUND 425 - 2005 BONDS ISSUE (4250-4255)	74,919,257.38	0.00	194,293.63	74,004,599.81	3,126.25	911,531.32
054053 91St-Memorial To Mingo Ed	300,000.00	-	190,571.16	300,000.00	(0.00)	0.00
055103 UDE Renovation	41,000.00	-	-	23,455.40	-	17,544.60
055105 UDSW Renovation	60,629.78	-	-	35,769.15	-	24,860.63
055105 UDSW Renovation	431,012.58	-	-	428,485.28	-	2,527.30
055200 Fire Trng Ctr/Reloc Sta 16	11,100,000.00	-	-	11,046,992.63	-	53,007.37
104020 Citywide-Arterial Rt&Pv Main	320,000.00	-	-	316,873.75	3,126.25	0.00
104021 Garnett Pine to Apache	300,000.00	-	-	291,261.92	-	8,738.08
147200 RP - Pedestrian Bridge Imp	100,000.00	-	-	-	-	100,000.00
147200 RP - Pedestrian Bridge Imp	157,598.94	-	-	-	-	157,598.94
147200 RP - Pedestrian Bridge Imp	396,595.56	-	-	-	-	396,595.56
147200 RP - Pedestrian Bridge Imp	97,273.46	-	-	-	-	97,273.46
155107 Police Courts Renovation	79,913.01	-	-	79,913.01	(0.00)	0.00
155107 Police Courts Renovation	83,169.14	-	-	46,782.86	(0.00)	36,386.28
155107 Police Courts Renovation	510,877.21	-	-	503,542.28	(0.00)	7,334.93
203400001Z Tulsa Zoo Department	2,811.76	-	-	-	-	2,811.76

**ALL FUNDS
BUDGET ACTIONS**

**THERE WERE NO
BUDGET ACTIONS POSTED
THIS MONTH**
