



**Department of Finance  
Budget and Planning Division  
Capital Planning Section  
175 E 2<sup>nd</sup>, Tulsa, Oklahoma 74103-3203**

**To:** STOC

Jake Epp

**From:** Capital Planning Manager

**Date:** April 25, 2023

**Subject:** April Meeting

Enclosed is the material for your April 25, 2023 meeting including the March 31, 2023 Financial Report for your review. 2016 and 2020 Sales Tax Program revenues for April 2023 and the fiscal year to date compared to 2016 and 2020 Sales Tax Program Adopted Budget Estimates are:

	Actual	Current Adopted Budget	Variance from Adopted Budget
<b>Month of April</b>	\$9,378,599	\$8,770,985	6.9%
<b>Year To Date</b>	\$98,843,616	\$93,631,174	5.6%

Please note the above amounts are the Sales Tax revenue only.

The 2016 and 2020 Sales Tax Programs Funds (4000 and 409), in addition to sales tax revenue, receives interest, and other revenues such as grants, transfers and miscellaneous revenues. Total revenue reported for the funds is not available until the end of the month so, the information provided below is for the most recently completed month. Total Fund 4000 and 409 revenue for the month of March was:

	<u>Month Ending:</u> <u>March 31, 2023</u>	<u>Variance from</u> <u>Adopted Budget</u>	<u>Year Thru:</u> <u>March 31, 2023</u>	<u>Variance from</u> <u>Adopted Budget</u>
Sales Tax Revenue	\$9,110,867	5.6%	\$89,465,016	5.4%
Interest on Investments	\$492,064	N/A	\$3,431,121	N/A
Other Revenue	<u>\$0</u>	N/A	<u>\$0</u>	N/A
<b>Total Fund Revenue</b>	<b>\$9,602,930</b>	5.3%	<b>\$92,896,137</b>	5.2%

SALES TAX OVERVIEW COMMITTEE  
APRIL 25, 8:00 AM  
175 E. 2<sup>ND</sup> ST, 10-SOUTH CONFERENCE ROOM

The STOC will meet in person at 8:00 am on April 25, 2023.

- I. Call to Order
- II. Reading of the February and March Minutes
- III. Chair Report to Council
- IV. Subcommittee Reports
  - A. Vison
  - B. Public Safety
  - C. Parks
  - D. Transportation
  - E. Financial
- V. Unfinished Business
- VI. New Business
  - A. Chair Report Presenters
  - B. Nominations for Officers
- VII. Adjournment

# STOC

Sales Tax Overview Committee

## MINUTES

### Sales Tax Overview Committee Meeting

February 28, 2023, 8:00 a.m.

175 E 2<sup>nd</sup> Street, 3<sup>rd</sup> Floor Presentation room

The Sales Tax Overview Committee met for the regular monthly meeting at 8:00 a.m. on February 28, 2023.

#### I. Call to Order

Chair Ashley Webb called the meeting to order at 8:00 a.m.

The following members were present:

Pamela Amburgy	Matt Meyer
Scott Grizzle	Sylvia Powell
Mareo Johnson	Kathy Sebert
Steve King	Ashley Webb
Diamond Marshall	

The following members were not present:

Janae Bradford	Alex Gomez	Paul McTighe
Marcia Bruno-Todd	Jonathan Hall	Renee Plocek
Jeffrey Covington	Linda Jenkins`	Charles Wilkes

Also present:

Anne Boyd	Jake Epp	Mary Kell	Susan Neal
Andrew Witte	Melissa Lynn		

#### II. Approval of Minutes

Minutes for the January meeting were read Pamela Amburgy moved the be approved as read, Kathy Sebert seconded the motion. The motion carried.

#### III. Chair's Report

Kathy Sebert gave the report. She mentioned the Turkey Mountain urban wilderness project and clarified the status the police helicopter. She brought up the trend upward in pricing and costs and made the Council aware that projects were going over budget for this reason. There was no other discussions or questions.

# STOC

## Sales Tax Overview Committee

### IV. Committee Reports

#### A. Vision

Susan Neal reported on the Gilcrease Museum project. The funding for the building has been reached. Fundraising now is for the exhibit installation, the total for this will be \$20.2 million. The increase in costs did not result in an increase in management fee, Flintco is holding to their fee based on the original budgeted amount. The project is still scheduled to be completed by the end of 2024. There were no other questions or discussions, and the report was accepted.

#### B. Public Safety

Ashley Webb gave the report. There is concern in the Committee that the Rte. 66 Xperience is taking so long. The 100<sup>th</sup> anniversary of Route 66, The Mother Road, is in 2026 and they would like to see this project completed before that celebration. The Fire Department has vehicles in the final stages of production. Two should be received by the end of February and 4 will be ready for inspection by the end of the same month. The helicopter designated Police 2 is still down for repairs and is expected to be back in service by the end of March. There is concern this was a manufacturing error and an investigation is ongoing. There were no other questions or discussions, and the report was accepted.

#### C. Parks

Ashley Webb reported on Parks. McClure Park has an anniversary in June. The old plunge pool area will be made safe by then with remediation work to continue by turning the area into a seating area with pavilion. Zeigler Park is to receive HUD funding to help with the playground that was burned. There were no further questions or comments, and the report was accepted.

#### D. Transportation

There was little discussion on the transportation projects. Members were urged to submit any questions they might have for future response. There were no further questions or comments, and the report was accepted.

#### E. Financial

The February collections were \$10.4M which is about 7.9 percent over budget. Current sales tax collections are about 5.4 percent ahead of budget for the year to date.

# STOC

Sales Tax Overview Committee

V. Unfinished Business

VI. New Business

A. Chair Report Presenters

Date	Presenter	Backup
Apr 12	Kathy Sebert	Ashley Webb
May 3	Mareo Johnson	Ashley Webb

6/7, 7/19, 8/2, 9/13, 10/4, 11/1, 12/6

VII. Adjournment

The meeting was adjourned at 9:04 a.m.

Ashley Webb, Chair

Kathy Sebert, Vice Chair



# STOC

Sales Tax Overview Committee

## MINUTES

### Sales Tax Overview Committee Meeting

March 28, 2023, 8:00 a.m.

175 E 2<sup>nd</sup> Street, 3<sup>rd</sup> Floor Presentation room

The Sales Tax Overview Committee met for the regular monthly meeting at 8:00 a.m. on March 28, 2023.

I. Call to Order

Chair Ashley Webb called the meeting to order at 8:02 a.m.

The following members were present:

Pamela Amburgy	Steve King
Scott Grizzle	Matt Meyer
Paul Hassink	Sylvia Powell
Linda Jenkins	Kathy Sebert
Mareo Johnson	Ashley Webb

The following members were not present:

Janae Bradford	Bruce Denny	
Marcia Bruno-Todd	Jonathan Hall	Renee Plocek
Jeffrey Covington	Paul McTighe	Charles Wilkes

Also present:

Anne Boyd	Jake Epp	Chris Havenar	Mary Kell
Jeff Edwards	Ryan Hall		

II. Approval of Minutes

The minutes for the February meeting were table, they were not included in the meeting packet.

III. Chair's Report

Ashley Webb gave the report. He reported that he highlighted the savings on playgrounds by using the state's contract with SourceWell. He noted that there were budget actions pending for the Animal Shelter and Gilcrease Museum. There were no other discussions or questions.

# STOC

## Sales Tax Overview Committee

### IV. Committee Reports

#### A. Vision

Jeff Edwards and Ryan Hall reported on the Turkey Mountain project. The 71<sup>st</sup> Street trail is expected to go out for bid in the next few weeks. The current estimate is \$1 million. There is work being done to identify how to use any balance of funds. There is work being done on making some areas ADA compliant. The topography does not allow all areas to be accessible to those with disabilities, but they are trying to get as much as the terrain allows. Others noted that there is ribbon cutting scheduled for Langston on March 29. Repairs to the concrete at the Cox Center have an April 3<sup>rd</sup> start date. There were no other questions or discussions, and the report was accepted.

#### B. Public Safety

Ashley Webb gave the report. There is concern in the Committee that the Rte. 66 Xperience is taking so long. Arrangements are being made with Ms. Carr from the Mayor's office to get an updated report on this project at the April meeting. Police report that all FY22 purchase orders are complete and work on FY23 orders is ongoing. There were no other questions or discussions, and the report was accepted.

#### C. Parks

Ashley Webb and Kathy Sebert reported on Parks. Mr. Webb reported McClure Park will have a 70<sup>th</sup> anniversary party on June 3. The plunge pool area is expected to be cleaned up and made safe prior to this event. Ms. Sebert reported that items for the Inclusive Playground are beginning to arrive. Once construction begins, it is expected to take around 75 days. There were no further questions or comments, and the report was accepted.

#### D. Transportation

There was little discussion on the transportation projects. Members were urged to submit any questions they might have for future response. There were no further questions or comments, and the report was accepted.

#### E. Financial

The March collections were \$9.1M which is about 5.6 percent over budget. Current sales tax collections are about 5.4 percent ahead of budget for the year to date.

# STOC

## Sales Tax Overview Committee

V. Unfinished Business

VI. New Business

A. Chair Report Presenters

Date	Presenter	Backup
May 3	Mareo Johnson	Ashley Webb

6/7, 7/19, 8/2, 9/13, 10/4, 11/1, 12/6

VII. Adjournment

The meeting was adjourned at 9:12 a.m.

Ashley Webb, Chair

Kathy Sebert, Vice Chair





# STOC

SALES TAX OVERVIEW COMMITTEE

Ashley Webb  
Chair

Ashley R. Webb  
Riggs, Abney, Neal, Turpen, Orbison & Lewis Inc.  
Attorney At Law  
Tulsa, OK 74119  
(918) 699-8905

**To:** City Council  
**Date:** April 12, 2023  
**Subject:** April Report to City Council

Attached is the March 2023 Sales Tax Overview Committee (STOC) Status Report

## **2006 Special Extended Sales Tax**

February expenditures totaled \$7,000, of which \$7,000 was spent on Citywide Bridge Rehab/Repair projects. Encumbrances and commitments total \$5,790,000. Current appropriations for the 2006 Special Extended Sales Tax Fund total \$271,812,000. There is a current appropriation balance of \$2,248,000.

## **2008 Sales Tax Special Temporary Streets**

There were no expenditures in February. Encumbrances and commitments total \$158,000. Current appropriations for the 2008 Sales Tax Special Temporary Streets Fund total \$145,494,000. There is a current appropriation balance of \$38,000.

## **2014 Sales Tax**

February expenditures totaled \$2,144,000, of which \$1,271,000 was spent on the Yale Avenue 81St - 91St Widening project. Encumbrances and commitments total \$45,135,000. Current appropriations for the 2014 Sales Tax Fund total \$568,601,000. There is a current appropriation balance of \$123,491,000.

## **2016 Sales Tax**

February expenditures totaled \$5,606,000, of which \$4,738,000 was spent on the Transfer to Tulsa Vision Advanced Sales Tax Revenue Bonds project. Encumbrances and commitments total \$4,041,000. Current appropriations for the 2016 Sales Tax Fund total \$256,927,000. There is a current appropriation balance of \$49,670,000.

## **2016 Revenue Bond**

February expenditures totaled \$7,681,000, of which \$3,539,000 was spent on the Gilcrease Museum Expansion project. Encumbrances and commitments total \$60,123,000. Current appropriations for the 2016 Revenue Bond Fund total \$350,600,000. There is a current appropriation balance of \$19,068,000.

## **2020 Sales Tax**

February expenditures totaled \$942,000, of which \$940,000 was spent on the Citywide Capital Equipment project. Encumbrances and commitments total \$19,983,000. Current appropriations for the 2020 Sales Tax Fund total \$73,956,000. There is a current appropriation balance of \$21,171,000.

**2020 General Obligation Bonds**

February expenditures totaled \$335,000, of which \$107,000 was spent on the Maintenance Zone 9044 (see maintenance zone map on following page) project. Encumbrances and commitments total \$20,639,000. Current appropriations for the 2020 General Obligation Bonds Fund total \$149,015,000. There is a current appropriation balance of \$104,567,000.

**2014 General Obligation Bonds**

February expenditures totaled \$1,379,000, of which \$771,000 was spent on the Maintenance Zone 4031 (see maintenance zone map on following page) project. Encumbrances and commitments total \$34,036,000. Current appropriations for the 2014 General Obligation Bonds Fund total \$313,615,000. There is a current appropriation balance of \$57,681,000.

**2008 General Obligation Bonds**

February expenditures totaled \$12,000, of which \$12,000 was spent on the Citywide Nonarterial Rehabilitation & Repair project. Encumbrances and commitments total -\$12,000. Current appropriations for the 2008 General Obligation Bonds Fund total \$230,055,000. There is a current appropriation balance of \$9,380,000.

**2005 General Obligation Bonds**

There were no expenditures in February. Encumbrances and commitments total \$11,000. Current appropriations for the 2005 General Obligation Bonds Fund total \$74,919,000. There is a current appropriation balance of \$89,000.

Respectfully submitted,

Ashley Webb, Chair



Attachments

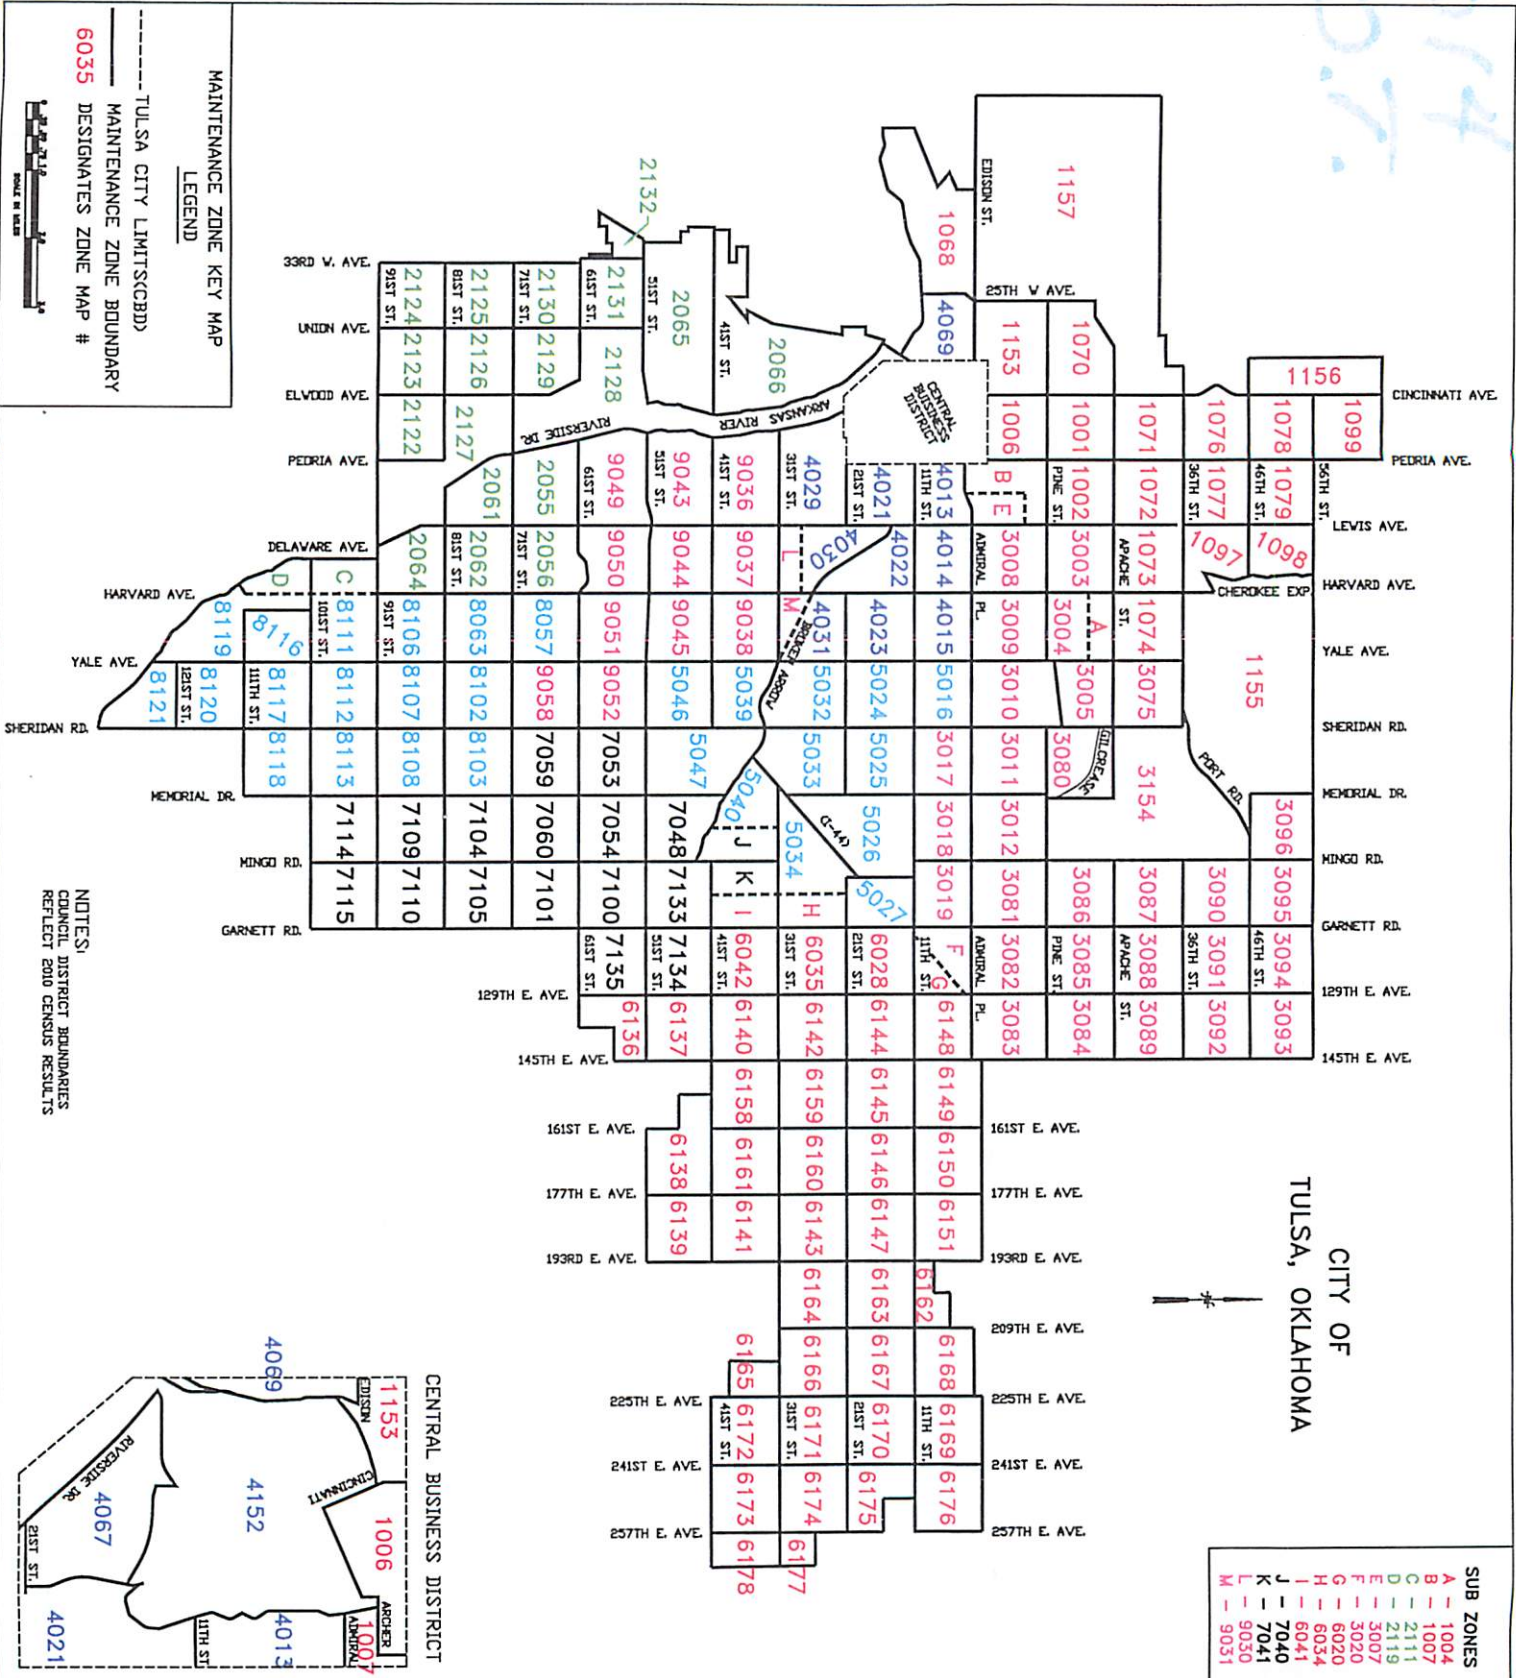
cc: Tammy Pitts  
Jarrod Moore  
Jake Epp

2014  
T.O.T.

CITY OF  
TULSA, OKLAHOMA

SUB ZONES


A	1004
B	1007
C	2111
D	2119
E	3007
F	3020
G	6020
H	6034
I	6041
J	7040
K	7041
L	9030
M	9031



MAINTENANCE ZONE KEY MAP  
LEGEND  
TULSA CITY LIMITS(CBD)  
MAINTENANCE ZONE BOUNDARY  
DESIGNATES ZONE MAP #



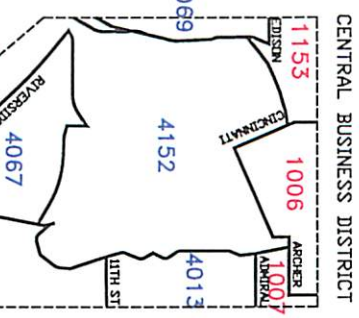NOTES:  
COUNCIL DISTRICT BOUNDARIES  
REFLECT 2010 CENSUS RESULTS





**FINANCIAL REPORT TO CITY COUNCIL**  
 Wednesday, April 12, 2023

**I. Financial Report**

*Revenue: 2016 Vision 0.805 Percent and 2020 Sales Tax 0.45 Percent Sales Tax Funds*

	<b>March</b>	<b>Fiscal Year to Date Thru March</b>
Actual	\$ 9,110,867	\$ 89,465,016
Adopted Budget - Current Year	8,631,254	84,860,189
<b>Actual vs Budget</b>	<b>\$ 479,613</b>	<b>\$ 4,604,827</b>

**Expenditures**

<b>Fund</b>	<b>February</b>	<b>Fiscal Year to Date Thru February</b>
409 - 2020 Sales Tax	\$ 941,980	\$ 13,906,142
4001, 4003-4004 - Tulsa Vision Rev Bonds	7,680,517	28,622,259
4000 - Tulsa Vision Sales Tax	5,606,153	50,993,418
405 - 2014 Sales Tax	2,144,144	20,052,129
404 - 2008 Streets Temporary Sales Tax	-	67,687
402 - 2006 Special Extended Sales Tax	6,530	2,481,668
<b>TOTAL</b>	<b>\$ 16,379,323</b>	<b>\$ 116,123,302</b>

**II. Expenditures in Other Funds**

<b>Fund</b>	<b>February</b>	<b>Fiscal Year to Date Thru February</b>
401 - 2001 Sales Tax	-	\$ -
428 - 2020 GO Bond	670,886	25,083,562
427 - 2014 GO Bond	2,757,004	22,860,123
426 - 2008 GO Bond	24,793	4,833,187
425 - 2005 GO Bond	-	-
<b>TOTAL</b>	<b>\$ 3,452,682</b>	<b>\$ 52,776,872</b>

**III. Items for the City Council's Attention**

- A. Monthly Financial Reports
- B. STOC Committee and Subcommittee Minutes and Reports

**IV. Attachments**

- A. Attendance Record for the last 12 months
- B. STOC Committee and Subcommittee Minutes and Reports

Respectfully submitted,

Ashley R. Webb, Chair

Attachments

cc: Tammy Pitts  
 Jarrod Moore  
 Jake Epp

**MAJOR CAPITAL IMPROVEMENTS CONSTRUCTION FUNDS SUMMARY**  
**As of February, 2023**

	CURRENT		EXPENDITURES		ENCUMBERED	PERCENT	BALANCE
	APPROPRIATIONS		Current Month	To Date			
Fund 401 and Fund 403							
<b>2001 Third Penny Sales Tax and 2006 Advance Funded Sales Tax</b>	\$ 112,558,928	\$	-	\$ 112,531,735	\$ (0)	100%	\$ 27,193
Fund 402							
<b>2006 Third Penny Sales Tax Extension</b>	\$ 271,811,704	\$	6,530	\$ 263,774,163	\$ 5,789,984	99%	\$ 2,247,558
Fund 404							
<b>2008 Sales Tax Special Temporary Streets Fund</b>	\$ 145,493,500	\$	-	\$ 145,298,037	\$ 157,931	100%	\$ 37,532
Fund 405							
<b>2014 Sales Tax Fund</b>	\$ 568,601,088	\$	2,144,144	\$ 399,975,519	\$ 45,134,691	78%	\$ 123,490,878
Fund 406: 4000							
<b>2016 Sales Tax Fund</b>	\$ 256,926,895	\$	5,606,153	\$ 203,215,756	\$ 4,040,841	81%	\$ 49,670,298
Fund 406: 4001, 4003, 4004							
<b>2016 Revenue Bond Fund</b>	\$ 350,600,000	\$	7,680,517	\$ 271,409,248	\$ 60,123,094	95%	\$ 19,067,658
Fund 409							
<b>2020 Sales Tax Fund</b>	\$ 73,955,556	\$	941,980	\$ 32,801,747	\$ 19,982,909	71%	\$ 21,170,900
Fund 428							
<b>2020 General Obligation Bonds</b>	\$ 149,015,000	\$	335,443	\$ 23,809,195	\$ 20,639,218	30%	\$ 104,566,587
Fund 427							
<b>2014 General Obligation Bonds</b>	\$ 313,615,000	\$	1,378,502	\$ 221,897,228	\$ 34,036,472	82%	\$ 57,681,300
Funds 426							
<b>2008 General Obligation Bonds</b>	\$ 230,054,937	\$	12,396	\$ 220,687,408	\$ (12,396)	96%	\$ 9,379,925
Funds 425							
<b>2005 General Obligation Bonds</b>	\$ 74,919,257	\$	-	\$ 74,819,697	\$ 10,911	100%	\$ 88,650
Fund 740: 7401-7408							
<b>TMUA--Water Capital Fund</b>	\$ 455,071,405	\$	1,814,776	\$ 344,659,920	\$ 57,740,231	88%	\$ 52,671,255
Funds 750: 7501-7522							
<b>TMUA-Sanitary Sewer Capital Funds</b>	\$ 571,056,957	\$	948,847	\$ 456,957,120	\$ 65,642,453	92%	\$ 48,457,384

# STOC

Sales Tax Overview Committee

## MINUTES

### Sales Tax Overview Committee Meeting

January 24, 2023, 8:00 a.m.

175 E 2<sup>nd</sup> Street, 3<sup>rd</sup> Floor Presentation room

The Sales Tax Overview Committee met for the regular monthly meeting at 8:00 a.m. on January 24, 2023.

#### I. Call to Order

Chair Ashley Webb called the meeting to order at 8:00 a.m.

The following members were present:

Pamela Amburgy	Matt Meyer
Scott Grizzle	Sylvia Powell
Mareo Johnson	Kathy Sebert
Steve King	Ashley Webb
Diamond Marshall	

The following members were not present:

Janae Bradford	Alex Gomez	Paul McTighe
Marcia Bruno-Todd	Jonathan Hall	Renee Plocek
Jeffrey Covington	Linda Jenkins`	Charles Wilkes

Also present:

Anne Boyd	Jake Epp	Mary Kell	Susan Neal
Andrew Witte	Melissa Lynn		

#### II. Approval of Minutes

Minutes for the November and December meetings were read Pamela Amburgy moved that both months be approved as read, Kathy Sebert seconded the motion. The motion carried.

#### III. Chair's Report

Kathy Sebert gave the report. She mentioned the Turkey Mountain urban wilderness project and clarified the status the police helicopter. She brought up the trend upward in pricing and costs and made the Council aware that projects were going over budget for this reason. There was no other discussions or questions.

# STOC

## Sales Tax Overview Committee

### IV. Committee Reports

#### A. Vision

Susan Neal reported on the Gilcrease Museum project. The funding for the building has been reached. Fundraising now is for the exhibit installation, the total for this will be \$20.2 million. The increase in costs did not result in an increase in management fee, Flintco is holding to their fee based on the original budgeted amount. The project is still scheduled to be completed by the end of 2024. There were no other questions or discussions, and the report was accepted.

#### B. Public Safety

Ashley Webb gave the report. There is concern in the Committee that the Rte. 66 Xperience is taking so long. The 100<sup>th</sup> anniversary of Route 66, The Mother Road, is in 2026 and they would like to see this project completed before that celebration. The Fire Department has vehicles in the final stages of production. Two should be received by the end of February and 4 will be ready for inspection by the end of the same month. The helicopter designated Police 2 is still down for repairs and is expected to be back in service by the end of March. There is concern this was a manufacturing error and an investigation is ongoing. There were no other questions or discussions, and the report was accepted.

#### C. Parks

Ashley Webb reported on Parks. McClure Park has an anniversary in June. The old plunge pool area will be made safe by then with remediation work to continue by turning the area into a seating area with pavilion. Zeigler Park is to receive HUD funding to help with the playground that was burned. There were no further questions or comments, and the report was accepted.

#### D. Transportation

There was little discussion on the transportation projects. Members were urged to submit any questions they might have for future response. There were no further questions or comments, and the report was accepted.

#### E. Financial

The February collections were \$10.4M which is about 7.9 percent over budget. Current sales tax collections are about 5.4 percent ahead of budget for the year to date.

# STOC

Sales Tax Overview Committee

V. Unfinished Business

VI. New Business

A. Chair Report Presenters

Date	Presenter	Backup
Apr 12	Kathy Sebert	Ashley Webb
May 3	Mareo Johnson	Ashley Webb

6/7, 7/19, 8/2, 9/13, 10/4, 11/1, 12/6

VII. Adjournment

The meeting was adjourned at 9:04 a.m.

Ashley Webb, Chair

Kathy Sebert, Vice Chair





Sales Tax Overview Committee

# STOC

SALES TAX OVERVIEW COMMITTEE

12-Month Attendance Record

Mar-23

Member	Expires	District	Jan-23	Feb-23	Mar-23	Apr-22	May-22	Jun-22	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	# Attended	# Possible	Comments
Wilkes, Charles	Dec-26	1	P	A	A	P	A	P	P	A	A	P	P	A	6 of 12		as of Jan. 2023
Jenkins, Linda	Dec-24	1	P	A	P	P	P	P	P	A	P	P	P	P	10 of 12		
McTighe Jr., Paul	Dec-26	2	A	A	A	P	P	P	P	A	P	P	P	A	7 of 12		
Powell, Sylvia	Dec-24	2	P	P	P	P	P	P	P	P	A	P	P	A	10 of 12		
Marshall, Diamond	Dec-26	3	A	P	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	1 of 2		Marshal resigned 3/23
Plocek, Renee	Dec-24	3	A	A	A	A	A	A	A	A	A	A	A	A	0 of 12		
Vacant	Dec-22	4	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	0 of 0		
Webb, Ashley (Chair )	Dec-24	4	P	P	P	P	P	P	P	P	P	P	P	P	12 of 12		
Sebert, Kathy (Vice-Chair)	Dec-22	5	P	P	P	P	P	P	P	P	P	P	P	P	12 of 12		
Covington, Jeff	Dec-24	5	P	A	A	A	A	P	P	P	P	A	A	P	6 of 12		
Vacant	Dec-24	6	A	A	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	0 of 2		as of Mar. 2023
Denny, Bruce	Dec-26	6	A	A	A	A	A	A	A	A	A	A	A	A	0 of 12		
Meyer, Matt	Dec-26	7	P	P	P	P	A	P	A	P	P	A	A	P	8 of 12		
Bradford, Janae (Secretary)	Dec-24	7	A	A	A	A	A	P	P	P	A	A	A	A	3 of 12		
Hall, Jonathan	Dec-22	8	A	A	A	P	P	P	P	P	A	A	A	A	5 of 12		
King, Steve	Dec-24	8	P	P	P	P	P	P	OT	P	P	P	P	P	11 of 12		
Grizzle, Scott	Dec-26	9	P	P	P	A	P	P	P	P	A	P	P	A	9 of 12		
Hassink, Paul	Dec-24	9	NM	NM	P	A	A	A	A	A	A	A	A	A	1 of 10		as of Mar. 2023
Amburgy, Pamela	Dec-26	M	P	P	P	P	P	P	A	P	A	P	P	P	10 of 12		
Vacant	Dec-24	M	A	A	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	0 of 2		
Johnson, Mareo	Dec-26	M	A	P	P	P	A	P	P	P	P	A	P	A	8 of 12		
<b>Members Present</b>			<b>10</b>	<b>9</b>	<b>10</b>	<b>11</b>	<b>9</b>	<b>14</b>	<b>11</b>	<b>11</b>	<b>8</b>	<b>9</b>	<b>10</b>	<b>7</b>			

A = ABSENT  
 P = PRESENT  
 NM = NO MEMBER APPOINTED  
 OC = OUT OF COUNTRY  
 OT = OUT OF TOWN on Business

Prepared by City of Tulsa  
 Department of Finance  
 Budget & Planning Division  
 Capital Planning Section

Sales Tax Overview Committee

# STOC

SALES TAX OVERVIEW COMMITTEE

12-Month Attendance Record

Mar-23

Member	Expires	District	Jan-23	Feb-23	Mar-23	Apr-22	May-22	Jun-22	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	# Attended	# Possible	Comments
Wilkes, Charles	Dec-26	1	P	A	A	P	A	P	P	A	A	P	P	A	6 of 12		as of Jan. 2023
Jenkins, Linda	Dec-24	1	P	A	P	P	P	P	P	A	P	P	P	P	10 of 12		
McTighe Jr., Paul	Dec-26	2	A	A	A	P	P	P	P	A	P	P	P	A	7 of 12		
Powell, Sylvia	Dec-24	2	P	P	P	P	P	P	P	P	A	P	P	A	10 of 12		
Marshall, Diamond	Dec-26	3	A	P	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	1 of 2		Marshal resigned 3/23
Plocek, Renee	Dec-24	3	A	A	A	A	A	A	A	A	A	A	A	A	0 of 12		
Vacant	Dec-22	4	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	0 of 0		
Webb, Ashley (Chair )	Dec-24	4	P	P	P	P	P	P	P	P	P	P	P	P	12 of 12		
Sebert, Kathy (Vice-Chair)	Dec-22	5	P	P	P	P	P	P	P	P	P	P	P	P	12 of 12		
Covington, Jeff	Dec-24	5	P	A	A	A	A	P	P	P	P	A	A	P	6 of 12		
Vacant	Dec-24	6	A	A	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	0 of 2		as of Mar. 2023
Denny, Bruce	Dec-26	6	A	A	A	A	A	A	A	A	A	A	A	A	0 of 12		
Meyer, Matt	Dec-26	7	P	P	P	P	A	P	A	P	P	A	A	P	8 of 12		
Bradford, Janae (Secretary)	Dec-24	7	A	A	A	A	A	P	P	P	A	A	A	A	3 of 12		
Hall, Jonathan	Dec-22	8	A	A	A	P	P	P	P	P	A	A	A	A	5 of 12		
King, Steve	Dec-24	8	P	P	P	P	P	P	OT	P	P	P	P	P	11 of 12		
Grizzle, Scott	Dec-26	9	P	P	P	A	P	P	P	P	A	P	P	A	9 of 12		
Hassink, Paul	Dec-24	9	NM	NM	P	A	A	A	A	A	A	A	A	A	1 of 10		as of Mar. 2023
Amburgy, Pamela	Dec-26	M	P	P	P	P	P	P	A	P	A	P	P	P	10 of 12		
Vacant	Dec-24	M	A	A	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	0 of 2		
Johnson, Mareo	Dec-26	M	A	P	P	P	A	P	P	P	P	A	P	A	8 of 12		
<b>Members Present</b>			<b>10</b>	<b>9</b>	<b>10</b>	<b>11</b>	<b>9</b>	<b>14</b>	<b>11</b>	<b>11</b>	<b>8</b>	<b>9</b>	<b>10</b>	<b>7</b>			

A = ABSENT  
 P = PRESENT  
 NM = NO MEMBER APPOINTED  
 OC = OUT OF COUNTRY  
 OT = OUT OF TOWN on Business

Prepared by City of Tulsa  
 Department of Finance  
 Budget & Planning Division  
 Capital Planning Section

# Tulsa Economic Development Project

**Attendees:**

Kathy Sebert  
Pamela Amburgy  
Scott Grizzle  
Paul Hassink  
Matt Meyer  
Linda Jenkins  
Steve King



**DATE:** April 19, 2023  
**TO:** STOC Committee  
**FROM:** Mary Kell, AIA, Engineering Services Department  
**SUBJECT:** **VISION TULSA STOC PROJECT UPDATES**

**Projects list**

1. 170000 Zink Dam
2. 147200 Arkansas River Pedestrian Bridge
3. 170010 Turkey Mountain Urban Wilderness
4. 170020 New Trail East Bank Cousins
5. 170025 23rd & Jackson Redevelopment
6. 170030 Gilcrease Museum
7. 170035 Cox Business Center Renovation
8. 170045.2 Airport Infrastructure – Spirit
9. 170045.4 Airport Infrastructure – American Airlines
10. 170050 Tulsa Zoo Elephant Exhibit
11. 170055 Langston Healthcare
12. 170060 BMX National Headquarters
13. 170065 South Mingo Corridor
14. 170070 Public Schools Safety First Initiative
15. 170080 Citywide: Commercial Revitalization
16. 170080 Citywide: Route 66
17. 170085 Peoria-Mohawk Business Park
18. 170100 Air National Guard MTC
19. 170145 Tulsa Arts Commission

**Completed Projects**

170035	Cox Arena District	January 2019
170040	Tulsa Fairgrounds	November 2021
170045.1	Airport Infrastructure – AA Tail Slot	January 2019
170045.2	Airport Infrastructure – Navistar	December 2021
170095	Community Health East Clinic	April 2020
170110	North Peoria Connection, 56 <sup>th</sup> – Mohawk	March 2020
170115	TCC Career Placement	August 2019
170125	McCullough Park	February 2023
170130	Mohawk Sports Complex	March 2022
170135	GO plan Bike Ped Master Plan	March 2022
170140	Route 66 Train Depot	October 2022
170155	PAC Master Plan	June 2021

**1. No. 170000**

Project Name: Zink Dam  
 Representative: Brooke Caviness, COT  
 Total Funding: \$54,673,411.53  
 Available Funding: \$54,673,411.53  
 Design Firm(s): Jacobs/CH2MHill, HISINC, LLC  
 Contractor: Crossland Construction Company  
 Start Date: 10.18.2020  
 Anticipated Completion: July 2023 (Mid – 2024 with east bank)

- Construction **85.5%** billed, **80.6%** time as of **03.28.23**
- Dam **construction - bay 12 excavation started 04.03.23, bay 10 concrete scheduled for 05.01.23**
- East bank electrical light poles near complete 03.09.23
- Entrance gate grouted core rock ongoing 03.09.23
- Sculpted concrete for drops began November 2022
  - Drop 1 – setting core rock and boulders **ongoing 03.23.23**
  - Drop 2 – **concrete to be complete about 04.14.23**
  - Drop 3 and 4 – **concrete complete, partially painted**
  - Drop 5, 6 and 7 – **concrete complete, awaiting paint 04.03.23**
  - Hydraulic vault concrete construction **started 04.03.23**
- For safety and work / laydown area, no public access to flume area during construction. Construction of the east bank and bumpout is anticipated to be complete mid-2024.
- Operations and maintenance planning ongoing included elected officials, RPA, Government staff and stakeholders. Bi-weekly meetings began week of 01.31.22.
- **Program and operation meetings underway, Last meeting 04.05.23, Focus working groups defined to cover construction , operations, recreational programming and communications / amenities.**
- **Grand opening planned for Labor Day 2024 PENDING**

**2. Project No. 147200**

Project Name: Arkansas River Pedestrian Bridge  
 Representative: Jeff Stava, RPA/TGP and Brooke Caviness, COT  
 Total Funding: \$27,400,000.00  
 Available Funding: \$27,400,000.00  
 Design Firm(s): SBP, MVVA, GKFF, and River Parks  
 Contractor: Crossland Construction Company  
 Start Date: 05.14.2021  
 Anticipated Completion: Summer / Fall 2023

- Tier III Funding - \$7.25 million in funding and donations committed
- Construction **86.34%** billed (**\$27,429,023.51**) of \$31,769,504.00 as of **04.13.23**
- **Exposed agg on the final span ongoing. All other spans are complete.**
- Decking & handrails
  - **Handrail welds to begin after the exposed agg is complete. Most of the replacement parts are on hand for the re-design**
  - **Landscaping sub will be back onsite and complete with the west bank in May 2023.**



- Handrails to be painted steel
- **Lighting conduit and fixture brackets installed. Lights to be powered and tested over the next month.**
- **CCC creating punch list for the east half of the Bridge.**

**3. Project No. 170020**

Project Name: Turkey Mountain Urban Wilderness  
 Representative: Ryan Howell, RPA (River Parks Authority)  
 Total Funding: \$ 7,600,000.00  
 Available Funding: \$ 7,600,000.00  
 Design Firm(s): LandPlan Consultants, Inc (LPCI)  
 Contractor: TBD  
 Start Date: TBD

- Acquisition of property: \$5,490,928.25
- Turkey Mountain Master Plan components: \$2,109,071.75
  - 71<sup>st</sup> Street to Turkey Mountain Trail Improvements final review set submitted 01.13.23
  - **Sent small changes back to engineer, Bidding projected for May 2023.**
- RPA has trail maintenance projects underway. New and old trail alignments to address erosion and clearing, ongoing.
- Wayfinding Signage installation has started. \$27,068 for 6x6 posts and \$6,438.98 for rental equipment related to posts has been spent to date.
- Negotiations underway with ODOT on land acquisition for portions of the westerly 2 Placerder properties (City owns). No impact on Mitchell Park exchange parcel.
- ODOT final land boundary has been defined and price offer will be finalized.
- Funding received from ODOT from land sale will reimburse the Vision Tulsa funding for RPA.
- A subsequent amendment will be entered into with RPA to fund Turkey Mountain improvements.

**4. Project No. 170020**

Project Name: New Trail East Bank 101<sup>st</sup> to Cousins Park  
 Representative: Doug Helt and Nancy Doutey, COT  
 Total Funding: \$ 4,000,000.00  
 Available Funding: \$ 600,000.00  
 Design Firm(s): LandPlan Consultants, Inc (LPCI)  
 Contractor: TBD  
 Start Date: TBD

- Conceptual design completed 02.16.2018 (\$68,454.00)
- Conceptual cost estimate for trail \$10.2 million, with time value at 3% for 13 years - \$15.0 million, with land, total cost is \$26 million.
- TAP (Transportation Alternative Program) grant awarded March 2021 through INCOG to fund design (\$133,991.00 requested, \$107,193.00 awarded) for Riverside Drive (Vensel Creek to south of Creek Turnpike)



- Consultant interviews with COT and ODOT held week of 04.07.22, Land Plan has been selected as design consultant for Vensel Creek design plans only (does not include construction funding).
- Land Plan scoping agreement ODOT LG 2360 for further processing.
- TA (Transportation Alternative) grant applications: 3 additional segments to Cousin's Park were on Mayor's agenda for 01.04.23, no information on award
- Trail segments will be coordinated with the South Tulsa – Jenks Dam project – **ongoing**
- **Mayor provided letter to affirm City matching funds - ongoing**

**5. Project No. 170025**

Project Name: 23<sup>rd</sup> & Jackson Redevelopment Site – Relocation Study Design and Acquisition  
 Representative: Marsha Hinds, COT  
 Total Funding: \$1,000,000.00  
 Available Funding: \$1,000,000.00  
 Design Firm(s): Cyntergy

- Scope includes planning, design work and partial acquisition costs to relocate Public Works, update master plan site at Harvard and Mohawk, appraise and acquire operation yard location.
- Draft report submitted to Administration, February 2020
- Acquisition of 2 parcels – Tulsa County Yard on North Harvard - \$320K (Vision funding), 56<sup>th</sup> & Garnett - \$1.46 million (water enterprise funds) – closing for both 08.30.2020
- Traffic Engineering is now occupying County site on North Harvard Avenue
- Amendment with consultant **to be resubmitted once direction is known** (originally recommended at 09.01.21 PCSSC).
  - Will include development of a phased transition plan for Water Distribution to move to 56<sup>th</sup> & Garnett site, and review of the Pine Street site as a possible location for Water Distribution.
  - On hold for Mayor's staff review of original report. Phase 1 and 2 environmental reports provided to Mayor's office for review. Last update received 08.01.22. **NO UPDATE**

**6. Project No. 170030**

Project Name: Gilcrease Museum  
 Representative: Susan Neal, Gilcrease, Mary Kell, COT  
 Current Budget: \$139,215,850.00  
 Total Funding: \$118,691,429.00  
 Fundraising Goal: \$ 20,524,151.00  
 Design Firm(s): Smith Group, 1 Architecture; Gallagher & Associates  
 Construction Manager: Flintco, LLC  
 Start Date: 05.10.22  
 Scheduled Completion: 11.30.2024  
 Anticipated Completion: 11.30.2024

- Funding:
  - Public Funding total: Vision (\$65 M), Remaining bond funds from past Gilcrease projects (\$2.6 M), IOT 2 (\$6 M), ARPA City Funding (\$1 M), Public





Utilities (\$817,113.00), Supplemental Appropriations (\$6.1M) 03.01.23 = \$81,517,113

- Private Funding total (\$37,174,586.00) = \$118,691,429.00
- Mayor's Task Force **meeting held 03.23.23, next is a site tour on 04.27.23.**
- Stair 1 complete, Stair 2 and waterproofing **ongoing**
- **Level 2 patio deck poured 04.17.23**
- **Interior CMU at CUP (Central Utility Plant) is ongoing**
- **Stair 2 in progress (LL1 to L1)**
- **STOC tours on 05.23.23 and 06.13.23**
- Construction update from **04.14.23** attached at end of report
- Jobsite camera link: <https://www.cityoftulsa.org/government/capital-programs/vision-tulsa/vision-projects/gilcrease-museum/>
- Fundraising goal as of as of 03.01.23 is \$20,524,151 - **ongoing.**
- **Mayor has proposed a \$10 million fundraising match in the IOT 3 program presented to City Council 03.22.23.**
- **IOT 3 Town Halls set for 04.24.23, 04.25.23 and 05.01.23**

**7. Project No. 170035**

Project Name: Cox Business Convention Center  
 Representative: Mary Kell, COT  
 Total Funding: \$ 54,500,000.00  
 Available Funding: \$ 54,500,000.00  
 Design Firm(s): Matrix Architects, Engineers and Planners, Inc., FFTT  
 Construction Manager: Tulsa Vision Builders  
 Start Date: 07.01.2018  
 Completion: 06.30.2020

- Concrete cracking repairs in front of main entrance: **concrete pours on 04.13.23 and 04.14.23, curing in process.**

**8. Project No. 170045**

Project Name: Airport Infrastructure – Spirit  
 Representative: Chris Gimmel, COT  
 Total Funding: \$ 5,000,000.00  
 Available Funding: \$ 5,000,000.00  
 Design Firm(s): Poe  
 Contractor: Grade Line Construction, LLC  
 Start Date: 02.13.23 (for TMUA-W 21-08)  
 Completion Date: TBD

- Paving Phases 1 and 2 (Areas 1,2 ,3 4, 5, 6A & 6B, and 9) completed 12.31.2020
- South parking area parking and parking completed 03.08.22.
- Approximately \$300K remaining in budget for Fire Line extension / elements, control valves and fire hydrant replacements.
- TMUA-W 21-08 contract executed 10.26.22, second pre-work held 02.07.23, security badges received.
- Potholing **started 03.16.23, issue with utility location. Schedule to be provided by contractor by 04.30.23.**

**9. Project No. 170045**

Project Name: Airport Infrastructure – AA (American Airlines)  
 Representative: Mary Kell, COT  
 Total Funding: \$ 14,500,000.00  
 Available Funding: \$ 14,500,000.00  
 Design Firm(s): FSB, Allana Buick & Bers Inc.  
 Contractor (s): The Ross Group Corp  
 Start Date: 12.02.2020  
 Anticipated Completion: TBD

- Agreement with list of projects signed by Mayor 12.02.2020
- Projects:
  - Tail Slot: \$ 2,122,396.00 completed 01.08.2019
  - Hangar 80 Re-Skin: \$ 1,500,000.00 99.8% billed
  - AAERO APU: \$ 2,012,277.00 98.5% billed
  - Master Plan \$ 575,000.00 72.4% billed
  - Plating Shop Roof, MAU \$ 2,405,000.00 100% billed
  - CUP Cooling Tower & Hangar 6 Cooling Tower \$ 5,757,723.00 100% billed

Total billed: \$14,181,548.24 – overall 98.4% (most recent invoices received 01.26.23)

**10. Project No. 170050**

Project Name: Tulsa Zoo Elephant Exhibit  
 Representative: Lindsay Hutchinson, TZMI, Gary Schellhorn, COT  
 Total Funding: \$ 25,000,000.00  
 Available Funding: \$ 22,000,000.00  
 Design Firm(s): Selser Schaefer Architects  
 Construction Manager: Nabholz Construction  
 Start Date: 04.04.22  
 Scheduled Completion: TBD  
 Anticipated Completion: TBD

- Current construction budget is \$32 million.
- \$20M of \$25M was previously allocated for Elephants with remaining \$5M originally allocated for front entrance.
- TZMI has requested \$2M of remaining \$5M to go towards Elephants, TZMI will fund remaining \$10.1M for Elephants.
- VE in process to reduce overage that TZMI will fund, \$1M goal **ongoing**
- Revised landscape bids **opened 03.30.23**
- IOT (Improve our Tulsa) 2 to provide \$6M to front entrance in FY25 / FY26.
- Amendment with Nabholz for remaining construction funding identified in the Interlocal agreement **processing**
- Construction of the Elephant Barn:
  - Concrete tilt-up panels and structural steel **complete**
  - Underground utilities, concrete slab of barn **ongoing**
  - Site grading scheduled to start May 2023**



- Preparation for metal cagework in coordination with supplier for operating hydraulic and electrical systems **ongoing**

**11. Project No. 170055**

Project Name: Langston Healthcare Professions Complex  
 Representative: Blake Allen, Flintco, Phil Thomas & Kirby Crain, OSU-LRFP  
 Total Funding: \$ 16,250,000.00  
 Available Funding: \$ 16,250,000.00  
 Design Firm(s): Beck  
 Construction Manager: Flintco, LLC  
 Start Date: 06.01.2020  
 Scheduled Completion: 11.30.2021  
 Anticipated Completion: 11.30.2021 (Spring 2023 with all amenities)

- OSU - LRFP (Long Range Facilities Planning) providing project oversight
- Certificate of Occupancy received week of 12.21.21
- Final IT installations started 02.03.23, will take 6 or so weeks to complete (by end of **April 2023**).
- Ribbon cutting 03.29.23
- Existing rooftop HVAC equipment replacement – **delivered** 04.07.23, coordinating a week for install with Langston, **May 2023**

**12. Project No. 170060**

Project Name: BMX National Headquarters  
 Representative: Ryan O’Neil, Nabholz, Shane Fernandez, BMX  
 Total Funding: \$ 23,000,000.00  
 Available Funding: \$ 23,000,000.00  
 Design Firm(s): Todd Architecture Group  
 Construction Manager: Nabholz Construction  
 Start Date: 06.01.2020  
 Scheduled Completion: 12.09.2021  
 Anticipated Completion: Spring 2022 / Fall 2022

- Funding - Vision (\$15 M), TPA (\$2 M), Hardesty (\$1.5 M), UCAT Vision (\$3.6 M) EDIF (\$900 K) = \$23 M total
- Overall construction 99% billed
- Leasehold with BMX began 03.01.22.
- Closeouts complete 02.23.23
- Platting ongoing. Rezoning of full site expected by April 2023, plat to be filed after rezoning is complete. TCO (Temporary Certificate of Occupancy) to remain in place until plat is finalized. Awaiting MPD (Master Planned Development) ordinance to be submitted. Site platting documents to be revised as MPD-5 with MPD standards.
- Fence between BMX and Evans site with emergency access behind Evans building **installed 03.23.23**.
- Concrete approach to be completed by Spring 2023, weather dependent, **survey of pad to be scheduled**.

**13. Project No. 170065**

Project Name: South Mingo Corridor  
 Representative: Patty Parks, COT



**MEMORANDUM**  
**ENGINEERING SERVICES DEPARTMENT**

Total Funding: \$ 15,000,000.00  
 Available Funding: \$ 15,000,000.00  
 Design Firm(s): Benham Design, LLC (170065), Garver (170065A), Poe (170065B)  
 Contractor: APAC Oklahoma (170065)  
 Start Date: 08.19.2019 (First Phase, 71<sup>st</sup> to 81<sup>st</sup> on Mingo)  
 Scheduled Completion: 10.27.2020  
 Completion: 07.28.22 (First Phase, 71<sup>st</sup> to 81<sup>st</sup> on Mingo)

- First Phase: 71<sup>st</sup> to 81<sup>st</sup> on Mingo (Project 170065)
- Project final payments to consultant and contractor complete as of 01.31.23
- Second Phase: 91<sup>st</sup> from Mingo to Memorial (Project 170065A)
- Garver is consultant
- 404 permit submitted to USACE on 10.11.21, will get 404 permit before project goes out to bid. Preliminary 404 mitigation cost is approximately \$1.1M
- NWP (Nationwide Permit) approved by USACE 09.12.22, valid until 03.14.26.
- Honey Springs Mitigation Bank credit cost \$973,706.50, agreement signed 12.14.22
- Construction funding in Improve Our Tulsa 2 - \$10.7 million
- Right-of-way: 2 of 16 closed, 13 in negotiations and 1 is pending. Potholing for ONG is pending. **ongoing**
- Projected construction starts: Fall/ Winter 2023 - **ongoing**
- Third Phase: 81<sup>st</sup> to 91<sup>st</sup> on Mingo (Project 170065B)
- Poe is consultant, Contract fulfilled at 60% plans: contract complete 09.01.2020
- Estimated construction cost is \$ 9 M, does not include ROW or utilities
- Construction funding in 2026 (earliest). Design to be completed at a later date.

**14. Project No. 170070**

Project Name: Public Schools Safety First Initiative  
 Representative: **Chris Gimmel, COT**  
 Total Funding: \$ 14,500,000.00  
 Available Funding: \$ 14,500,000.00  
 Design Firm(s): Lee Engineering, LLC  
 Contractor: R & L Construction (Bid package 4)  
 Start Date: TBD  
 Scheduled Completion: TBD

- Bid package 1, 2 and 3 – complete
- Bid package 4
  - Project consists of signing, pavement marking, sidewalks, drainage improvements, pavement, lighting, and traffic signal improvements at Priority 3, 4, and 5 schools.
  - Plans also include bus shelter construction at Priority 1-5 schools.
  - Bids received 10.28.22. Change Order to reduce number of site and/or scope of work to fit within budget. TPS defined scope reductions to fit within existing funding. Bid award on Mayor’s agenda 01.04.23, contractor is R & L Construction.
  - Pre-work held 02.07.23
  - **Striping has started at Sequoyah, signage ordered but delayed in receiving**

**15. Project No. 170080**

Project Name: Citywide Commercial Revitalization  
 Representative: Jonah Toay, Partner Tulsa  
 Total Funding: \$ 3,600,000.00  
 Available Funding: \$ 1,454,393.39 remaining (as of June 2022)  
 Design Firm(s): Place Dynamics, Inc., Medium Giant

- Retail Market Study by Place Dynamic, Inc. (\$125K) completed January 2019
  - will inform use of Commercial Revitalization fund, as well as assist Route 66 Commission in targeting Route 66 funds
- Project 1: \$100K – Medium Giant media strategy consultant
- Launch of a \$150K - \$300K marketing campaign paused until Partner Tulsa hires a Director of Retail Recruitment.
  - Once hired, this person will take a comprehensive look at commercial revitalization efforts and the use of remaining funds – planning to have Director hired by **Spring 2023 as candidates can be found**
- Project 2: \$1.1 million from Commercial Revitalization used to seed Business Resilience and Recovery Fund, reimbursement from CARES act dollars is expected to fully fund the Commercial Revitalization Strategy.
- All funds disbursed
- City has received \$509,232.38 as of 07.12.22 in repayments
- Project 3: \$1.5 million BRT (Bus Rapid Transit) Revolving Loan Fund
- TEDC is evaluating projects for program and providing low to zero interest loans
  - TEDC approved a loan of \$210K loan to Rise and Develop
  - Working on policy updates to expand availability of loans – these policy changes to be advanced through Council in 2023 as part of a comprehensive update to incentive policies. **ongoing**
- Project 4: \$150K (3 years x \$50K) 4 Destination Districts – INCOG administering: Greenwood, Route 66, Kendall Whittier, and Global District (formerly International District) (21<sup>st</sup> & Garnett area).

**16. Project No. 170080**

Project Name: Route 66 Beautification & Reinvestment  
 Representative: Dennis Whitaker, INCOG  
 Total Funding: \$ 3,700,000.00  
 Available Funding: \$ 3,700,000.00  
 Design Firm(s): INCOG staff

- Route 66 Commission and Tulsa Planning Office (INCOG) staff providing oversight
- Retail Market Study informed targeted funding uses on corridor
- Uses include marketing, wayfinding, façade grants, neon sign grants and project maintenance.
- **56** neon sign grants in various stages of contracting through installation:  
Total for neon signs: \$ **717,243.29** total costs \$ **327,881.64** total grants.
- “Shop Saturday” monthly event continues **ongoing**
- Special Event Grant Draft – Press conference held 01.10.23 to launch the program some inquiries, no applications yet
- An inaugural event for a casual Route 66 bike ride to be rescheduled for 2023



- Legal department pursuing a trademark designation for Tulsa as, “Capital of Route 66”. **Ongoing**
- OK Tourism and ODOT created a standard statewide historic Route 66 marker sign. Tulsa is preparing to implement the signage along the local alignments. Final documents for bid being prepared. Ongoing, approximately 125 locations planned.
- YMCA of Greater Tulsa submitted neon sign grant applications for co-located facilities at East Central High School and the downtown campus of TCC.
- Neon sign grant requires applicant to be property owner(s) or commercial lessee(s). If a lessee, the Application must include the property owner(s) signature on the Application.
- RFP for Marketing being routed for **final review**
- Meadow Gold sign upgrades and repairs **complete**
- **Preparations for the 2023 AAA Road Fest 06.24.23 participation are underway**

**17. Project No. 170085**

Project Name: Peoria-Mohawk Business Park  
 Representative: Chris Gimmel, COT  
 Total Funding: \$ 10,000,000.00  
 Available Funding: \$ 10,000,000.00  
 Design Firm(s): Cedar Creek (no Vision funding)  
 Contractor: Crossland Heavy  
 Start Date: 10.22.2020 (Bid package 3)  
 Scheduled Completion: 10.31.2021  
 Completion: 05.15.22 (packages 1, 2 and 3).

- Bid package 1 – mass grading with earth change permit – completed 04.30.2020
- Bid package 2 – public road and site utilities – completed 09.30.2020
- Bid package 3 – scope is water line, paving, storm and sidewalks / trail for Mohawk Blvd and the Utica cul-de-sac off 36<sup>th</sup> street North
- Crossland change order for time additional work (fencing, sidewalk, retaining walk etc.) \$31K and time given for weather and repair of 30-inch waterline by others. Completed 05.15.22.
- Ribbon cutting for Muncie to be scheduled, delayed due to supply chain issues, want facility to be fully operational before schedule **ongoing**
- 61.4% of \$10 million has been expended towards this set of projects.
- Future projects may include extension of Utica, grading, infrastructure, and other public utilities. **No update**

**18. Project No. 170100**

Project Name: Air National Guard 138FW MTC (Mission Training Center)  
 Representative: Mary Kell, COT  
 Total Funding: \$ 9,400,000.00  
 Available Funding: \$ 9,400,000.00  
 Design Firm(s): LWPB Architects  
 Construction Manager: Crossland Construction Company, Inc.  
 Start Date: 07.01.2018  
 Scheduled Completion: 07.01.2020 (Building operational)  
 Completion: 01.31.2021





- Artist Agreement **executed 03.23.23**
- MOU between TAIT, City and TASM **executed 04.05.23**
- TCAA (Tenant Construction or Alternation Application) – **application permit draft underway with artist.**

**19. Project No. 170145**

Project Name:	Tulsa Arts Commission
Representative:	Roshita Taylor, INCOG
Total Funding:	\$ 2,250,000.00
Available Funding:	\$ 900,000.00

- 1<sup>st</sup> round of artist grants totaling \$300K, 29 agreements signed by Mayor 09.02.2020
- 2<sup>nd</sup> round of grants totaling \$300K, 33 agreements approved by Mayor 03.03.2021.
- 3<sup>rd</sup> round of grants totaling \$150K, 12 agreements approved by Mayor 06.08.2022
  - 11 of the 12 contracts have been executed
- 4<sup>th</sup> round of grants totaling \$150K opened to artists on 10.01.22
  - Vision Arts 4 was approved by City Council on 08.03.22
  - The submission period is 10.01.22 through 01.23.23
  - The funding period is from 07.01.2023 to 06.30.2024
  - Workshops held 10.12.22, 10.28.22 and 11.07.22 and 12.10.22
  - Tulsa Planning Office reviewed applications for those that are not eligible based on requirements, 01.23.23 through 01.27.23
  - Panel made final recommendations to Arts Commission 03.03.23
  - Arts Commission to review recommendations and **voted 03.13.23.**
  - **Awardees sent to the Mayor's Office for approval on 03.16.23.**
  - **The Mayor signed off on the recommendation on 03.22.23.**
  - **Notifications sent to the awardees on 04.05.23.**
  - **Public announcements to be made by 04.30.23**



# Issue #39 | April 17th, 2023 Vision Tulsa Gilcrease Museum



**GILCREASE MUSEUM**  
*Thomas Gilcrease Institute of American History and Art*

## *Weekly Construction Update*



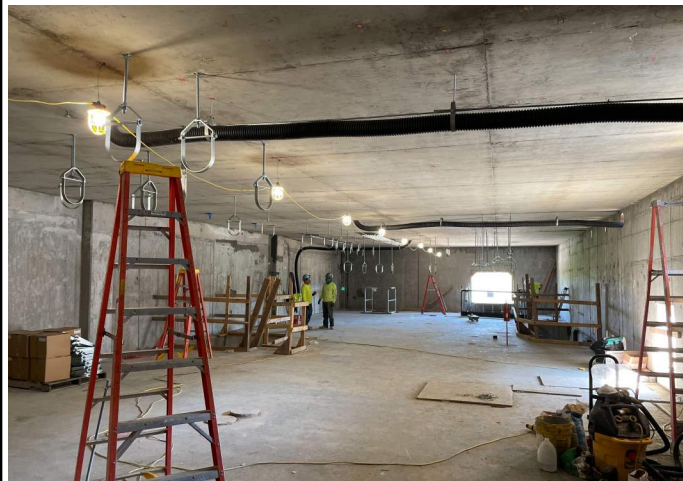
Overall main building view




L2 Patio deck is in place. Fall protection anchors are also in place as shown.



Interior CMU is in progress in the CUP.



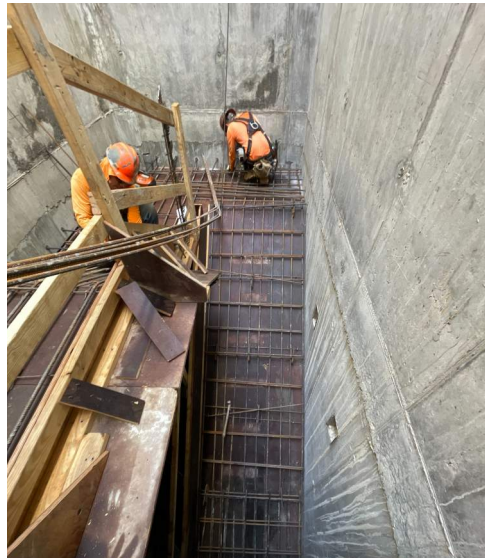Overhead MEP pipe and rack are in progress in LL3, LL2, & LL1.



Stair #2 is currently in progress.



Cooling tower walls are now in place. Parapet CMU wall at cooling tower to follow.





Issue #39 | April 17th, 2023  
 Vision Tulsa Gilcrease Museum



**GILCREASE MUSEUM**  
*Thomas Gilcrease Institute of American History and Art*

***Weekly Construction Update***

**Site Aerial View**



(Drone: 04/17/23)

**Upcoming Work**

- Continue Freestanding Mock Up Construction
- Continue to Shore, Prep, & Place L2 Main Deck
- Continue Hanging Pipe and Rack for MEP
- Continue Below-Grade CMU for Stone Veneer Foundation
- Continue Interior CMU Placement
- Begin Exterior CMU Placement
- Begin Structural Steel Erection
- Begin Entry Canopy Truss Erection
- Install Post-Tension System in L2 Elevated Deck
- Form, Prep, & Install Amphitheater Site Foundation Walls

# Public Safety and Economic Development

**Attendees:**

Kathy Sebert  
Steve King  
Ashley Webb  
Paul Hassink



**Report  
To  
Sales Tax Overview Committee  
On  
Public Safety, Urban Development  
and Equipment**

TO: Public Safety, Urban Development and Equipment Subcommittee  
Sales Tax Overview Committee

SUBMITTED BY: Marsha Hinds, Lead Engineer  
Special Projects Design, Engineering Services Department

DATE: **April 13, 2023**

The status of projects managed by the Special Projects Design section of the Engineering Services Department as of **April 13, 2023** is as follows:

2006 Sales Tax (6009)

Project No. 067520 and 040430-7, Route 66 Xperience, TAC 1011  
Budget \$5,000,000

Project Description: Interactive Route 66 Interpretive Center located at the southeast corner of Riverside Drive and Southwest Blvd.

Status: This project is now under the Mayor's office purview.  
**Deputy Mayor Cassia Carr is lead for this project.**

The Standards, Specifications & Award Committee accepted the Mayor's recommendation on May 5<sup>th</sup> for the Sharp Development proposal. This begins a process to negotiate a development agreement. This is a fluid process with various components to consider. There are several preliminary steps leading into the process also, so no timeline is initially prescribed until variables are better defined. The discussions are still ongoing with Sharp Development, they are revising their Performa.

Project No. 065100, Contract 32, Misc. Electrical / Mechanical Services Citywide

Consultant: Cyntergy

Status: \$25K agreement executed.

Project No. 065100, Contract 31, Misc. Structural Engineering Services Citywide

Consultant: Wallace Engineering – Structural Consultants, Inc.

Status: The consultant is providing services as requested by the City.  
**Used \$514.5K out of the \$617.5K agreement.**

## 2014 Improve Our Tulsa (6014)

### Project No. 145100, ADA Transition Plan – Building

Project Description: Improve accessibility for disabled citizens at various identified City facilities by improving to Americans with Disabilities Act (ADA) standards.

The 2016 Transition Plan Study included the following sites: Municipal / Police Courts, BOK Center, Tulsa City Hall, 23<sup>rd</sup> and Jackson Facilities, Tulsa Zoo, and Nature Center Maxwell Convention Center = The Maxwell Convention Center items were taken care of in the Vision Tulsa Cox Business Center project.

Animal Shelter = The Animal Shelter items will be taken care of in the Improve Our Tulsa Animal Shelter expansion project.

Performing Arts Center = Performing Arts Center items were taken care of in the Improve Our Tulsa PAC renovations project.

Gilcrease Museum = The Gilcrease Museum items will no longer be valid with the new building.

Police- Gilcrease Division = The Police -Gilcrease Division some items will be addressed in the upcoming renovation project.

Authorized \$100K at each of the 3 Police Uniform Divisions. These funds are being incorporated into project 146120.

Status: 911 Center and Forensics Lab requests complete.

Consultant: TODD Architecture Group: GH2

Total Appropriations: \$1,275,000, Balance: \$625K

Held a kick-off meeting with Todd Architecture to restart the design and implementation for additional ADA facility projects on 4/27/22. Site visited Police Courts building 5/23/22, next location to be addressed. Design agreement executed, with Todd Architecture for the Police Courts design, consultant working.

Received preliminary plans 11/30/22, transmitted to reviewers.

City plan review meeting held 12/14/22. We have hired a new Engineer in Special Projects he will be assuming the Project Manger role for this project. A project review meeting was held on 2/2/23 at which we introduced our new PM and discussed various design options. Consultant continues design work. Site walk scheduled for 3/10/23 to go over the designs with the user groups. **OTC site walk was held 4/10/23 reviewed existing conditions and space usage. Consultant is reviewing details for code compliance. The Police Courts and OTC ADA projects will be bid as one package.**

Special Projects staff working with Engineering Services Planning section and their consultant on an update to the City of Tulsa Transition plan.

### Project No. 145200, ADA Transition Plan – Parks

Project Description: Improve accessibility for disabled citizens at various identified City parks by improving to Americans with Disabilities Act (ADA) standards.

Total Appropriations: \$1,140,000. Balance \$166K

McIntosh agreement for Hunter Park was executed on 11/2/22. Kick off meeting was held 11/7/22, site visit 11/8/22. We have hired a new Engineer in Special Projects he will be assuming the Project Manger role for this project. A review meeting was held on 1/20/23 at which we introduced our new PM and discussed various design options. Consultant working on survey and preliminary plans. Scheduling a project update meeting for late March. **Received plans early April, staff reviewing.**

Project No. 145300, Public Facilities – OTC City Hall

Total Appropriations: \$3,295,000. Balance \$1.52M

New design agreement with Todd Architecture has been executed for the solar stairwell re-carpet project SP 22-11. Purchasing has put out an Invitation for Sealed bids for the OTC Solar Stairwell Carpet Replacement IFB23-426. **The bids opened 3/15/23. Proceeding with awarding the bid for base bid only, in the amount of \$160,905.68, with L&M Office Furniture, LLC.**

Project No. 145400, Public Facilities – Roofing

Project Description: Inspection, assessment, prioritization, and repairs of roofing for various City facilities.

Consultants: Cyntergy, LLC & SGA Design Group, PC

Total Appropriations: \$3,000,000. Balance \$8K

Status: Combined FS #23 and #25 into one project.

Location	Project #	Status	Consultant	Funding Source
EMF Roof (Electronics Maintenance Facility)	SP 17-05	<b>Construction Contract Executed, pre-construction meeting held 3/20/23. Lowry Construction contract amount \$1,089,999.67 funding sources IOT 1 &amp; 2.</b>	SGA	<b>IOT-1 (145400) and IOT-2 (2234B00006) Facilities Roofing</b>
Lacy Rec. Center	SP 21-2	Contractor: American Roofing Construction. <b>Contract amount \$481,100.00.</b> Construction review walk was held 3/7/23	SGA	<b>TIF (7239000)</b>
TFD Station #23 & #25	SP 17-17 & SP 17-18	<b>Bids opened 3/17/23. Apparent low bidder Sooner Recon, processing Award of Bid, in the amount of \$708,135.00.</b>	Cyntergy	<b>IOT-2 (2234B00006) Facilities Roofing and IOT-2 (2234B00024) Public Facilities Rehab</b>
Mohawk Admin Bldg	SP 22-15	<b>Advertising, bids open 5/5/23</b>	SGA	<b>TMUA</b>

Project No. SP 16-1-1453XX, PAC Renovations

Consultant: Matrix

Project Description: Combined Project 145350; PAC Renovations, 145340; PAC Fire sprinklers, 145360; PAC Fan coil replacement and 145370; PAC HVAC motor replacement into one design agreement.

Contractor: CEI (Contract # 33312)

Contract Amount: \$1,861,694.12

The City has filed suit. City of Tulsa has been served with discovery requests.

A mediation meeting was held 6/30/22. An updated listing of incomplete and or re-do tasks is being compiled by the City to transmit to the mediator by July 15, 2022. Ultimately CEI will go back on site to finish the contract. Negotiating scope of work. **Case No. CJ-2020-2561. One year deadline is July 8, 2023 date case was dismissed.**

Project No. SP 21-1, PAC Renovations, Phase 2

Consultant: Beck Associates Architects

Project Description: Williams Theater stage floor replacement.

Contractor: Lowry Construction

Contract Amount: \$482,985.70

Status: Construction Contract executed 12/14/22.

The window for construction at the Williams Theater is July 2023.

Part 2: Renovations to office spaces.

Status: Consultant completed plans. **MyIars signed, preparing to Advertise.**

Project No. 145500, Animal Shelter Expansion, Phase I

Consultant: GH2

Project Description: Renovation and expansion, adding a new Adoptive Center and support areas.

Budget: \$ 4,784,552.29 (2014 IOT, 2019 IOT and residual from 145600)

Additional funding was received Balance \$8,306,490.59

Construction Manager At Risk: Timberlake Construction

Status: City Council approved \$2.5M ARPA funds. Tulsa County possible \$0.9M ARPA

March 2022 cost estimate increased an additional 1.9M over July 2021 prices. 4/21/22 reboot meeting with user group, consultant and construction management company.

Consultant and CM reviewed the bid proposal for price stability. Comparisons of March 2022 to May 2022 very similar. Mayor's office reviewing funding needs.

Moving forward with the 36<sup>th</sup> Street North and west of Sheridan location. The Zoo has voiced concerns. A meeting with the Zoo has been scheduled for 2/22/23. Our consultant has hired an Infectious Diseases Veterinarian to determine best practices for the site.

The best practice meeting was held, attendees included Zoo representatives,

Consultant representatives, Animal Welfare representatives, Engineering

representatives and the Mayor. We are moving forward with the site. **Consultant interviewing the Animal Welfare staff.**

Project No. 146110, Police Academy Renovation/Police Courts/Compstat Bldg

Project Description: Phase II: Police Courts and Compstat Bldg items to be worked on elevators, building envelope i.e. roof

Budget \$4.04M, Balance \$1.105M

Status: Facilities Maintenance is scheduling the following upgrades for the Police Courts and CompStat buildings:

Elevator work complete. Additional Jail elevator 'control' work performed.

HVAC renovations which include but not limited to upgrading coils, valves and DD controls,

Plumbing upgrades-replacing galvanized pipe with pex,

Interior and Exterior lighting. Facility maintenance is working with a contractor on an exterior lighting layout and quote. Contractor has begun exterior lighting project.

Project No. 146120, Tulsa Police Department, Uniform Divisions Renovations

Project Description: To renovate police facilities to improve efficiency of divisional operations in existing facilities.

Budget: \$3M plus \$300K ADA

Balance: \$2.609M plus the \$300K

Consultant:BKL

Status: Consultant has been working on plans.

New Division Commanders; presented plans to the new Division Commanders. The new Commanders reviewed and made comment of plans. Consultant is addressing the new Commanders inquiries and comments. Preparing to advertise this project.

Project No. 146240, Tulsa Fire Department Facilities

Project Description: Rehabilitate garage, training center, storage, and supply at 1760-1790 Newblock Park Drive, HVAC, and external building repairs.

Budget: \$2M, Balance: \$1.757M

Consultant: BKL

Status: Working with Stormwater Design on flooding issues.

Finalizing plans to advertise.

Project No. SP 16-10-1400XX, EMD Facilities Maintenance & Upgrades

Consultant: BKL, Inc.

Contractor: Voy Phase I Construction Contact complete.

Project #140070. Available Balance: \$144K

Project #140080. Available Balance: \$769K

Status: EMD has requested concrete work at the Newblock location. Concrete work complete.

Held a Teams meeting (8/20/2020) with EMD on additional work for various EMD sites.

EMD is preparing a priority listing for a future discussion meeting.

Held another Teams meeting (12-21-20) discussing project priorities.

Items Requested and Completed: concrete work requested at the Eastside Fuel Pump Island, West Yard Truck Wash repair.

Meeting to review status of requested work 2/10/2021.

Items Requested and Completed: Car Wash replacement at the Gilcrease Division, LED lighting at various locations, emergency generators at 470 and 480 West 23<sup>rd</sup> shops, painting 470/480/490 West 23<sup>rd</sup> shops, 56<sup>th</sup> and Garnett fueling island repairs, LED lights and LED glass cover replacements in the paint booth at 1790 Newblock, replacing compressor-shop air supply.



Held another Teams meeting 1/26/22 to discuss additional projects: generator replacement at Newblock was requested, moving forward to have Cyntergy prepare construction documents.

Purchase Order for the new generator has been processed and sent to the vendor.

5/12/22 EMD requested a new A/C unit for the 1720 Newblock Parts Room. Item was approved, writing a PO for the purchase and install.

EMD requested a new monitoring system for leakage protection of hydrocarbons. The request was approved and a PO is being prepared.

## **2019 Improve Our Tulsa**

Project No. SP21-5

Project No. 2234B00006

Project Description: Citywide Public Facilities-Roofs

Ordinance Amount \$2.46M, **Available \$0K of \$1M**

Consultant: GH2-Parks, Todd-Parks, BKL -TMUA, JCJ -TMUA projects

Contractor: Lowry

Contract Amount: \$616,909.30 of \$1,089,999.67 total contract for EMF roof

Construction status: Awaiting pre-construction meeting.

Design Status: Consultants working on assigned projects.

Project No. 2234B00007

Project Description: Animal Shelter Phase II,  
Combined with Project #145500 listed above.

Project No. 2234B00008

Project Description: One Technology Center-Maintenance & Rehabilitation

Ordinance Amount \$1M, **Available \$275K of \$300K**

Consultant: Wallace: Design and inspection fees thus far \$11K

Contractor: Impact

Contract Amount: Total contract amount \$110K, funds from this project no. \$10K

Status: Funds used for project SP 22-01, R2: OTC Parking Garage repairs.

Held final walk thru 2/23/23, no punch list, awaiting closeout documents.

Project No. 2234B00025

Project Description: ADA Improvements for City Facilities

Ordinance Amount \$5M, Available \$350K

Consultant:

Contractor:

Contract Amount:

Status: Construction money for designs from IOT-1

**The following project is funded by IOT-2 but no assignment or work has begun.**

Project No. 2234B00024

Project Description: CW- Public Facilities Rehab/Repair

Ordinance Amount \$7M, Available \$950K

Consultant:

Contractor:

Contract Amount:

Status: Facilities Maintenance is working with a Heat and Air company to review various sites for HVAC upgrades. Should improve efficiency and lower power consumption.

**The following projects have not received any funding yet.**

Project No. 2234B00028

Project Description: Police Courts Building

Ordinance Amount \$1M, Available \$0

Consultant:

Contractor:

Contract Amount:

Status:

Project No. 2234B00029

Project Description: 600 Civic Center-Equipment Relocation

Ordinance Amount \$200K, Available \$0

Consultant:

Contractor:

Contract Amount:

Status:

Project No. 2234B00027

Project Description: ADA Improvements for City Parks

Ordinance Amount \$3M, Available \$0

Consultant:

Contractor:

Contract Amount:

Status:

**Tulsa Fire Department  
Sales Tax/Bond Projects Report  
04/12/2023**

Mike Mallory  
Physical Resource Chief  
Office 918-596-1230  
Mobile 918-527-0262  
mmallory@cityoftulsa.org

**Command Vehicles**

Improve Our Tulsa funds

P.O. #220619 Car 642 Total less equipment for \$39,215.00

P.O. #220707 Car 835 Total less equipment for 35,453.50

- District Chief Car 642 at Station 22, 7303 East 15<sup>th</sup> Street
- Shift EMS Officer Car 835 Field Operations, Station 1, 1420 Charles Page

Both vehicles are receiving final communications equipment.

**Urban Search & Rescue Vehicles (Pickups)**

P.O. #220708 Improve Our Tulsa funds Total \$86,208.00

USAR #2 and #3 @ 2819 North New Haven

A purchase order has been issued and the first of the two Ford F350 crew cab, long box, 4x4 has been delivered. Efforts are now being made to prepare the vehicle for service as USAR 2. No new changes

**Four Specified Engines**

P.O. #220463 Improve Our Tulsa funds Total of \$3,636,115.60

Mobile routers are being installed into the apparatus and training should begin with fire companies beginning April 17<sup>th</sup>.

**Two Specified Ladders**

P.O. #220464 Improve Our Tulsa funds Total of \$2,975,905.94

Two 107-ft aerial ladders have been ordered. The apparatus will be identical in appearance and operation as the two ladders that were delivered earlier this year. The apparatus is likely to be delivered in November 2022. A preconstruction meeting was held here in Tulsa on April 6<sup>th</sup>. A few changes were made with the greatest being the addition of changing the rear axles to steer axles to increase maneuverability. The



into service in early February. Though it is currently designated as a reserve, it will likely be placed temporarily into service as Ladder 26 until the specified aerials arrive later this calendar year. The two remaining stock aerials are nearing completion and will be inspected at the manufacturing plant the week of February 12<sup>th</sup>. Awaiting receipt of generator, ground ladders, and MSO from Pierce and Conrad Fire Equipment for the first unit. Preparation for service will begin after the four Engines are finished and sent to Training.

**Technical Heavy Rescue**

Requisition 20232487

To be funded through SAFER funds.

Awaiting issuance of a P.O. Estimate \$2,006,959.45

Delivery expected 32 months from date of P.O.

**Extended Cab Air Trucks**

Requisition 20220688

Requisition is for two F-550 extended cab 4x4 mini-rescue body Air Trucks.

Awaiting issuance of a P.O. The estimate of the P.O. for quantity of two is \$689,858.66

Delivery expected 30 months from date of P.O.

A third Air Truck will likely be requisitioned in July of similar design but with a crew cab chassis for assignment to the HazMat team. The concept is that they could use the smaller truck for natural gas leaks and response to carbon monoxide alarms without the deployment of the large heavy rescue sized apparatus.



# **INTEROFFICE CORRESPONDENCE**

**TO:** Sales Tax Oversight Committee (STOC)  
**FROM:** Deputy Chief Dennis L. Larsen  
**DATE:** April 11, 2023  
**SUBJECT:** Tulsa Police Fleet Activity



## **Fiscal Year 2023 Tulsa Police Fleet Vehicles**

- 76** - Total number of Marked Police Utility Interceptors have been ordered.
- 52** - Have been received.
- 4** - Ford F150 Responders were ordered, received, and have been placed in service.
- 2** – Ford F250 Trucks have been ordered, received, and placed in service.
- 1** - Ford Transit Bomb Squad Technician Vans has been ordered. Ford has notified us we should receive the van before May 1, 2023.
- 2** – Ford Edges have been ordered.
- 1** – Ford Escape has been ordered, received and was placed into service.

**Police 1 – Tail Number: N301TP –**

Is a 2013 Airbus AS350B2. It is fully operational and is currently slated for replacement in late 2023.

**Police 2 – Tail Number: N302TP –**

Is a 2019 Airbus AS350B3. The repairs to the engine have been completed and the Helicopter returned to full-service Thursday, April 6<sup>th</sup>, 2023.

**New helicopter:** City of Tulsa Purchase Order **231494** was issued on December 22,2022 for a 2023 Airbus H125 Helicopter in the amount of \$3,506,538.00. That price is for a “Green” ship which is just the base aircraft. This aircraft will replace our current Police 1, the 2013 Airbus AS350B2 listed above, and should be placed in service late 2023.







# Parks

**Attendees:**

Kathy Sebert  
Steve King  
Ashley Webb  
Paul Hassink



## **Parks STOC Report**

04/13/23

**Submitted To: Public Safety, Urban Development and Equipment Subcommittee Sales Tax Overview Committee**

**Submitted By: Gary Schellhorn, Resource and Facilities Coordinator, Special Projects Design, Engineering Services Dept.**

1. McCLURE PARK SLIDE / PLUNGE POOL (147500-1R)
  - 7440 E. 7<sup>th</sup> Street – District 3
  - 2014 Sales Tax – part of McClure Pool Reconstruction Project (\$406,000)
  - Advertising for bids began November 16, 2018, with bids opening December 14, 2018.
  - 2 contractors provided bids of \$538,466 and \$794,999 which are 51% and 122% over the estimated cost.
  - Redesign began November 12, 2019 and is complete. Mylars were submitted on April 16, 2020.
  - Advertising for bids began April 24, 2020, with bids opening on June 5, 2020.
  - One bid was received at bid opening in the amount of \$572,536 which is over the estimated amount of \$390,129.40. The bid was rejected.
  - Revised Mylars have been submitted.
  - Project advertised for bids from July 22, 2022 till August 19, 2022.
  - Bid opening was held on August 19, 2022. No contractors bid on this project.
  - **Project to provide shade shelter with tables and benches that can be used for the pool patrons.**
  - **Purchase Order is being prepared to demolish tower and remove vegetation from enclosure.**
  - **Community input and Conceptual Design is underway.**
  
2. LANGENHEIM PARK PLAYGROUND AND SAFETY SURFACING (147520J)
  - 4701 South Harvard Ave – District 9
  - 2014 Sales Tax (6014-5455101-005011147520)
  - Budget: \$275,000 (\$30k in FY2018 and \$245k in FY 2020)
  - Consultant: LandPlan Consultants
  - Design Fees: \$33,299.90 / fees spent = \$23,661.90 / fees remaining balance = \$9,638.00
  - Design contract approved August 6, 2018.
  - Design began on August 23, 2018 – Preliminary Design review meeting was held December 21, 2018.
  - A privately funded playground was installed in 2016.
  - Funding balance remaining for improvements = \$251,338.10
  - Reallocate of the funding is requested to go to Whiteside Park for site design for an all-inclusive playground in conjunction with a private donation for the playground. (See #3 below)
  
3. INCLUSIVE PLAYGROUND (located at Whiteside Park)
  - 4009 S. Pittsburg Ave. – District 9
  - 2014 Sales Tax (6014-5455101-005011147520) and Private Funding from the Burnstein Foundation
  - Consultant: LSI Playgrounds and Landplan Consultants
  - Playground has been purchased and is being manufactured.
  - A site survey has been completed and site improvement design has begun.
  - **The Playground has been delivered to the construction site.**
  - **The site improvements will be constructed concurrently with the playground installation.**
  - **The Site Work Project opens bids 4/14/2023.**
  - **The site has been excavated by Parks staff and a site survey has been provided to layout the playground area. The playground is being laid out for installation of berms and footings.**

## **Parks STOC Report**

04/13/23

### 4. MINSHALL PARK PLAYGROUND AND SAFETY SURFACING (147520L)

- 7404 South Kingston Ave – District 8
- 2014 Sales Tax (6014-5451101-005011147520)
- Budget: \$275,000 (\$30k in FY2018 and \$245K in FY2020)
- Consultant: LandPlan Inc.
- Design Fees: \$33,299.90 / fees spent = \$23,661.90 / fees remaining balance = \$9,638.00
- Design began on August 23, 2018 – Preliminary Design review meeting was held December 21, 2018.
- Funding balance remaining for improvements = \$251,338.10
- Neighborhood Association's desired improvements to the Park include trail repair, new benches along the trail, repairs to the gazebo floor slab, and dredging/cleanup of the pond. Stormwater Design is managing the design and construction work.
- **Construction continues. Punch List Inspection was held September 14, 2022.**
- **Work remaining is installation of benches and completion of sod.**

### 5. REED PARK SWIMMING POOL RECONSTRUCTION (147120)

- 4333 S. Yukon Ave. – District 2
- 2014 Sales Tax (6014-5451101-005011147120)
- Budget: \$2,410,000 (\$300k in FY2019 AND \$2,110K in FY2021)
- Consultant: Alaback Design Associates
- Design Fees: \$299,986.04
- Design is complete – Mylars submitted on August 17, 2020
- Advertising for bids began December 11, 2020 and will open on January 29, 2021.
- The bid is being awarded to Magnum Construction at a cost of \$2,650,000.00.
- Construction began August 12, 2021.
- Construction status = 491 calendar days / 300 calendar days = 162% time.
- Completion originally scheduled for May 28, 2022 - additional days have been recommended to add to the construction time.
- Punch List Inspection was held on October 12, 2022. Contractor has completed all corrections.
- **Existing sanitary sewer line has been tested and is being evaluated for future improvements.**

### 6. REED PARK WATER PLAYGROUND (147190)

- 4333 S. Yukon Ave. – District 2
- 2014 Sales Tax (6014-5451101-005011147190)
- Budget: \$500,000 (\$60k in FY2019 AND \$440K in FY2021)
- Consultant: Alaback Design Associates
- Design Fees: \$57,347.87
- Design is complete – Mylars submitted on August 17, 2020
- Advertising for bids began December 11, 2020 and will open on January 29, 2021.
- The bid is being awarded to Magnum Construction at a cost of \$2,650,000.00.
- Construction began August 12, 2021.
- Construction status = 491 calendar days / 300 calendar days = 162% time.
- Completion originally scheduled for May 28, 2022 - additional days have been recommended to add to the construction time.
- Punch List Inspection was held on October 12, 2022. Contractor has completed all corrections.
- **Water line service is scheduled for enlargement to increase water flow to equipment.**

## **Parks STOC Report**

04/13/23

### **7. CARL SMITH IMPROVEMENTS (147270)**

- 17120 E. 21<sup>st</sup> Street – District 6
- 2014 Sales Tax
- Budget: \$185,000 (\$25,000 in FY2020 and \$160,000 in FY2021)
- Consultant: Method Architecture
- Design Fees: \$22,173.63
- Scope of work: HVAC improvements, flooring, painting, and roofing at Carl Smith Office, Concession, Restrooms, and Tournament Office.
- Design began October 30, 2019 – Mylars submitted on September 28, 2020.
- Advertising for bids began October 23, 2020 with bids opening December 11, 2020. 3 Bids were received – the low bid was \$307,138 which was 20% over the project budget. Bids were rejected.
- Bids opened on November 19, 2021. One bidder submitted a bid of \$415,920 which is \$165,920 over the budget. The bid has been rejected.
- The project will be completed with City of Tulsa annual contracts. Electrical work for the project has been completed. **Additional Purchase Orders for painting, HVAC, and flooring are being prepared to complete the Project.**

### **8. SAVAGE PARK IMPROVEMENTS (147230)**

- 17800 E. 21<sup>st</sup> Street – District 6
- 2014 Sales Tax
- Budget: \$120,000 (\$15,000 in FY2019 and \$105,000 in FY2020)
- Consultant: Method Architecture
- Design Fees: \$22,173.63
- Scope of work: HVAC improvements, flooring, painting, and roofing at Savage Park Concession, Restrooms.
- **Project design, advertising, and construction in conjunction with Carl Smith Improvements.**

### **9. WOODWARD PARK IMPROVEMENTS (147250)**

- 2324 S. Rockford Ave. – District 4
- 2014 Sales Tax (147250.ArchEngr.)
- Budget: \$4,850,000 (\$870k in FY20 and \$3,980k in FY21)
- Consultant: LandPlan Consultants, Inc.
- Kick-off meeting was held June 10, 2020.
- Final Public Meeting has been delayed coordinating with Stormwater Design concerning the adjacent 90-inch stormwater line at the bottom of the azalea garden slope. Stormwater Design to reroute part of the stormwater line (design and construction costs to be provided by Stormwater Design Department)
- 95% review meeting was held with the consultant on November 18, 2022.
- **100% design originally scheduled to be submitted January 25, 2023, is delayed for final coordination with stormwater sewer design engineering firm - 100% drawings to be submitted April 21, 2023.**
- **Advertising for bids originally scheduled to begin in February 2023 with bids opening in March 2023 is also delayed until June 2023.**

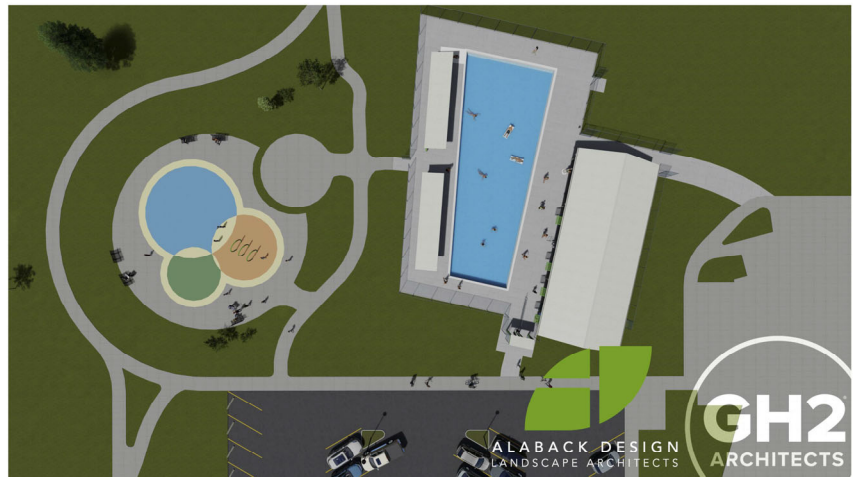


## Parks STOC Report

04/13/23

### 10. CHAMBERLAIN PARK POOL RECONSTRUCTION (147300)

- 4940 North Frankfort Ave. – District 1
- 2014 Sales Tax (147300.ArchEngr.)
- Budget: \$2,424,185
- Consultant: Alaback Design Associates
- Design Fees: \$266,583.77
- Community Outreach resulted in approval of Pool being constructed at Chamberlain Park – Brown Ordinance processed.
- Contract was approved March 9, 2022. Design Kick-off meeting was held March 17<sup>th</sup>.
- 95% Design Documents were submitted on November 9, 2022. A review meeting was held on Nov. 29, 2022.
- **100% Documents were submitted on January 17, 2023 and are being reviewed by staff.**
- **Board of Adjustment approval and State Health Department approval is required.**
- **Coordination with Privately Funded site improvements continues.**



### 11. TULSA ZOO CARNIVORES (147150)

- 5701 East 36<sup>th</sup> Street North. – District 1
- 2014 Sales Tax and Private Funding
- Budget: \$8,000,000 (2014) + \$17,000,000 (Private) = \$25,000,000
- Consultant: WDM (contract is with TZMI)
- Flintco Construction has been selected as the Construction Manager.
- **Consultant is preparing final Construction Documents and final cost estimates in preparation for bidding.**
- **Additional private funding is being sought by TZMI to make the project funding complete.**

## **Parks STOC Report**

04/13/23

### 12. GREENWOOD CULTURAL CENTER FACILITY REHABILITATIONS

- 322 North Greenwood Ave. – District 1
- IOT2 Sales Tax (2234B00000)
- Budget: \$5,340,000
- Interim Repair costs = \$195,044.48
- Design Fees: \$693,536.56
- Consultant: JCJ / Moody Nolan Architects.
- Design agreement approved 2/02/2022.
- Kick-off meeting was held February 17, 2022.
- Facility assessment and project scoping meeting was held March 1, 2022.
- Draft Master Plan and assessment report was submitted May 20, 20 22 with a review meeting held on June 28, 2022.
- Master Plan was submitted on September 30, 2022.
- **The contract amendment for the design phase was approved 4/5/2023. A design kick-off meeting is being scheduled.**

### 13. FRED JOHNSON PARK IMPROVEMENTS

- 6002 South Riverside Drive – District 7
- IOT2 Sales Tax (2244P00012)
- Total Budget: \$3,125,000
- Master Plan Budget: \$39,950
- Master Plan Consultant: Greenplay / Berry Dunn Consultants
- Information gathering meeting with Berry Dunn and City staff was held on March 3, 2022.
- A Community outreach event was held on May 14<sup>th</sup>, with interviews the following week.
- Design Charrettes were held on June 8, 2022 and July 7, 2022.
- The final community outreach session was held August 27, 2022.
- Final Master Plan documents have been submitted.
- **Consultant selection process continues. 4 design firms will be interviewed to select the design consultant for the Project.**

### 14. SWAN LAKE FOUNTAIN REHABILITATION (2242P00030)

- 1573 Swan Drive – District 4
- IOT2 Sales Tax (2244P00030)
- Total Budget: \$1,700,000
- Scope: Rehabilitation of the historic Swan Lake Fountain and improvements to the water quality of the lake.
- Consultant: Alaback Design Associates, Inc.
- Design Fees: \$203,825.55
- Design agreement has been approved – the Design Kick-off meeting was held May 12, 2022.
- Geotechnical investigations and Preliminary Design have been completed.
- **95% design drawings are being prepared and are scheduled to be submitted April 17, 2023.**
- **Advertising for bids is scheduled for July 2023 with construction to begin in October 2023.**

### 15. CARBONDALE PARK PLAYGROUND AND SURFACING (14750c)

- 2802 W. 48<sup>th</sup> – District 2
- IOT Sales Tax (6014-5451101-005011147520)
- Total Budget: \$275,000
- Contractor: ACS Solutions Inc.
- Cost: \$141,900.59
- Purchase Order has been released through the Source Well state contract to ACS Solutions Inc.
- Parks staff has removed the existing playground equipment.
- **Playground and artificial turf are installed. Site work and clean-up items have been completed – a final inspection was held 4/12/23.**



## **Parks STOC Report**

04/13/23

### 16. SCHLEGEL PARK PLAYGROUND AND SURFACING (14750q)

- 3825 W. 53<sup>rd</sup>. PI – District 2
- IOT Sales Tax (6014-5451101-005011147520)
- Total Budget: \$275,000
- Contractor: ACS Solutions Inc.
- Cost: \$112,984.92
- Purchase Order has been released through the Source Well state contract to ACS Solutions Inc.
- Parks staff will remove the existing playground equipment.
- **Playground is installed, and the artificial turf surfacing is being installed.**

### 17. WEST HIGHLAND PARK PLAYGROUND AND SURFACING (14750v)

- 2626 W. 61st – District 2
- IOT Sales Tax (6014-5451101-005011147520)
- Total Budget: \$275,000
- Contractor: ACS Solutions Inc.
- Cost: \$122,257.56
- Purchase Order has been released through the Source Well state contract to ACS Solutions Inc.
- Parks staff is removing the existing playground equipment.
- **Playground has been installed. Artificial safety turf is being prepared for installation.**

### 18. OWEN PARK CENTER IMPROVEMENTS

- 560 N. Maybelle Ave.- District 1
- IOT2 Sales Tax (2244B00009) – Park Facilities
- Total Budget: \$50,000
- Repairs per Annual Tulsa Contractors Purchase Orders
  - New storefront entrance – **Purchase Order is being processed**
  - Remove existing entry doors– **Purchase Order is being processed**
  - Relocate fire alarm pull station – **to accompany new entrance**
  - New panic hardware and exit signs on 2 doors
  - New drinking fountains – **completed by Parks staff**
  - New VCT floor and base in annex – **completed by Parks staff**
  - HVAC split unit in new entry – **to follow new entrance installation**
  - Gym floor repairs – **Purchasing bid in process**
  - Replace glass in gym windows – **Purchase Order is being processed**
  - Finish back side of partition wall – **complete by Parks staff**
  - **The Center is open for operation while these improvements are being made.**

### 19. ZINK PARK EROSION AND SITE REPAIRS

- 3216 S Trenton Ave.- District 4
- IOT2 Sales Tax (2244B00009)
- Total Budget: \$151,800
- Consultant: Wallace Engineering
- Design Fees: \$10,500.00
- **Design review drawings to be submitted by April 17, 2023 with final design scheduled to be completed by May 1, 2023.**
- **Advertising for bids is anticipated to begin in June 2023 and construction begin in August 2023.**



## Parks STOC Report

04/13/23

### 20. 1712 CHAS PAGE PARK MAINTENANCE ROOF REPLACEMENT











- 1712 Charles Page Blvd. – District 1
- IOT2 Sales Tax (2244B00009)
- Total Budget - \$358,399
- Consultant: GH2 Architects
- Design Fees: \$35,378.00
- **Design continues - 95% Design drawings are being prepared.**

### 21. MOHAWK STATION MAINTENANCE ROOF REPLACEMENTS

















- 4508 E. Mohawk Blvd. – District 1
- IOT2 Sales Tax (2244B00009)
- Total Budget - \$183,084
- Consultant: Todd Architects / GH2 Architects
- Design Fees: \$16,327.00
- **Design continues - 95% Design drawings are being prepared.**

### 22. TENNIS COURT REHABILITATION


- Parks System Wide
- IOT2 Sales Tax (2244P00011)
- Budget: \$1,200,000
- Project is to repair and resurface tennis and sports courts, provide new nets, screens, fencing, and new sports striping.
- Specifications have been prepared and submitted to Purchasing for Bidding.
- **Bidding is scheduled to open March 15, 2023.**
- **Construction is anticipated to begin in April 1, 2023 when temperatures become warm enough to install the new surfacing and striping.**
- **Total Estimated Improvement Costs: \$1,110,483.00**

Park	District	Court	Action	Total Cost	Current Configuration	Proposed Configuration
Challenger 7	2	Tennis Court	Re-Key, Refinish	40,510.00		
		Tennis Court	Convert to Bball			
Norvell	3	Tennis Court	Refinish	41,030.00		
		Bball Half Court	Convert to single full court			
		Bball Half Court	Convert to single full court			
Braden	5	Tennis Court	Add 2 pickleball, refinish tennis	32,230.00		
		Tennis Court	Add 2 pickleball, refinish tennis			
Aaronson	7	Tennis Court	Refinish, Repair Fence	50,260.00		
		Bball Half Court	Convert to Single Full Court			
		Bball Half Court	Convert to Single Full Court			
		Tennis Court	Refinish, Repair Fence			
Carbondale	2	Bball Half Court	Convert to 2 pickleball	33,573.00		
		Tennis Court	Convert to Bball			

**Parks STOC Report**  
04/13/23

Cowan	5	Tennis Court	Convert to Bball, soccer	37,610.00		
		Tennis Court	Convert to Bball, soccer			
Explorer	7	Tennis Court	Refinish	49,370.00		
		Tennis Court	Refinish			
		Tennis Court	Convert to Pickleball			
		Tennis Court	Convert to Pickleball			
Hicks	7	Tennis Court	Refinish	67,494.00		
		Tennis Court	Refinish			
		Tennis Court	Refinish			
		Tennis Court	Convert to Soccer/Bball			
		Tennis Court	Convert to Soccer/Bball			
Langenheim	9	Tennis Court	Convert to Pickleball	28,530.00		
		Tennis Court	Convert to Pickleball			
McClure	3	Basketball Court	Refinish	95,930.00		
		Basketball Court	Refinish			
		Tennis Court	Refinish			
		Tennis Court	Refinish			
		Tennis Court	All sports/bike polo court			
		Tennis Court	All sports/bike polo court			
		Tennis Court	Convert to Pickleball			
Norberg	6	Tennis Court	Refinish	58,830.00		
Tennis Court	Refinish					
Bball Half Court	Convert to single full court					
Bball Half Court	Convert to single full court					
Ute	3	Basketball Court	Maintain	35,830.00		
		Bball Half Court	Convert to single full court			
		Bball Half Court	Convert to single full court			
Zink	9	Tennis Court	Refinish	30,010.00		
		Tennis Court	Refinish			
		Tennis Court	Pickleball			
		Tennis Court	Pickleball			
Henthorne	9	Basketball Court	Refinish	70,550.00		
		Tennis Court	Refinish			
		Tennis Court	Refinish			
		Tennis Court	Refinish			
Zeigler	1	Tennis Court	Refinish	52,220.00		
		Tennis Court	Refinish			
		Basketball Court	Refinish			
		Basketball Court	Refinish			
Crutchfield	1	Bball Half Court	Maintian	9,535.00		
Leake	8	Tennis Court	Refinish	23,510.00		
		Tennis Court	Refinish			
Rose Dew	6	Bball Half Court	Maintain	12,485.00		
Starks Cheyenne	1	Basketball Court	Refinish	23,510.00		
		Tennis Court	Refinish, pickleball overlay			
Terwilliger	1	Bball Half Court	Maintain	9,535.00		

**Parks STOC Report**  
04/13/23

Admiral	3	Bball Half Court	Refinish	35,830.00		
		Bball Half Court	Refinish			
		Basketball Court	Refinish			
Clark	3	Basketball Court	Maintain	18,310.00		
		Basketball Court	Maintain			
Lakeview	1	Bball Half Court	Maintain	9,535.00		
Manion	9	Basketball Court	Maintain	45,422.00		
		Tennis Court	Maintain			
		Tennis Court	Maintain			
		Tennis Court	Maintain			
Whiteside	9	Tennis Court	Maintain	20,182.00		
		Tennis Court	Maintain			
Heller	9	Tennis Court	Maintain	60,000.00		
		Tennis Court	Convert to Full Basketball			
		Pickleball	Maintain			
		Pickleball	Maintain			
		Pickleball	Maintain			
		Bball Half Court	Convert to 2 Pickleball			
Tracy	4	Tennis Court	Maintain	54,112.00		
		Tennis Court	Maintain			
		Tennis Court	Maintain			
		Tennis Court	Maintain			
		Tennis Court	Maintain			
		Tennis Court	Maintain			
Berry	1	Tennis Court	Refinish	41,030.00		
		Basketball Court	Refinish			
Chamberlain	1	Garden (Tennis Court)	N/A	23,510.00		
		Tennis Court	Refinish			
		Basketball Court	Refinish			
		Basketball Court	Refinish			

23. REED PARK CENTER ROOF REPLACEMENT (SP23-6)

- 4333 S. Yukon Ave. – District 2
- IOT2 – Parks Facilities
- Consultant: GH2 Architects
- **Existing roof and structure are being inspected / evaluated to determine the scope of repairs / replacement.**

24. CRAWFORD PARK SHELTER ROOF REPLACEMENT (SP23-7)

- 2425 N. Hartford Ave. – District 1
- IOT2 – Parks Facilities
- Consultant: GH2 Architects
- Design Fees: \$22,421.23
- Existing roof has been inspected / evaluated.
- **Preliminary design is underway.**
- **Advertising for bids is scheduled to begin in June 2023.**

25. CARL SMITH PARK SEWER LAGOON EXPANSION AND REPAIR (SP23-4)

- 17120 E. 21<sup>st</sup> Street – District 6
- IOT2 Sales Tax – Park Facilities
- Budget: \$650,000
- **Consultant: Consultant selection is underway.**
- **Expansion of the existing sanitary sewer lagoon system to meet current needs and codes.**

# Sewer, Stormwater, and Transportation

**Attendees:**

Kathy Sebert

Steve King

Sylvia Powell

Paul Hassink



CITY OF TULSA, OKLAHOMA  
 SALES TAX OVERVIEW COMMITTEE  
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

03/01/23

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
<b>FUND 405 - SALES TAX FUND (2014)</b>											
144017	Arterial Street Rehab										
a	Charles Page Blvd. - 33rd W. Ave. to 25th W. Ave.	Jun-15	Sep-17	Garver	\$206	80%					
b	49th W. Ave. - Edison St. to Charles Page Blvd.	May-18	Apr-19	CEC	\$165	80%					
c	Utica Ave. - Pine St. to Admiral Blvd.	Nov-15	Apr-16	CEC	\$528	80%					
d	Lewis Ave. - 36th St. N. to Apache St.	Jun-18	Dec-18	Cytergy	\$118	95%					
e	Southwest Blvd. - W. 23rd St. to W. 31st St.	Dec-16	Sep-17	Dewberry/Poe	\$300	95%	Jul-22	Dec-23	Becco	\$7,097	68%
f	Southwest Blvd. - W. 31st St. to W. 40th St.	Dec-16	Sep-17	Dewberry/Poe	\$315	95%	Jul-22	Dec-23			
g	Union Ave. - Southwest Blvd. to W. 41st St.	May-15	Sep-17	Dewberry	\$158	95%					
h	Union Ave. - W. 51st St. to W. 61st St.	Jun-15	Aug-17	Garver	\$157	100%	Jan-21	Aug-21	Ellsworth	\$1,598	100%
j	Pine St. - Harvard Ave. to Yale Ave.	May-18	Apr-19	Benham	\$289	90%					
k	Admiral Pl. - Lewis Ave. to Harvard Ave.	Jan-18	Aug-18	BKL	\$253	90%					
l	Admiral Pl. - Harvard Ave. to Yale Ave.	Nov-16	Jul-17	Poe	\$325	95%	Feb-21	May-22	Ellsworth	\$4,177	100%
m	Sheridan Rd. - Apache St. to Pine St.	Nov-15	Sep-17	AAB	\$156	95%					
o	Mingo Rd. - 36th St. N. to Pine St.	Nov-16	Nov-17	McClelland	\$727	100%	Mar-19	Sep-21	Becco	\$8,435	100%
p	Mingo Rd. - Admiral Blvd. to 11th St.	Oct-18	Aug-09	Wallace	\$89	90%	Nov-21	Sep-22	Ellsworth	\$1,187	100%
q	11th St. - 89th E. Ave. to Mingo Rd.	Feb-15	Nov-15	CEC	\$162	100%	Apr-19	Oct-19	Ellsworth	\$1,631	100%
r	15th St. - Peoria Ave. to Lewis Ave.	May-15		Garver	\$248	100%	Sep-19	Nov-20	Crossland	\$3,094	100%
s	15th St. - Lewis Ave. to Harvard Ave.	Jan-17	Oct-17	Garver	\$302	90%	Jul-24				
t	Peoria Ave. - Admiral Blvd. to 11th St.	May-18	Feb-19	MARQUARDT	\$214	90%					
u	Peoria Ave. - 11th St. to 21st St.	Feb-16	Nov-16	MARQUARDT	\$252	90%					
v	Utica Ave. - Admiral Blvd. to 11th St.	Nov-19	Aug-20	C&K	\$317	70%					
w	Utica Ave. - 11th St. to 15th St.	Dec-16	Jul-17	BKL	\$224	90%					
x	Harvard Ave. - 15th St. to 21st St.	Sep-19	Jul-20	Garver	\$245	90%					
y	Harvard Ave. - 21st St. to 31st St.	Apr-18	Apr-19	Poe	\$469	92%					
z	21st St. - Yale Ave. to Sheridan Rd.	May-18	Mar-19	CEC	\$259	90%					
aa	31st St. - Yale Ave. to Sheridan Rd.	Aug-19	May-20	HNTB	\$237	90%					
ac	41st St. - Sheridan Rd. to Memorial Dr.	Apr-18	Jan-19	CGA	\$262	90%					
ad	Memorial Dr. - 21st St. to 31st St.	Nov-15	Jun-16	BKL	\$289	100%	Jul-19	Oct-21	Grade Line	\$5,086	100%
ae	51st St. - Mingo Rd. to Garnett Rd.	Apr-18	Jun-19	Garver	\$234	90%					
af	71st St. - Memorial Dr. to Mingo Rd.			COT		100%	Apr-21	Jun-22	Crossland	\$2,228	100%
ag	91st St. - Mingo Rd. to Hwy 169.			COT		100%	May-20	Aug-20	Becco		100%
ah	Memorial Dr. - 81st St. to 91st St.	Sep-17	Mar-18	Marquardt	\$129	100%	Mar-21	Jan-22	Crossland Heavy	\$2,987	100%
ai	Memorial Dr. - 91st St. to Creek Tpk.	Jun-15	Dec-15	Marquardt	\$58	100%	Mar-21	Jan-22	Crossland Heavy		100%

CITY OF TULSA, OKLAHOMA  
 SALES TAX OVERVIEW COMMITTEE  
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

03/01/23

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
aj	Sheridan Rd. - 91st St. to 101st St.	Apr-18	Jun-19	HUB	\$84	95%					
al	Harvard Ave. - 41st St. to 51st St.	Apr-18	Dec-18	PEC	\$236	80%					
am	36th. St. N. - Mingo Rd. to Hwy 169	Jun-18	Apr-19	McClelland	\$301	90%					
an	Downtown Arterial Streets	May-15	Aug-15	Poe	\$923	70%					
	Phase 4 - Boulder/1ST to 10th		May-17	Poe		95%	Jan-19	Apr-20	Becco	\$4,415	100%
ao	Phase 5 - 6th Street / 7th Street		Jul-17	Poe		95%	Apr-20	Feb-21	Crossland	\$4,663	99%
ao	Phase 6A - Detroit / 8th Street		Aug-17	Poe		95%	Oct-22	Aug-23	Crossland Heavy	\$4,146	48%
ao	Phase 6B - 7th Street			Poe		95%					
ao	Phase 7 - Cheyenne		Jan-18	Poe		50%					
ap	Pine St. & MLK Jr. Blvd Intersection	May-08	Feb-19	CP&Y	\$117	98%					
aq	Pine St. & Peoria Ave. Intersection	Jun-17	Jun-18	Schemmer	\$135	90%					
ar	Pine St. & Lewis Ave. Intersection	Mar-17	Aug-17	Wallace	\$75	95%	Jan-21	Jun-21	Gradeline	\$1,598	100%
as	41st St. & Union Ave. Intersection	May-15	Sep-19	Dewberry	\$158	99%					
at	51st St. & Union Ave. Intersection			Garver		0%					
av	36th St. N. & Mingo Rd. Intersection	Nov-16	Nov-17	McClelland	\$727	95%	Aug-19	Sep-21	Becco		100%
aw	Admiral Blvd. & Lewis Ave. Intersection	Dec-17	Aug-18	BKL	\$250	90%					
ax	11th St. & Utica Ave. Intersection	Dec-16	Jul-17	BKL	\$224	90%					
ay	21st St. & Peoria Ave. Intersection			MARQUARDT							
az	21st St. & Memorial Dr. Intersection	Nov-15	Apr-16	BKL	\$289	98%	Jul-19	Jul-21	Gradeline		100%
ba	51st St. & Mingo Rd. Intersection	Apr-18	Mar-19	Garver	\$234	90%					
bb	71st St. & Sheridan Rd. Intersection	Mar-17	Nov-17	Cytergy	\$99	60%					
bd	71st St. & Memorial Dr. Intersection			COT		100%	Apr-21	Jan-22	Crossland		100%
be	81st St. & Memorial Dr. Intersection	May-17	Dec-17	Benham		95%	Jun-21	Jan-23	Becco	\$13,875	88%
bf	61st St. & Yale Ave. Intersection	Dec-16	Aug-17	C&K	\$77	100%	Mar-21	Aug-21	Crossland	\$1,747	100%
144020	Citywide Non-Arterial Routine and Preventive Maintenance										
144101	Widen Yale Avenue, 81st St. to 91st Street South	Jun-15	Jul-17	Benham	\$600	95%	Oct-21	Dec-23	Becco	\$29,257	58%
144102	Widen 81st Street South, Sheridan Road to Memorial Drive	Sep-16	May-18	Benham	\$950	95%	May-21	May-23	Becco	\$13,875	88%
144103	Widen Yale Avenue, 96th St. South to 101st St. South	Aug-16	Jul-17	CEC	\$200	95%	Mar-20	Jan-22	Becco	\$8,752	100%
144105	Widen 25th W. Ave., Edison to Apache (design)	Apr-21		Poe		80%					
144108	Widen Pine Street, Mingo to U.S. 169 (design)			Garver							
144120	Gilcrease Expressway Local Match										
144063	Bridges - Replacement and Rehabilitation Programs										
a	Bridge No. 275 - 10100 E. 36th St. N.	Jun-18	Dec-19	McClelland		90%					

CITY OF TULSA, OKLAHOMA  
 SALES TAX OVERVIEW COMMITTEE  
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

03/01/23

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
g	Bridge No. 250 - 11200 E. 11th St.	Jun-15	Dec-15	Cowen	\$39	100%			Becco	\$693	100%
h	Bridge No. 247 - 9200 E. 11th St.	Jun-15	Dec-15	Cowen	\$39	100%			Becco	\$693	100%
k	Bridge No. 401 - 3800 S. Memorial Dr.	Jun-15	Dec-15	Cowen	\$39	100%	Sep-19	Feb-20	Becco	\$693	100%
s	Bridge No. 333 - 1300 S. 177th E. Ave.	Jun-20	Oct-21	CP&Y		90%	Jan-22	Oct-22	Grade Line	\$503	100%
u	Bridge No. 209 - 3000 N. Mingo Rd.	Nov-16	Nov-17	McClelland	\$727	90%					
x	Bridge No. 222 - 3200 S. Peoria Ave.	May-18	Jul-19	Garver	\$227	100%	Nov-21	Jun-22	Tri-Star	\$2,275	100%
144094	ODOT Rehabilitation and Replacement Program										
144003	Citywide guardrail replacement										
144004	Citywide traffic signalization										
144005	Roadway, pedestrian, and decorative lighting replacement										
144006	Signing, pavement marking and delineation										
144007	Traffic calming										
144008	Traffic signal installation, modification, and safety improvements										
144009	Traffic signal pole replacement										
144010	Creek Turnpike Trail pedestrian bridge over Memorial Dr. (\$200,000 for study only)										
144011	GPS emergency vehicle preemption system (approx. 30 intersections)										
144109	Citywide ADA Transition Plan Implementation (Minimum for 30-Year Schedule - High and Medium Priority Needs)	Feb-16	Aug-18	BKL	\$639	90%					
	ADA Transition Plan - Package #1		Sep-17			100%	Mar-20	Nov-20	Daris	\$1,642	100%
	ADA Transition Plan - Package #2					100%			Crossland		100%
	ADA Transition Plan - Package #3		Mar-23			90%	Apr-23				
144093	Citywide Matching Funds										
144018	Bicycle/Pedestrian Master Plan Implementation			Garver							
144019	IDL Entrance Rehabilitation (1st, 7th, and 8th Streets; signals at 1st and Greenwood)	see ao 144017		POE	\$1	100%					
<b>TOTAL FUND 405 INCOMPLETE PROJECTS</b>											
<b>FUNDS 4260-4266 - 2008 STREETS GENERAL OBLIGATION BOND</b>											
<b>Streets, Expressways, Sidewalks, Lighting, Traffic Calming</b>											
Arterial Street Rehabilitation and Citywide Projects:											
104009	Citywide-Arterial Rehab & Reconstruction										



**CITY OF TULSA, OKLAHOMA  
SALES TAX OVERVIEW COMMITTEE  
TRANSPORTATION PROJECTS STATUS REPORT**

Design & Construction as of:

03/01/23

DESIGN								CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl		Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
104010	Citywide-Arterial Sidewalk Repair & Construction											
104011	Citywide - Trails											
104012	Citywide - Railroad Crossings											
104013	Citywide - Local Match											
104014	Citywide-Gen.Engineering/Testing Inspection											
	Non-Arterial Rehabilitaiton and Citywide Projects.											
104107	Maintenance Zone 1007	May-13	May-15	BKL	\$557	100%		Nov-18	Apr-21	Becco	\$7,500	100%
104944	Maintenance Zone 9044	Oct-19	Jan-20	Meshek	\$41	100%		Sep-20	Jun-21	Tri-Star	\$3,575	100%
104015	Citywide Non-Arterial Rehab & Reconstruction											
104016	Citywide Non-Arterial Sidewalk Repair and Construction											
104000	Bond Issuance Costs											
104039	Harvard Ave. - Admiral Blvd. to Pine St.	Jun-12	May-13	Meshek	\$312	100%		Mar-18	May-19	Becco	\$3,529	100%
104041	Memorial Dr. - 21st St. S. to 11th St. S.	Aug-12	Dec-13	BKL	\$352	100%		Jul-19	Jul-21	Becco		100%
104043	Pine St. - Yale Ave. to Sheridan Rd.	Aug-12	Mar-13	Dewberry	\$467	95%		Jul-20	Jun-22	Becco	\$4,587	100%
144023	Citywide - Arterial Routine & Preventative Maintenance											
144022	Citywide-Art/Non-Art Routine & Preventative Maintenance											
104053	Pine St. - Yale Ave. Intersection	Jan-13	Aug-13	Dewberry	\$247	100%			2015			100%
104054	Citywide - General Engineering / Testing / Inspection											
<b>TOTAL FUNDS 4260-4266 - 2008 Streets General Obligation Bond</b>												
<b>FUNDS 4270-4276 - 2014 STREETS GENERAL OBLIGATION BOND</b>												
<b>Streets, Expressways, Sidewalks, Traffic Calming</b>												
Arterial Street Rehabilitation and Citywide Projects:												
144200	36th St. - N. MLK Jr. Blvd. to Peoria Ave.	Jun-15	Mar-20	PEC	\$232	90%		Sep-21	Feb-24	Ground Level	\$4,895	86%
144201	Apache St. - MLK Jr. Blvd. to Peoria Ave.	Nov-14	Aug-15	MESHEK	\$267	100%		Mar-19	Nov-19	Crossland	\$3,380	100%
144202	Apache St. - Peoria Ave. to Lewis Ave.	Aug-16	Mar-17	C&K	\$500	98%						
144203	W. 41st St. S. - 41st W. Ave. to S. 33rd W. Ave.	Sep-14	Aug-15	DEWBERRY/COT	\$175	95%		Mar-22	Dec-23	Grade Line	\$3,692	29%
144204	S. 33rd W. Ave. - 41st St. to 51st St.	Sep-14	Aug-15		\$275	95%						
144205	Apache St. - Lewis Ave. to Harvard Ave.	Sep-14	Sep-15	GUY	\$210	92%		Apr-22	Feb-23	Becco	\$3,987	78%
144206	11th St. - Peoria Ave. to Utica Ave.	Nov-14	Nov-15	BKL	\$185	95%		Mar-20	Jan-21	Becco	\$2,343	100%
144207	11th St. - Lewis Ave. to Harvard Ave.	Jun-16	Mar-17	BKL	\$205	85%						
144208	11th St. - Sheridan Rd. to Memorial Dr.	Nov-14	Nov-15	BKL	\$180	95%		Feb-22	Dec-22	Becco	\$3,227	99%
144209	21st St. - Garnett Rd. to 129th E. Ave.	Dec-14	Jul-15	GARVER	\$235	95%		Oct-20	Aug-21	Becco	\$4,079	100%

CITY OF TULSA, OKLAHOMA  
 SALES TAX OVERVIEW COMMITTEE  
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

03/01/23

DESIGN							CONSTRUCTION					
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl	
144210	21st St. - 129TH East Ave. Intersection	Dec-14	Jul-15	GARVER	\$156	95%	Oct-20	Aug-21	Becco		100%	
144213	91st St. - Harvard Ave. to Yale Ave.		May-19	CEC	\$177	95%						
144215	Peoria Ave. - 41st St. to 51st St.	Dec-16	Aug-17	MARQUARDT	\$340	95%						
144216	41st St. - Lewis Ave. to Harvard Ave.	Oct-14	Aug-15	CEC	\$275	95%	Apr-21	Jul-22	Crossland	\$5,653	100%	
144217	Apache St. & Harvard Ave. Intersection	Sep-14	Sep-15	GUY	\$176	95%	Apr-22	Feb-23	Becco	\$3,987	78%	
144218	41st St. & Lewis Ave. Intersection	Oct-14	Aug-15	CEC	\$210	95%	Apr-21	Jul-22	Crossland		100%	
144309	Citywide - Arterial Rehabilitation											
144110	Citywide - Arterial Sidewalk Improvements											
144020	Citywide - Arterial Routine and Preventive Maintenance											
144093	Citywide Matching Funds											
144094	ODOT Rehabilitation and Replacement Program											
	Non-Arterial Rehabilitaiton and Citywide Projects.											
144111	Maintenance Zone 1001:	May-15	Feb-16	MAR / ARB	271 / 284	95%	Feb-22	Feb-24	Gradeline	\$8,291	56%	
144106	Maintenance Zone 1006:	Sep-14	Jun-15	TETRA-TECH	\$356	95%	Apr-19	Oct-19	Ellsworth	\$2,585	100%	
144107	Maintenance Zone 1007:	Oct-14	Apr-15	Cynergy	\$56	95%	Nov-18	Jan-21	Becco		100%	
144168	Maintenance Zone 1068:	Sep-16	Sep-17	TEP / Cowan	152./168.	95./95%						
144173	Maintenance Zone 1073:	Oct-14	Jul-15	COWAN	\$49	95%	Jul-17	Nov-17	PCSI	\$437	100%	
144199	Maintenance Zone 1099:	Jun-15	Dec-15	CP&Y	\$259	95%	Apr-21	Apr-22	Ellsworth	\$2,343	100%	
144153	Maintenance Zone 1153:	Sep-14	Jun-15	POE	\$334+	95%	Sep-22					
144157	Maintenance Zone 1157 N:	Sep-14	Jun-15	BKL	\$302	100%	May-18	Feb-19	Ellsworth	\$3,195	100%	
144158	Maintenance Zone 1157 S:	Jun-15	Mar-16	SKW	\$210	100%	Oct-19	May-20	Crossland	\$2,493	100%	
144225	Maintenance Zone 2125:	Nov-14	Aug-15	WALLACE	\$179	95%	Apr-19	Jan-20	Becco	\$2,189	100%	
144230	Maintenance Zone 2130:	Oct-14	Aug-15	MESHEK	\$270	95%	Oct-20	Nov-21	Becco	\$3,485	100%	
144310	Maintenance Zone 3010:	May-15	Jan-16	MCCLELLAND	\$544	85%						
144311	Maintenance Zone 3011:	Jun-16	Jun-17	POE	\$656	100%	Aug-20	Sep-21	Crossland Heavy	\$7,603	100%	
144317	Maintenance Zone 3017:	Oct-17	Jul-18	CGA	\$324	96%						
144320	Maintenance Zone 3020:	Aug-16	May-17	AAB	\$345	80%						
144413	Maintenance Zone 4013:	Sep-14	Apr-15	LEIDOS	\$512	80%						
144421	Maintenance Zone 4021:	Jul-16	Apr-17	CEC	\$343	96%						
144431	Maintenance Zone 4031:	May-15	Feb-16	GARVER	\$576	95%	Nov-22	Apr-24	Crossland Heavy	\$10,082	28%	
144467	Maintenance Zone 4067 phase 1	Oct-14	Jun-15	GUY	\$344	100%	Jan-20	Aug-20	Crossland	\$3,127	100%	
144467	Maintenance Zone 4067 phase 2			GUY/COT		80%						
144452	Maintenance Zone 4152:	Oct-17	Jul-18	HUB	\$373	97%						
144527	Maintenance Zone 5027:	Nov-14	May-15	CRAFTENTULL	\$115	95%	Sep-18	Jan-19	Paragon	\$1,144	100%	
144533	Maintenance Zone 5033:	Oct-14	Jun-15	CGA	\$444	100%	Oct-18	Aug-19	Crossland	\$4,847	100%	

CITY OF TULSA, OKLAHOMA  
 SALES TAX OVERVIEW COMMITTEE  
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

03/01/23

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
144546	Maintenance Zone 5046:	Jun-16	Mar-17	MCCLELLAND	\$540	96%					
144547N	Maintenance Zone 5047: North										
144547S	Maintenance Zone 5047: South	Aug-16	Jun-17	GARVER	\$584	90%			RLConstr	\$1,690	
144628	Maintenance Zone 6028:	Jan-18	Aug-19	MCCLELLAND	\$428	90%					
144635	Maintenance Zone 6035:	May-15	Apr-16	HUB	\$253	100%	Oct-19	Jul-19	Becco	\$2,768	100%
144642	Maintenance Zone 6142:	Oct-14	Jun-15	HOOD/ Poe	\$78	95%	Feb-22	Feb-23	Ellsworth	\$1,313	95%
144645	Maintenance Zone 6145:	Oct-04	May-15	Cytergy	\$195	95%	Mar-21	Jul-22	Becco	\$2,957	100%
144740	Maintenance Zone 7040:	Jun-16	Apr-17	HUB	\$254	95%	Dec-20	Oct-21	Crossland Heavy	\$3,478	100%
144754	Maintenance Zone 7054:	Sep-17	Feb-19	POE	\$747	90%					
144857	Maintenance Zone 8057:	Apr-17	Jul-19	WALLACE	\$107	100%	Oct-20	Jun-21	Ellsworth	\$1,601	100%
144863A	Maintenance Zone 8063: North	Oct-17	Sep-19	CraftonTull	\$195	95%	Jan-23		Crossland Heavy	\$3,211	10%
144863B	Maintenance Zone 8063: South	Oct-17	Sep-19	PEC	\$195	95%	Jul-22				
144944	Maintenance Zone 9044:	Oct-14	May-15	Meshek	\$293	95%	Sep-20	May-21	Tri-Star	\$3,575	100%
144945	Maintenance Zone 9045:	Oct-14	Jul-15	GARVER	\$200	100%	Jan-19	Nov-19	Crossland	\$3,557	100%
144949	Maintenance Zone 9049:	Sep-17	May-19	GARVER	\$770	85%					
144950	Maintenance Zone 9050:	Jul-16	Feb-17	CP&Y	\$255	95%	Nov-22	Aug-23	Tri-Star	\$3,600	23%
144951	Maintenance Zone 9051:	Jul-16	Feb-17	SKW	\$130	95%					
144015	Citywide Non-Arterial Rehabilitation										
144021	Citywide Non-Arterial Routine and Preventive Maintenance										
144016	Citywide Non-Arterial Sidewalk Improvements										
144060	Bridge No. 189 - 4700 N. Iroquois Ave.	Nov-14	Jul-15	MEHLBURGER		90%					
144062	Bridge No. 323B - 12000 E. 21st	Dec-14		GARVER	\$10	95%	Oct-20	Aug-21	Becco		99%
<b>TOTAL FUNDS 4270-4273 - 2014 Streets General Obligation Bond</b>											
<b>FUNDS 4281-4285 - 2020 STREETS GENERAL OBLIGATION BOND</b>											
<b>'Non-Arterial Street Rehabilitation Projects:</b>											
2036N100Z	Maintenance Zone 1007:	Dec-20	Aug-21	Cowan	\$81	95%					
2036N1068Z	Maintenance Zone 1068:			McClelland							
2036N1070Z	Maintenance Zone 1070:	Feb-21	Oct-21	CGA	\$204	95%					
2036N1071Z	Maintenance Zone 1071:			PEC							
2036N1072Z	Maintenance Zone 1072:			BKL							
2036N1076Z	Maintenance Zone 1076:		Jul-21	McClelland	\$236	90%					
2036N1078Z	Maintenance Zone 1078:	Oct-20	Jun-21	Olsson	\$253	85%					
2036N1097Z	Maintenance Zone 1097:										
2036N1098Z	Maintenance Zone 1098:										
2036N1153Z	Maintenance Zone 1153:	Apr-22	Feb-23	Poe	\$164	25%					
2036N1155Z	Maintenance Zone 1155:	Aug-22	Apr-23	CGA	\$45	90%					
2036N1157Z	Maintenance Zone 1157:			Poe							

**CITY OF TULSA, OKLAHOMA  
SALES TAX OVERVIEW COMMITTEE  
TRANSPORTATION PROJECTS STATUS REPORT**

Design & Construction as of:

03/01/23

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036N2056Z	Maintenance Zone 2056:			Garver							
2036N2065Z	Maintenance Zone 2065:	Jan-21	Sep-21	Garver	\$218	95%					
2036N2066Z	Maintenance Zone 2066:	Oct-20	Jul-21	C&K	\$101	100%					
2036N2131Z	Maintenance Zone 2131:										
2036N3004Z	Maintenance Zone 3004:			Marquardt							
2036N3005Z	Maintenance Zone 3005:			CEC							
2036N3008Z	Maintenance Zone 3008:										
2036N3010Z	Maintenance Zone 3010:	Aug-22	Jul-23	McClelland	\$115	15%					
2036N3011Z	Maintenance Zone 3011:			Benham							
2036N3017Z	Maintenance Zone 3017:			CGA							
2036N3075Z	Maintenance Zone 3075:	Aug-22	Apr-23	CGA	\$45	68%					
2036N3080Z	Maintenance Zone 3080:										
2036N3081Z	Maintenance Zone 3081:	Feb-21	Mar-22	EST	\$58	95%					
2036N3082Z	Maintenance Zone 3082:										
2036N4014Z	Maintenance Zone 4014:	Oct-20	May-21	Poe	\$136	95%					
2036N4015Z	Maintenance Zone 4015:			Garver							
2036N4021Z	Maintenance Zone 4021:	Sep-20	Feb-22	CEC	\$256	80%					
2036N4022Z	Maintenance Zone 4022:	Oct-20	Apr-21	BKL	\$322	90%					
2036N4023Z	Maintenance Zone 4023:	Aug-22	Apr-23	CGA	\$45	90%					
2036N4029Z	Maintenance Zone 4029:										
2036N4030Z	Maintenance Zone 4030:	Dec-20	Aug-21	Marquardt	\$143	95%	Dec-22	Jul-23	R&L	\$1,886	14%
2036N4031Z	Maintenance Zone 4031:			Garver							
2036N4067Z	Maintenance Zone 4067:			Ollson							
2036N4069Z	Maintenance Zone 4069:	Aug-22	Jul-23	BKL	\$200	40%					
2036N5016Z	Maintenance Zone 5016:	Jun-22	Apr-23	Garver		83%					
2036N5026Z	Maintenance Zone 5026:										
2036N5027Z	Maintenance Zone 5027:	Sep-22	Jul-23	Wallace	\$46	60%					
2036N5033Z	Maintenance Zone 5033:			Garver							
2036N5039Z	Maintenance Zone 5039:			FNI							
2036N5040Z	Maintenance Zone 5040:	Apr-21	Mar-22	TEP	\$81	90%					
2036N6035Z	Maintenance Zone 6035:			Benham							
2036N6142Z	Maintenance Zone 6142:	Jul-22	Nov-22	C&K		90%	Apr-23				
2036N6144Z	Maintenance Zone 6144:										
2036N6148Z	Maintenance Zone 6148:										
2036N6149Z	Maintenance Zone 6149:										
2036N6150Z	Maintenance Zone 6150:										
2036N7048Z	Maintenance Zone 7048:	Nov-20	Mar-22	Benham	\$252	90%					
2036N7060Z	Maintenance Zone 7060:	Dec-20	Dec-21	HUB	\$73	95%	Apr-23				
2036N7104Z	Maintenance Zone 7104:										
2036N7109Z	Maintenance Zone 7109:										

CITY OF TULSA, OKLAHOMA  
 SALES TAX OVERVIEW COMMITTEE  
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

03/01/23

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036N7115Z	Maintenance Zone 7115:										
2036N8057Z	Maintenance Zone 8057:	Feb-21	Mar-22	Wallace	\$107	90%	Mar-23				
2036N8102Z	Maintenance Zone 8102:	Oct-20	Apr-22	FNI	\$171	90%					
2036N8113Z	Maintenance Zone 8113:	Aug-22	Feb-23	Keithline		80%					
2036N8116Z	Maintenance Zone 8116:			Wallace							
2036N9036Z	Maintenance Zone 9036:	Sep-22		CEC	\$236	20%					
2036N9037Z	Maintenance Zone 9037:	Jan-21	Aug-21	CP&Y	\$183	85%					
2036N9038Z	Maintenance Zone 9038:	Dec-20	Oct-21	PEC	\$71	95%					
2036N9043Z	Maintenance Zone 9043:										
2036N9044Z	Maintenance Zone 9044:	Sep-22	Sep-23	Benham		10%					
2036N9045Z	Maintenance Zone 9045:	Aug-22	Feb-23	Keithline							
2036N9049Z	Maintenance Zone 9049:	Jun-22	Mar-23	Marquardt	\$207	65%					
2036N9050Z	Maintenance Zone 9050:	Jan-21	Sep-21	CP&Y	\$98	90%					
2036N9051Z	Maintenance Zone 9051:	Sep-20	Apr-21	Keithline	\$83	95%					
2036N9052Z	Maintenance Zone 9052:										
<b>Arterial Street Rehabilitation Projects:</b>											
<b>Arterial Street Projects:</b>											
2036A0001Z	56th St N-MLK Blvd to 1500ft W of Peoria										
2036A0002Z	46th St N - Peoria Ave to Lewis Ave	Apr-22	Mar-23	C&K	\$273	60%					
2036A0003Z	46th St N - Elwood Ave to MLK Jr Blvd										
2036A0004Z	36th St N - Peoria Ave to Lewis Ave										
2036A0005Z	36th St N - Osage Cnty Line to MLK Blvd			Benham							
2036A0006Z	31st St N - 53rd W Ave to 41st W Ave										
2036A0007Z	Apache St - Harvard Ave to Yale Ave	Jun-22	Jan-23	Native Strategies	\$49	20%					
2036A0008Z	Pine St - Gilcrease Museum Rd to Union	Sep-21	Sep-22	Poe		95%	Feb-23				
2036A0009Z	Pine St - Peoria Ave to Lewis Ave			CEC							
2036A0010Z	Edison St - 33rd W Ave to Union Ave	Sep-21	Sep-22	Poe		95%	Feb-23				
2036A0011Z	33rd W Ave - Apache St to Pine St	Sep-21	Sep-22	Poe		95%	Feb-23				
2036A0012Z	33rd W Ave - Pine St to Edison St	Sep-21	Sep-22	Poe		95%	Feb-23				
2036A0013Z	Gilcrease Museum Rd - Apache to Pine	Sep-21	Sep-22	Poe		75%					
2036A0014Z	MLK Jr Blvd - 56th St N to 46th St N										
2036A0015Z	MLK Jr Blvd - 36th St N to Apache St			Benham							
2036A0016Z	MLK Jr Blvd - Apache St to Pine St			Benham							
2036A0017Z	Peoria Ave - 56th St N to 46th St N	Apr-22	Mar-23	C&K	\$273	80%					
2036A0018Z	Peoria Ave - 46th St N to 36th St N	Apr-22	Mar-23	C&K	\$273	80%					
2036A0019Z	Peoria Ave - Pine St to Admiral Blvd										
2036A0020Z	Lewis Ave - Pine St to Admiral Pl			CEC							
2036A0021Z	Harvard Ave - Mohawk Blvd to 36th St N			Schemmer	\$49						
2036A0025Z	41st St S - Union Ave to Elwood Ave			BKL							

CITY OF TULSA, OKLAHOMA  
 SALES TAX OVERVIEW COMMITTEE  
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

03/01/23

DESIGN								CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl		Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036A0026Z	51st St S - 33rd W Ave to Union Ave											
2036A0027Z	61st St S - Lewis Ave to Harvard Ave	Jun-22	Jan-23	Native Strategies	\$49	80%		Jun-23				
2036A0028Z	Elwood Ave - 71st St S to 81st St S											
2036A0029Z	Lewis Ave - 61st St S to 71st St S											
2036A0030Z	Lewis Ave - 71st St S to 81st St S											
2036A0031Z	Delaware Ave - 81st St S to 91st St S			BKL								
2036A0032Z	Harvard Ave - 61st St S to 71st St S											
2036A0033Z	Harvard Ave - 71st St S to 81st St S			Benham								
2036A0034Z	Harvard Ave - 81st St S to 91st St S											
2036A0039Z	36th St N - Garnett Rd to 129th E Ave			Keithline								
2036A0040Z	36th St N - 129th E Ave to 141st E Ave											
2036A0041Z	Apache St - Gilcrease Expy to Sheridan Rd											
2036A0042Z	Pine St - Lewis Ave to Harvard Ave			McClelland								
2036A0043Z	Pine St - State Hwy 11 to Mingo Rd			Garver								
2036A0044Z	Pine St - Mingo Rd to Garnett Rd											
2036A0045Z	Pine St - Garnett Rd to 129th E Ave			EST								
2036A0046Z	Admiral Pl - Sheridan Rd to Memorial Dr			CEC								
2036A0047Z	Admiral Pl - Memorial Dr to Mingo Rd			CEC								
2036A0048Z	Admiral Pl - Garnett Rd to 129th E Ave			CEC								
2036A0049Z	11th St S - Memorial Dr to 89th E Ave											
2036A0050Z	Yale Ave - Apache St to Pine St			HUB								
2036A0051Z	Yale Ave - Pine St to Admiral Pl											
2036A0052Z	Sheridan Rd - 36th St N to Apache St											
2036A0053Z	Garnett Rd - Admiral Pl to 11th St S			CGA								
2036A0054Z	129th E Ave - 36th St N to Apache St			Keithline								
2036A0055Z	129th E Ave - Apache St to Pine St											
2036A0064Z	11th St S - Utica Ave to Lewis Ave			Wallace								
2036A0065Z	11th St S - Harvard Ave to Yale Ave											
2036A0066Z	15th St S - Boston Ave to Denver Ave											
2036A0067Z	15th St S - Harvard Ave to Yale Ave			Garver								
2036A0068Z	21st St S - Lewis Ave to Harvard Ave											
2036A0069Z	21st St S - Harvard Ave to Yale Ave											
2036A0070Z	Peoria Ave - 21st St S to 31st St S											
2036A0077Z	15th St S - Sheridan Rd to 73rd E Ave											
2036A0078Z	41st St S - Yale Ave to Sheridan Ave											
2036A0079Z	Yale Ave - 31st St S to 36th St S											
2036A0080Z	Yale Ave - 41st St S to I-44											
2036A0081Z	Sheridan Rd - 21st St S to 31st St S											
2036A0082Z	Sheridan Rd - 31st St S to 41st St S											

CITY OF TULSA, OKLAHOMA  
 SALES TAX OVERVIEW COMMITTEE  
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

03/01/23

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036A0083Z	Sheridan Rd - 41st St S to 51st St S			Garver							
2036A0086Z	Admiral Pl: 225th EA to 22200 Blk E Adm.			CEC							
2036A0087Z	11th St S - 145th E Ave to 161st E Ave										
2036A0088Z	11th St S - 161st E Ave to 177th E Ave			TEP							
2036A0089Z	11th St S - 177th E Ave to 193rd E Ave			TEP							
2036A0090Z	21st St S - 145th E Ave to 161st E Ave										
2036A0091Z	21st St S - 161st E Ave to 177th E Ave										
2036A0092Z	31st St S - Garnett Rd to 129th E Ave			Marquardt							
2036A0093Z	41st St S - 177th E Ave to 193rd E Ave										
2036A0094Z	129th E Ave - 51st St S to 61st St S										
2036A0095Z	145th E Ave - 11th St S to 21st St S										
2036A0096Z	145th E Ave - 21st St S to 31st St S										
2036A0097Z	161st E Ave - 11th St S to 21st St S			TEP							
2036A0108Z	61st St S - Sheridan Rd to Memorial Dr										
2036A0109Z	Memorial Dr - 51st St S 61st St S			Poe							
2036A0110Z	Mingo Rd - 61st St S to 71st St S			C&K							
2036A0111Z	Mingo Rd - 91st St S to 101st St S										
2036A0113Z	101st St S- Yale Ave to Sheridan Ave										
2036A0114Z	101st St S - Sheridan Rd to Memorial Dr										
2036A0115Z	111st St S - Yale Ave to Sheridan Rd										
2036A0116Z	121st St S - Yale Ave to Sheridan Rd										
2036A0117Z	Yale Ave - 61st St S to 71st St S										
2036A0118Z	Yale Ave - 111th St S to 121st St S			CEC							
2036A0119Z	Sheridan Rd - 71st St S to 81st St S			CGA							
2036A0122Z	41st St S - Riverside Dr to Peoria Ave										
2036A0123Z	41st St S - Peoria Ave to Lewis Ave										
2036A0124Z	Peoria Ave - 31st St S to 41st St S			Marquardt							
2036A0125Z	Lewis Ave - 41st St S to I-44	Aug-21	Aug-23	Benham	\$85	35%					
	<b>Intersection Projects</b>										
2036A0022Z	36th St N & Harvard Ave Intersection			Schemmer							
2036A0023Z	Apache St & MLK Jr Blvd Intersection			Benham							
2036A0024Z	Pine St & Gilcrease Museum Rd Intersection										
2036A0035Z	41st St S & Elwood Ave Intersection			BKL							
2036A0036Z	51st St S & 33rd W Ave Intersection										
2036A0037Z	71st St S & Union Ave Intersection										
2036A0038Z	81st St S & Union Ave Intersection										
2036A0056Z	36th St N & 129th E Ave Intersection			Keithline							
2036A0057Z	Pine St & Sheridan Rd Intersection										
2036A0058Z	Pine St & Mingo Rd Intersection			CGA							
2036A0059Z	Pine St & Garnett Rd Intersection			EST							

CITY OF TULSA, OKLAHOMA  
 SALES TAX OVERVIEW COMMITTEE  
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

03/01/23

DESIGN							CONSTRUCTION				
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl
2036A0060Z	Admiral PI & Sheridan Rd Intersection			CEC							
2036A0061Z	Admiral PI & Garnett Rd Intersection										
2036A0062Z	11th St S & Sheridan Rd Intersection										
2036A0063Z	11th St S & Mingo Rd Intersection										
2036A0071Z	11th St S & Peoria Ave Intersection										
2036A0072Z	11th St S & Lewis Ave Intersection			Wallace							
2036A0073Z	11th St S & Harvard Ave Intersection										
2036A0074Z	15th St S & Harvard Ave Intersection			Garver							
2036A0075Z	21st St S & Harvard Ave Intersection										
2036A0076Z	31st St S & Peoria Ave Intersection			Marquardt							
2036A0084Z	15th St S & Sheridan Rd Intersection										
2036A0085Z	41st St S & Yale Ave Intersection										
2036A0098Z	11th St S & 145th E Ave Intersection										
2036A0099Z	11th St S & 161st E Ave Intersection			TEP							
2036A0100Z	11th St S & 177th E Ave Intersection			TEP							
2036A0101Z	11th St S & 193rd E Ave Intersection			TEP							
2036A0102Z	21st St S & 145th E Ave Intersection										
2036A0103Z	21st St S & 161st E Ave Intersection										
2036A0104Z	21st St S & 177th E Ave Intersection										
2036A0105Z	21st St S & 193rd E Ave Intersection										
2036A0106Z	31st St S & 145th E Ave Intersection										
2036A0107Z	41st St S & 177th E Ave Intersection										
2036A0112Z	91st St S & Memorial Dr Intersection										
2036A0120Z	121st St S & Yale Ave Intersection										
2036A0121Z	111th St S & Yale Ave Intersection			CEC							
2036A0126Z	41st St S & Peoria Ave Intersection										
<b>Arterial Street Widening Projects:</b>											
2036W0001Z	Gilcrease Museum Rd - Pine St to Admiral Blvd			Poe		75%					
2036W0002Z	81st St S - Tacoma Ave to Maybelle Ave			ODOT							
2036W0003Z	81st St S & Elwood Ave Intersection			BKL							
2036W0004Z	91st St S - Memorial Dr to Mingo Rd			Garver		80%					
2036W0005Z	101st St S & Sheridan Rd Intersection			CEC							
2036W0006Z	81st St S - Harvard Ave to Yale Ave			Garver	\$1,485						
<b>Central Business District (CBD)</b>											
<b>Streets and Alleyways</b>											
2036D0001Z	4th St										
2036D0002Z	MLK Ave & Detroit Ave north of BNSF	Aug-20	Feb-21	Poe		95%	Oct-21	May-22	Crossland	\$1,592	99%
2036D0003Z	Cincinnati Ave			Poe							
2036D0004Z	Detroit Ave south of BNSF			Poe							



CITY OF TULSA, OKLAHOMA  
 SALES TAX OVERVIEW COMMITTEE  
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

03/01/23

DESIGN							CONSTRUCTION					
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl	
2036D0005Z	Reconciliation Way	Aug-20	Feb-21	Poe		95%	Oct-21	May-22	Crossland	\$1,592	99%	
2036D0006Z	Lansing Ave			Poe								
2036D0007Z	Alleyways			Str & Stwtr								
<b>Bridge Maintenance &amp; Rehabilitation</b>												
2037B0201C	Bridge #201C			Benham								
2037B0216Z	Bridge #216											
2037B0219D	Bridge #219D											
2037B0286Z	Bridge #286			Benham								
2037B0340Z	Bridge #340											
2037B0343Z	Bridge #343			Benham								
2037B0179Z	Bridge #179											
2037B0232Z	Bridge #232											
2037B0245Z	Bridge #245	Jan-21	Sep-21	Garver	\$89	90%						
2037B0258Z	Bridge #258	Jan-21	Sep-21	Garver	\$35	90%						
2037B0263Z	Bridge #263	Jul-21		CP&Y		40%						
2037B0301Z	Bridge #301	Jul-21		CP&Y		40%						
2037B0359Z	Bridge #359	Feb-22	Dec-22	Garver		90%	Mar-23					
2037B0232A	Bridge #232A	Jan-21	Sep-21	Garver		95%						
2037B0301A	Bridge #301A											
2037B0425Z	Bridge #425											
2037B0225Z	Bridge #225											
2037B0167Z	Bridge #167	Feb-22	Dec-22	Garver		90%	Mar-23					
2037B0173Z	Bridge #173			Poe								
2037B0236Z	Bridge #236											
2037B0241Z	Bridge #241	Jul-21		CP&Y	\$54	60%						
2037B0261A	Bridge #261A	Feb-22	Dec-22	Garver		90%	Mar-23					
2037B0261B	Bridge #261B	Feb-22	Dec-22	Garver		90%	Mar-23					
2037B0269Z	Bridge #269			Benham								
2037B0474Z	Bridge #474											
2037B0482Z	Bridge #482											
2037B0153Z	Bridge #153											
2037B0183Z	Bridge #183											
2037B0252Z	Bridge #252											
2037B0271Z	Bridge #271											
2037B0322Z	Bridge #322			Benham								
2037B0329Z	Bridge #329											
2037B0478Z	Bridge #478											
2037B0204Z	Bridge #204	Mar-21		CP&Y		90%						
2037B0315Z	Bridge #315											
2037B0336Z	Bridge #336											

CITY OF TULSA, OKLAHOMA  
 SALES TAX OVERVIEW COMMITTEE  
 TRANSPORTATION PROJECTS STATUS REPORT

Design & Construction as of:

03/01/23

DESIGN							CONSTRUCTION					
Budget Number	Project Description	Estimated Start Date	Currently Anticipated Completion Date	Engineer	Contract Amount	Pct Compl	Adv or Contract Award Date	Currently Anticipated Completion Date	Contractor	Contract Amount	Pct Compl	
2037B0404Z	Bridge #404											
2037B0346Z	Bridge #346											
2037B0423Z	Bridge #423			Benham								
2037B0424Z	Bridge #424											
2037B1000Z	Citywide Bridge Rehab and Inspection											
<b>Citywide Projects</b>												
<b>Citywide ADA Transition Plan Impl &amp; Update (ROW)</b>												
2036X0001Z	Transition Plan Update											
2036X0002Z	Transit Stops			BKL								
2036X0003Z	Signalized Intersections			BKL								
2036S0001Z	Sidewalk Corridors			BKL								
2036X0004Z	Citywide Infrastructure Partnership Funds											
2036N0001Z	Citywide Non-Arterial Routine & Preventive											
2036A1000Z	Citywide Arterial Routine and Preventive											
2036A1001Z	Pavement Reinspection											
2035X0001Z	Transit-MTTA-Route 66 Bus Rapid Transit			HNTB	\$1,317	60%						
<b>Traffic Engineering</b>												
2036X0005Z	Signal Coordination & Communication											
2036X0006Z	Signal Installation, Repair and Replace											
2036X0007Z	Traffic Calming											
2036X0008Z	Lighting Repair and Replacement											
2036X0009Z	Pavement Markings and Signs											
2036X0010Z	Guardrail Repair and Replacement											
2039X0009Z	Traffic Studies											
<b>Bicycle-Pedestrian Infrastructure</b>												
2036S0002Z	Go Plan Implementation - Engineering			Garver								
2036S0003Z	Go Plan Implementation-Traffic Operation			Traffic								
2036S0004Z	Arterial Sidewalk			Strt & Strmwtr								
2036S0005Z	Non Arterial Sidewalk			Strt & Strmwtr								
2036X0011Z	Arena District Mstr Plan Implementation			MKSK								
<b>TOTAL FUNDS 4281-4285 - 2020 STREETS GENERAL OBLIGATION BOND</b>												

\* Same design contract for \$35,000  
 \*\* Same design contract for \$15,000  
 Total contract with Becco is \$4,448,000 for stormwater project 993311 & street projects 6008-014180 & 6312-994526

# Finance and Economic Indicators



# STOC

SALES TAX OVERVIEW COMMITTEE

Ashley Webb  
Chair

Ashley R. Webb  
Riggs, Abney, Neal, Turpen, Orbison & Lewis Inc.  
Attorney At Law  
Tulsa, OK 74119  
(918) 699-8905

**To:** City Council  
**Date:** May 3, 2023  
**Subject:** May Report to City Council

Attached is the April 2023 Sales Tax Overview Committee (STOC) Status Report

## **2006 Special Extended Sales Tax**

March expenditures totaled \$1,000, of which \$1,000 was spent on the Public Facilities Renovation project. Encumbrances and commitments total \$5,789,000. Current appropriations for the 2006 Special Extended Sales Tax Fund total \$272,920,000. There is a current appropriation balance of \$3,356,000.

## **2008 Sales Tax Special Temporary Streets**

There were no expenditures in March. Encumbrances and commitments total \$158,000. Current appropriations for the 2008 Sales Tax Special Temporary Streets Fund total \$145,494,000. There is a current appropriation balance of \$38,000.

## **2014 Sales Tax**

March expenditures totaled \$4,177,000, of which \$1,953,000 was spent on the Arterial Street Rehabilitation & Citywide project. Encumbrances and commitments total \$41,977,000. Current appropriations for the 2014 Sales Tax Fund total \$579,640,000. There is a current appropriation balance of \$133,510,000.

## **2016 Sales Tax**

March expenditures totaled \$5,660,000, of which \$4,738,000 was spent on the debt service for the Tulsa Vision advanced sales tax revenue bonds. Encumbrances and commitments total \$3,740,000. Current appropriations for the 2016 Sales Tax Fund total \$256,927,000. There is a current appropriation balance of \$44,311,000.

## **2016 Revenue Bond**

March expenditures totaled \$4,011,000, of which \$2,002,000 was spent on the Gilcrease Museum Expansion project. Encumbrances and commitments total \$56,799,000. Current appropriations for the 2016 Revenue Bond Fund total \$350,600,000. There is a current appropriation balance of \$18,381,000.

## **2020 Sales Tax**

March expenditures totaled \$5,884,000, of which \$4,925,000 was spent on the Fire Apparatus and Equipment project. Encumbrances and commitments total \$15,876,000. Current appropriations for the 2020 Sales Tax Fund total \$73,956,000. There is a current appropriation balance of \$19,394,000.

**2020 General Obligation Bonds**

March expenditures totaled \$1,393,000, of which \$625,000 was spent on the citywide non-arterial Routine & Preventative maintenance project. Encumbrances and commitments total \$20,501,000. Current appropriations for the 2020 General Obligation Bonds Fund total \$149,015,000. There is a current appropriation balance of \$103,312,000.

**2014 General Obligation Bonds**

March expenditures totaled \$1,634,000, of which \$382,000 was spent on the Apache & Harvard Intersect project. Encumbrances and commitments total \$35,015,000. Current appropriations for the 2014 General Obligation Bonds Fund total \$313,615,000. There is a current appropriation balance of \$55,069,000.

**2008 General Obligation Bonds**

There were no expenditures in March. Encumbrances and commitments total \$5,602,000. Current appropriations for the 2008 General Obligation Bonds Fund total \$230,055,000. There is a current appropriation balance of \$3,765,000.

**2005 General Obligation Bonds**

March expenditures totaled \$25,000, of which \$19,000 was spent on the Uniform Division Southwest Renovation project. Encumbrances and commitments total \$1,000. Current appropriations for the 2005 General Obligation Bonds Fund total \$74,919,000. There is a current appropriation balance of \$73,000.

Respectfully submitted,

Ashley Webb, Chair



Attachments

cc: Tammy Pitts  
Jarrod Moore  
Jake Epp



## FINANCIAL REPORT TO CITY COUNCIL

Wednesday, May 3, 2023

### I. Financial Report

*Revenue: 2016 Vision 0.805 Percent and 2020 Sales Tax 0.45 Percent Sales Tax Funds*

	Fiscal Year to Date	
	April	Thru April
Actual	\$ 9,378,599	\$ 98,843,616
Adopted Budget - Current Year	8,770,985	93,631,174
<b>Actual vs Budget</b>	<b>\$ 607,614</b>	<b>\$ 5,212,442</b>

### Expenditures

Fund	March	Fiscal Year to Date Thru March
409 - 2020 Sales Tax	\$ 5,883,816	\$ 19,789,958
4001, 4003-4004 - Tulsa Vision Rev Bonds	4,011,113	32,633,371
4000 - Tulsa Vision Sales Tax	5,660,177	56,653,595
405 - 2014 Sales Tax	4,177,261	24,229,390
404 - 2008 Streets Temporary Sales Tax	-	67,687
402 - 2006 Special Extended Sales Tax	907	2,482,575
<b>TOTAL \$</b>	<b>19,733,274</b>	<b>\$ 135,856,576</b>

### II. Expenditures in Other Funds

Fund	March	Fiscal Year to Date Thru March
401 - 2001 Sales Tax	-	\$ -
428 - 2020 GO Bond	1,392,717	13,934,888
427 - 2014 GO Bond	1,633,739	13,064,004
426 - 2008 GO Bond	-	2,416,593
425 - 2005 GO Bond	25,326	25,326
<b>TOTAL \$</b>	<b>3,051,782</b>	<b>\$ 29,440,811</b>

### III. Items for the City Council's Attention

- A. Monthly Financial Reports
- B. STOC Committee and Subcommittee Minutes and Reports

### IV. Attachments

- A. Attendance Record for the last 12 months
- B. STOC Committee and Subcommittee Minutes and Reports

Respectfully submitted,

Ashley R. Webb, Chair

Attachments

cc: Tammy Pitts  
Jarrod Moore  
Jake Epp

**MAJOR CAPITAL IMPROVEMENTS CONSTRUCTION FUNDS SUMMARY**  
**As of March, 2023**

	CURRENT		EXPENDITURES		ENCUMBERED		PERCENT	BALANCE			
	APPROPRIATIONS		Current Month	Life To Date	COMMITTED						
Fund 401 and Fund 403											
<b>2001 Third Penny Sales Tax and 2006 Advance Funded Sales Tax</b>	\$	112,611,653	\$	-	\$	112,531,735	\$	(0)	100%	\$	79,918
Fund 402											
<b>2006 Third Penny Sales Tax Extension</b>	\$	272,920,362	\$	907	\$	263,775,069	\$	5,789,107	99%	\$	3,356,186
Fund 404											
<b>2008 Sales Tax Special Temporary Streets Fund</b>	\$	145,493,500	\$	-	\$	145,298,037	\$	157,931	100%	\$	37,532
Fund 405											
<b>2014 Sales Tax Fund</b>	\$	579,639,705	\$	4,177,261	\$	404,152,780	\$	41,976,548	77%	\$	133,510,377
Fund 406: 4000											
<b>2016 Sales Tax Fund</b>	\$	256,926,895	\$	5,660,177	\$	208,875,933	\$	3,740,424	83%	\$	44,310,538
Fund 406: 4001, 4003, 4004											
<b>2016 Revenue Bond Fund</b>	\$	350,600,000	\$	4,011,113	\$	275,420,360	\$	56,798,796	95%	\$	18,380,844
Fund 409											
<b>2020 Sales Tax Fund</b>	\$	73,955,556	\$	5,883,816	\$	38,685,563	\$	15,875,534	74%	\$	19,394,459
Fund 428											
<b>2020 General Obligation Bonds</b>	\$	149,015,000	\$	1,392,717	\$	25,202,302	\$	20,500,731	31%	\$	103,311,967
Fund 427											
<b>2014 General Obligation Bonds</b>	\$	313,615,000	\$	1,633,739	\$	223,531,170	\$	35,014,821	82%	\$	55,069,009
Funds 426											
<b>2008 General Obligation Bonds</b>	\$	230,054,937	\$	-	\$	220,687,408	\$	5,602,233	98%	\$	3,765,296
Funds 425											
<b>2005 General Obligation Bonds</b>	\$	74,919,257	\$	25,326	\$	74,845,023	\$	832	100%	\$	73,403
Fund 740: 7401-7408											
<b>TMUA--Water Capital Fund</b>	\$	455,071,405	\$	3,476,741	\$	348,136,661	\$	55,396,571	89%	\$	51,538,174
Funds 750: 7501-7522											
<b>TMUA-Sanitary Sewer Capital Funds</b>	\$	581,286,957	\$	7,308,403	\$	464,280,318	\$	60,525,357	90%	\$	56,481,282



# Report On Tulsa Economic Indicators February 2023

## Economic Overview

Economic Overview will be updated at the end of every quarter. The Next EO summary will be posted with the March 2023 Report.

## Wage & Salary Employment Conditions

Labor force participation fell 486,900 in February, reporting a total of 486,900 . Compared to the previous month, this was a decrease of (510) or -0.1% in Labor Participants. Meanwhile, the Total Employment survey reported an increase of 40 positions within the metro area. This was an increase of 0.0% over the previous month and reported a total of 471,740 . The area unemployment rate was reported at 3.1% for February which fell from the January number of 3.2%. Total unemployment for the area was 2.9% this time last year. Regarding the second employment survey, Wage and Salary Employment increased by 1,500 in February, to report a total of 453,800 . The Manufacturing sector decreased by (600) positions in February, totaling 48,500 positions. The Service sector remained stable at - positions in February, totaling 230,400 positions. Trade decreased by (900) positions in February, totaling 87,200 positions.

## Freight Conditions

TIA reported February boarding at 99,310 passengers. Outgoing passenger counts fell by (2,711) over the previous month. This time last year, the airport reported a total of 78,296 for the month. February cargo fell at the TIA, decreasing by (2,711) tons, and reporting a total of 99,310 tons shipped in February. Lastly, freight at the Port of Catoosa reported 183,294 of barge tonnage for the month. This is a decrease vs. previous month by -1,820,670 in barge tonnage.

## Enterprise Customers

Sewer customer totals increased by 35 customers in February, totaling 134,806 for the month. The current customer base is -2.1% less than this time last year. Water Customers also increased by 18 customers in February, totaling 146,794 for the month. The current customer base is 0.2% greater than this time last year.

## Price Indices

PPI fell -0.1% in February to 209.9

MCI moved up 0.0% in February to 308.5

CPI-U moved up 0.4% in February to 285.1<sup>i</sup>

20 Year GO Bond rates moved up 19 basis points to 3.64% in February

~~Revenue Bond rates remained stable at 0 basis points to 0.00% in February (No Data this month)~~

30-Day Treasury Bill rates moved up 1.58 basis points to 4.356% in February

# Tulsa Economic Indicators

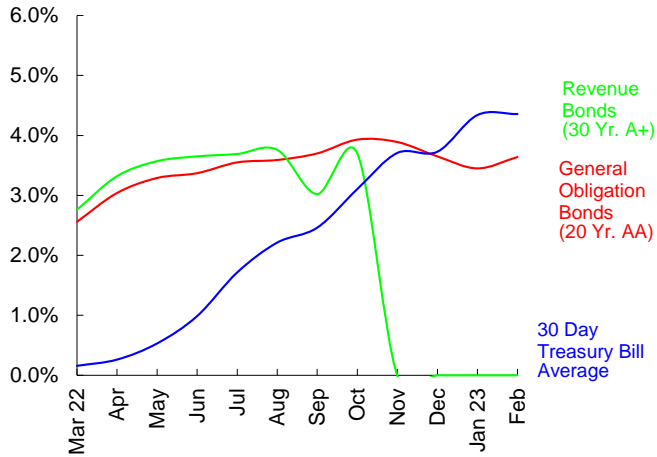
## Most Recent Twelve Months

(unless otherwise Indicated)


	March 22 to February 23	March 21 to February 22	Change
<b>Wage &amp; Salary</b>			
<b>Employment (TMSA 12 Mo. Avg.):</b>			
	<u>Feb-23</u>	<u>Feb-22</u>	
Manufacturing	48,800	46,700	4.5%
Services	231,800	223,200	3.9%
Trade	89,900	84,600	6.3%
Other	<u>88,200</u>	<u>86,700</u>	1.7%
<b>Total</b>	458,700	441,200	4.0%
<b>Unemployment Rates (TMSA 12 Mo. Avg.):</b>			
	<u>Feb-23</u>	<u>Feb-22</u>	
Tulsa MSA	3.2%	3.1%	0.1%
Oklahoma	3.1%	3.2%	-0.1%
United States	3.5%	5.0%	-1.5%
<b>Air Passengers (Calendar YTD):</b>			
	<u>Feb-23</u>	<u>Feb-22</u>	
<b>Barge Tonnage (Calendar YTD):</b>	100,700	158,000	(36.3%)
	1,093,600	264,200	>100.00%
<b>Price and Cost Indices:</b>			
	<u>Feb-23</u>	<u>Feb-22</u>	
Consumer Price Index - Urban	285.1	269.6	5.7%
Producer Price Index	209.9	221.4	(5.2%)
Municipal Cost Index (Est.)	308.5	294.8	4.6%
(Indices are not adjusted for seasonality)			
<b>Financial Rates (Monthly Avg.):</b>			
	<u>Feb-23</u>	<u>Feb-22</u>	
30-Day Treasury Bill	4.356%	0.03%	4.33
Municipal General Obligation Bond			
Buyer 11 Bond Index (20 Yr. A-AAA)	3.64%	2.44%	1.20
Municipal Revenue Bond Buyer			
25 Bond Index (25 Yr. A-AA+)	0.00%	2.36%	(2.36)
<b>Utilities:</b>			
	<u>Feb-23</u>	<u>Feb-22</u>	
Water Customers	146,800	146,400	0.3%
Sewer Customers	134,800	137,700	(2.1%)

\*Data unavailable at time of report. Therefore figure is a 12 month average forecast.


**Rates on Municipal Investments and Cost of Financing\*\***




**Consumers, Producers, and Municipal Price/Cost Indices**

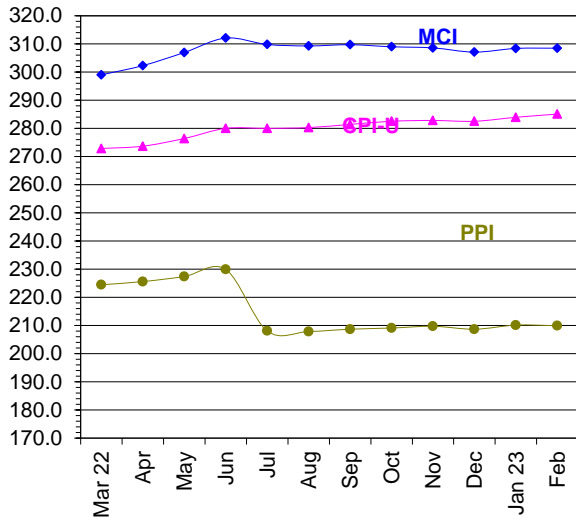

**Monthly (- -) and Average (—) Unemployment Rates (Most Recent 12 Months)**

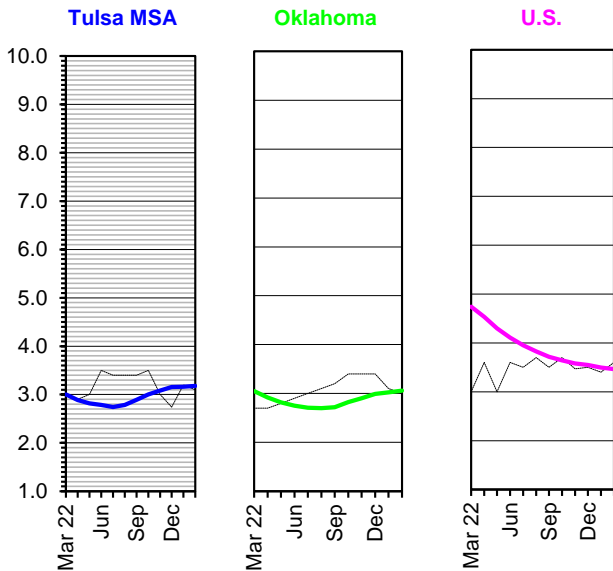

**Tulsa MSA Wage & Salary Employment and 12 Month Moving Average (000's)**

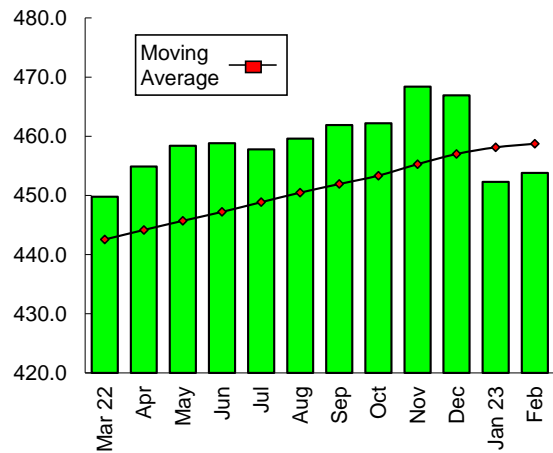


\*Data unavailable at time of report. Therefore figure is a 12 month average forecast.

**Short Term Capital Purchases Summary (Fund 477) as of March 2023  
2006 Sales Tax Capital Equipment Replacement Report**

<b>Department/Entitiy</b>	<b>Appropriations</b>	<b>Month's Expenditures</b>	<b>Year to Date Expenditures</b>	<b>Encumbrances Commitments</b>	<b>Balance</b>
Human Resources	\$ 107,042	\$ -	\$ 32,145	\$ 57,440	\$ 17,457
Finance	\$ 58,000	\$ -	\$ 2,084	\$ 54,474	\$ 1,442
Customer Care	\$ 365,000	\$ -	\$ 241,532	\$ 105,860	\$ 17,608
Legal	\$ 4,800	\$ -	\$ -	\$ -	\$ 4,800
Asset Management	\$ 987,363	\$ 26,381	\$ 172,604	\$ 538,775	\$ 275,983
Information Technology	\$ 7,845,568	\$ 274,553	\$ 4,295,811	\$ 1,155,289	\$ 2,394,468
Police	\$ 6,083,536	\$ 87,902	\$ 3,775,925	\$ 2,160,707	\$ 146,904
Fire	\$ 4,672,842	\$ 1,709,566	\$ 2,216,866	\$ 58,892	\$ 2,397,084
Municipal Court	\$ 11,406	\$ -	\$ 11,406	\$ -	\$ -
Engineering Services	\$ 457,616	\$ 5,308	\$ 168,069	\$ 101,925	\$ 187,622
Streets & Stormwater	\$ 4,414,521	\$ 123	\$ 560,522	\$ 3,729,553	\$ 124,446
Parks & Recreation	\$ 1,360,550	\$ 23,013	\$ 98,373	\$ 872,853	\$ 389,324
Manage Entities - Culture & Recreation	\$ 193,000	\$ -	\$ -	\$ -	\$ 193,000
WIN	\$ 385,946	\$ -	\$ 40,100	\$ -	\$ 345,846
Development Services	\$ 243,050	\$ -	\$ -	\$ 217,896	\$ 25,154
Transfer to Other Funds*	\$ 138,000	\$ 15,000	\$ 138,000	\$ -	\$ -
Transfer to River Parks*	\$ 36,000	\$ -	\$ 36,000	\$ -	\$ -
Transfer to Tulsa Transit*	\$ 115,000	\$ -	\$ 115,000	\$ -	\$ -
	<b>\$ 27,479,240.00</b>	<b>\$ 2,141,845.35</b>	<b>\$ 11,904,437.79</b>	<b>\$ 9,053,663.64</b>	<b>\$ 6,521,138.57</b>

\* Total appropriation is transferred to the agency in a lump sum during the year and incorporated into their budget.

City of Tulsa  
Department of Finance  
**FINANCIAL REPORT**



**SALES TAX OVERVIEW COMMITTEE**

PERIOD ENDING **March 28, 2023**

**City of Tulsa**  
**Department of Finance**  
**FINANCIAL REPORT**



**G. T. Bynum**  
**Mayor**

**Tammy Pitts**  
**Director of Finance**

MAYOR

G. T. Bynum

CITY COUNCIL

VANESSA HALL-HARPER.....DISTRICT 1  
JEANNIE CUE .....DISTRICT 2  
CRISTA PATRICK.....DISTRICT 3  
LAURA BELLIS.....DISTRICT 4  
GRANT MILLER.....DISTRICT 5  
CHRISTIAM BENGEL .....DISTRICT 6  
LORI DECTER WRIGHT .....DISTRICT 7  
PHIL LAKIN JR .....DISTRICT 8  
JAYME FOWLER .....DISTRICT 9

CITY AUDITOR

CATHY CRISWELL

SALES TAX OVERVIEW COMMITTEE

Ashley Webb, Chair  
Kathy Sebert, Vice Chair  
Janae Bradford, Secretary

Charles Wilkes	Linda Jenkins
Paul McTighe	Sylvia Powell
Diamond Marshall	Renee Plocek
	Ashley Webb
Kathy Sebert	Jeff Covington
	Alex Gomez
Matt Meyer	Janae Bradford
Jonathan Hall	Steve King
Scott Grizzle	Steven Watts
Pamela Amburgy	Mareo Johnson
Marcia Bruno-Todd	

**SALES TAX OVERVIEW COMMITTEE REPORT**  
**Table of Contents**

<u>FUND NO.</u>	<u>PAGE NO.</u>
<b>TABLE OF CONTENTS .....</b>	<b>3</b>
<b>CONSOLIDATED REPORTS</b>	
Balance Sheets .....	4
Schedule of Sales Tax Revenue .....	5
<b>402.....2006 SPECIAL EXTENDED SALES TAX.....</b>	<b>6</b>
Statement of Revenue, Expenditures, and Encumbrances.....	7
<b>405.....2014 EXTENDED 1.1% SALES TAX.....</b>	<b>10</b>
Statement of Revenue, Expenditures, and Encumbrances.....	11
<b>409.....2020 SALES TAX.....</b>	<b>15</b>
Statement of Revenue, Expenditures, and Encumbrances.....	16
<b>4000 .....2016 LIMITED PURPOSE TEMPORARY SALES TAX .....</b>	<b>18</b>
Statement of Revenue, Expenditures, and Encumbrances.....	19
<b>4001 .....2016 VISION ADVANCE FUNDED REVENUE BOND FUND .....</b>	<b>21</b>
Statement of Revenue, Expenditures, and Encumbrances.....	22
<b>4003 .....2016 VISION ADVANCE FUNDED REVENUE BOND FUND .....</b>	<b>24</b>
Statement of Revenue, Expenditures, and Encumbrances.....	25
<b>4004 .....2016 VISION ADVANCE FUNDED REVENUE BOND FUND .....</b>	<b>27</b>
Statement of Revenue, Expenditures, and Encumbrances.....	28
<b>4260-4266.....2008 GO BOND FUNDS .....</b>	<b>30</b>
Statement of Revenue, Expenditures, and Encumbrances.....	31
<b>4270-4276.....2014 GO BOND FUNDS .....</b>	<b>34</b>
Statement of Revenue, Expenditures, and Encumbrances.....	35
<b>4281-4283.....2020 GO BOND FUNDS .....</b>	<b>38</b>
Statement of Revenue, Expenditures, and Encumbrances.....	39
<b>COMBINED STATEMENT OF OTHER FUND ACTIVITY .....</b>	<b>43</b>
(400, 401, 403, 404, 425) .....	44
<b>BUDGET ACTIONS.....</b>	<b>45</b>



**CITY OF TULSA, OKLAHOMA  
SALES TAX OVERVIEW COMMITTEE REPORT  
BALANCE SHEET  
MARCH 2023**

	FUND 402 2006 SPECIAL EXTENDED SALES TAX	FUND 405 2014 EXTENDED 1.1% SALES TAX	FUND 409 2020 SALES TAX	FUND 4000 2016 LIMITED PURPOSE TEMPORARY SALES TAX	FUNDS 4260 through 4266 2008 GO BOND FUNDS	FUNDS 4270 through 4276 2014 GO BOND FUNDS	FUNDS 4281 through 4285 2020 GO BOND FUNDS	TOTAL
<b>ASSETS:</b>								
POOLED EQUITY WITH TREASURER ACCRED INTERST RECEIVABLE	\$9,455,867.93	\$183,679,022.42	\$38,911,461.65	\$75,263,000.47	\$10,584,610.85	\$187,259,924.64	\$28,659,460.53	\$505,153,887.96
OTHER CURRENT RECEIVABLES	27,301.32	541,316.48	112,267.54	213,740.52				\$894,625.86
TAX RECEIVABLE			5,739,510.29	10,267,346.18				\$16,006,856.47
				1,637,650.87				\$1,637,650.87
<b>TOTAL ASSETS</b>	<b>\$9,483,169.25</b>	<b>\$184,220,338.90</b>	<b>\$44,763,239.48</b>	<b>\$87,381,738.04</b>	<b>\$10,584,610.85</b>	<b>\$187,259,924.64</b>	<b>\$28,659,460.53</b>	<b>\$523,693,021.16</b>
<b>LIABILITIES, RESERVES, AND FUND BALANCE:</b>								
<b>LIABILITIES AND RESERVE FOR ENC.:</b>								
ACCOUNTS PAYABLE		72,394.10				6,652.56	13,101.46	79,046.66
CONTRACTS PAYABLE - RETAINAGE	186,824.90	2,744,585.94	495.40	1,110,117.02	506,909.77	1,794,442.47	208,661.40	6,343,375.50
CONTRACTS RETAINAGE CLEAR		20,413.40			294,095.52			314,508.92
PURCHASING CARD ESCROW								
DUE TO OTHER FUNDS		110,149.30						110,149.30
ADVANCES FROM OTHER FUNDS								
RESERVE FOR ENCUMBRANCES	876,187.12	41,176,933.51	14,577,588.65	3,620,787.91	5,587,848.44	34,731,401.30	18,457,347.47	100,570,746.93
RESERVE FOR COMMITMENTS								
<b>UNENCUMBERED FUND BALANCE:</b>								
APPROPRIATED	3,356,185.98	133,510,377.29	19,394,459.13	44,310,538.04	3,765,296.12	55,069,008.62	9,980,350.20	259,405,865.18
UNAPPROPRIATED	5,063,971.25	6,585,485.36	10,790,696.30	38,340,295.07	430,461.00	95,658,419.69		156,869,328.67
RESERVED FOR ADVANCES								
<b>TOTAL FUND BALANCE</b>	<b>8,420,157.23</b>	<b>140,095,862.65</b>	<b>30,185,155.43</b>	<b>82,650,833.11</b>	<b>4,195,757.12</b>	<b>150,727,428.31</b>	<b>9,980,350.20</b>	<b>416,275,193.85</b>
<b>TOTAL LIABILITIES, RESERVES, AND FUND BALANCE</b>	<b>\$9,483,169.25</b>	<b>\$184,220,338.90</b>	<b>\$44,763,239.48</b>	<b>\$87,381,738.04</b>	<b>\$10,584,610.85</b>	<b>\$187,259,924.64</b>	<b>\$28,659,460.53</b>	<b>\$523,693,021.16</b>

**CITY OF TULSA, OKLAHOMA**  
**SALES TAX OVERVIEW COMMITTEE REPORT**  
**SCHEDULE OF SALES TAX REVENUE**  
 March 2023

Month	COMPARISON TO BUDGET (2022-2023)			COMPARISON TO PRIOR YEAR				
	BUDGET	ACTUAL	DIFFERENCE	2021-2022	2022-2023	AMOUNT	PERCENT	
	AMOUNT	AMOUNT		ACTUAL	ACTUAL	INCREASE (DECREASE)	INCREASE/DECREASE ACTUAL BUDGET	
July	\$ 9,362,635.00	\$ 9,845,859.25	\$ 483,224.25	\$ 8,204,546.00	\$ 9,845,859.25	\$ 1,641,313.25	20.0%	14.1%
August	\$ 9,583,941.00	\$ 10,095,265.54	511,324.54	\$ 8,300,632.00	\$ 10,095,265.54	1,794,633.54	21.6%	15.5%
September	\$ 9,318,082.00	\$ 9,641,274.74	323,192.74	\$ 8,125,952.00	\$ 9,641,274.74	1,515,322.74	18.6%	14.7%
October	\$ 9,324,195.00	\$ 10,019,197.63	695,002.63	\$ 8,122,870.00	\$ 10,019,197.63	1,896,327.63	23.3%	14.8%
November	\$ 9,268,158.00	\$ 9,615,664.08	347,506.08	\$ 8,041,056.00	\$ 9,615,664.08	1,574,608.08	19.6%	15.3%
December	\$ 9,248,814.00	\$ 9,937,888.82	689,074.82	\$ 8,140,730.00	\$ 9,937,888.82	1,797,158.82	22.1%	13.6%
January	\$ 9,851,373.00	\$ 10,072,232.25	220,859.25	\$ 8,606,939.00	\$ 10,072,232.25	1,465,293.25	17.0%	14.5%
February	\$ 9,601,051.00	\$ 10,361,581.82	760,530.82	\$ 8,435,116.00	\$ 10,361,581.82	1,926,465.82	22.8%	13.8%
March	\$ 8,631,254.00	\$ 9,821,460.85	1,190,206.85	\$ 7,425,426.00	\$ 9,821,460.85	2,396,034.85	32.3%	16.2%
April	\$ 8,770,985.00			\$ 7,819,042.00				12.2%
May	\$ 9,602,020.00			\$ 8,057,614.00				19.2%
June	\$ 9,171,752.00			\$ 7,649,339.00				19.9%
<b>TOTAL</b>	<b>\$ 111,734,260.00</b>	<b>\$ 89,410,424.98</b>	<b>\$ 5,220,921.98</b>	<b>\$ 96,929,262.00</b>	<b>\$ 89,410,424.98</b>	<b>\$ 16,007,157.98</b>	<b>21.8%</b>	<b>15.3%</b>

PERCENT INCREASE (DECREASE) 5.84%

# **2006 SPECIAL EXTENDED SALES TAX**

**FUND 402**

**(SIXTH THIRD PENNY SALES TAX PROGRAM)**

**CITY OF TULSA, OKLAHOMA  
SALES TAX OVERVIEW COMMITTEE REPORT  
FUND 402 - 2006 SPECIAL EXTENDED SALES TAX**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES  
FOR THE NINE MONTHS ENDED MARCH 31, 2023**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<b><u>Revenue</u></b>					
Sales Tax	\$	\$	\$	\$ 430,935,953.99	\$
Donations					
Interest on Investments		15,763.52	118,028.72	16,468,756.89	(118,028.72)
Intergovernmental Revenue					
Federal, State & Local grants					
Transfers from other funds					
Miscellaneous Revenue				1,424,225.61	
Total Revenue		15,763.52	118,028.72	448,828,936.49	-118,028.72
<b><u>Expenditures</u></b>					
Project Expenditures	271,811,704.47	906.73	2,557,821.38	263,522,345.69	8,289,358.78
Total Expenditures	271,811,704.47	906.73	2,557,821.38	263,522,345.69	8,289,358.78
Excess (Deficiency) of Revenue Over Expenditures			(2,439,792.66)	185,306,590.80	
Completed Projects Encumbrances			5,789,107.11	5,789,107.11	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(8,228,899.77)	5,100,896.70	
June 30, 2022 Ending Fund Balance			12,345,345.27		
Prior year expenditures					
June 30, 2022 Encumbrances			984,451.20		
Adjusted Beginning Fund Balance			13,329,796.47		
Ending Fund Balance			\$ 5,100,896.70	\$ 5,100,896.70	

**Fund 402**  
**2006 SPECIAL EXTEND SALES TAX**

as of: 3/31/2023

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
402	016100	Forensic Lab Expansion	14,729,241.90	0.00	0.00	14,729,241.90	0.00	0.00	0.00
402	016130	Replace 2 Police Helicopters	4,344,475.00	0.00	0.00	4,344,475.00	0.00	0.00	0.00
402	016200	Apparatus Replacement	12,863,575.91	0.00	0.00	12,863,575.91	0.00	0.00	0.00
402	016240	Site Acq. For Addnl. Station	5,300,000.00	0.00	253,126.13	4,833,832.22	2,256.75	0.00	463,911.03
402	016310	Network System Replacement	1,402,150.04	0.00	0.00	1,402,150.04	0.00	0.00	0.00
402	017110	General Park Improvements	4,829,359.78	0.00	0.00	4,816,917.98	441.80	0.00	12,000.00
402	017120	Golf Course Development	459,640.57	0.00	0.00	459,640.57	0.00	0.00	0.00
402	017140	Tulsa Zoo Department	2,938,780.81	0.00	0.00	2,938,780.81	0.00	0.00	0.00
402	060020	Comprehensive Plan Update	649,253.49	0.00	0.00	649,253.49	0.00	0.00	0.00
402	060040	Equipment Mgmt Projects	2,242,000.00	0.00	0.00	2,242,000.00	0.00	0.00	0.00
402	062100	Unservd Area & Offsite Mns	7,200,000.00	0.00	0.00	7,200,000.00	0.00	0.00	0.00
402	062120	Sswwtp 71 Ls Expansion	400,000.00	0.00	0.00	400,000.00	0.00	0.00	0.00
402	062130	Spunky Crk Bsn Ms & Ls	9,497,696.77	0.00	0.00	9,497,696.77	0.00	0.00	(0.00)
402	062140	Lower Bird Creek Wwtp Expn	11,000,000.00	0.00	0.00	11,000,000.00	0.00	0.00	0.00
402	063101	Fred Creek Drainage Imprv	12,250,000.00	0.00	0.00	12,250,000.00	0.00	0.00	(0.00)
402	063106	Elm Crk 6th St Drainage	2,000,000.00	0.00	0.00	2,000,000.00	(0.00)	0.00	(0.00)
402	063107	Citywide Mdp Updates	450,000.00	0.00	0.00	450,000.00	0.00	0.00	0.00
402	063109	Engr And Insp Svc-Fc	500,000.00	0.00	0.00	500,000.00	0.00	0.00	0.00
402	064001	Arterial Streets Rehab	28,169,343.33	0.00	548.47	28,116,232.47	11,612.76	0.00	41,498.10
402	064002	Residential Streets Rehab	25,849,169.10	0.00	33,995.30	25,849,169.10	0.00	0.00	0.00
402	064003	Traffic Signals & Lighting	2,600,000.00	30.00	30.00	2,600,000.00	0.00	0.00	(0.00)
402	064004	TRAFFIC SIGNAL SYNCH	1,700,000.00	0.00	0.00	1,692,173.06	0.00	0.00	7,826.94
402	064005	St Surface Rpr & Crack Seal	10,000,000.00	0.00	0.00	10,000,000.00	0.00	0.00	0.00
402	064060	Bridge Replacement	2,500,000.00	0.00	0.00	2,499,613.73	385.00	0.00	1.27
402	064062	Bridge Rehab/Repair Cw	2,500,000.00	426.80	6,956.48	2,488,162.31	11,837.69	0.00	(0.00)
402	064093	City Match-Fed/St/Co Projs	1,500,000.00	0.00	0.00	1,410,000.00	90,000.00	0.00	0.00
402	064101	41St-Garnett To 129Th E Ave	500,000.00	0.00	0.00	498,500.00	1,500.00	0.00	(0.00)
402	064102	81St-Memorial To Mingo	7,402,272.09	0.00	0.00	7,402,272.09	0.00	0.00	0.00
402	064103	91St & Harvard Intersection	2,217,000.00	0.00	0.00	2,217,000.00	0.00	0.00	0.00
402	064104	91St And Sheridan Inters	4,417,718.54	0.00	0.00	4,414,613.00	0.00	0.00	3,105.54
402	064105	61St St Riverside To Peoria	800,000.00	0.00	104.67	705,989.93	23,660.27	0.00	70,349.80
402	064106	Garnett-11Th To I-244	500,000.00	0.00	0.00	499,555.00	0.00	0.00	445.00
402	064107	Mingo 71St To 81St	500,000.00	0.00	0.00	498,721.40	0.00	0.00	1,278.60
402	064108	Pine St-Memorial To Mingo	500,000.00	0.00	0.00	487,498.67	(0.00)	0.00	12,501.33
402	064109	129Th-31St To 41St	5,500,000.00	0.00	0.00	5,500,000.00	0.00	0.00	0.00
402	064110	61St-Riverside To Peoria	7,369,000.00	0.00	0.00	7,369,000.00	0.00	0.00	0.00
402	064111	91St-Memorial To Mingo	500,000.00	0.00	0.00	59,808.17	0.00	0.00	440,191.83
402	065100	Public Facilities Renov	7,080,000.00	449.93	1,231.72	6,797,333.46	227,912.17	0.00	54,754.37
402	065300	Energy Efficiency Facil Impr	1,600,000.00	0.00	0.00	1,134,165.67	0.00	0.00	465,834.33
402	065320	Gilcrease Museum Renovation	4,451,158.00	0.00	0.00	3,342,089.45	410.55	0.00	1,108,658.00
402	065330	Performing Arts Ctr Renova	1,560,000.00	0.00	0.00	1,560,000.00	0.00	0.00	0.00
402	066210	New Fs 11-11Th/177Th	0.00	0.00	0.00	0.00	0.00	0.00	0.00
402	066220	Homeland Sec Equip Facil	2,708,852.22	0.00	0.00	2,708,852.22	0.00	0.00	(0.00)
402	066310	Weather Alert Sirens Repl	1,694,929.61	0.00	0.00	1,694,929.61	0.00	0.00	0.00

**Fund 402**  
**2006 SPECIAL EXTEND SALES TAX**

as of: 3/31/2023

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
402	066320	61St Twr Comm Shelter Repl	299,964.04	0.00	0.00	299,964.04	0.00	0.00	0.00
402	066330	Pwr Prtct Bok Comm Site Bok	104,569.00	0.00	0.00	104,569.00	0.00	0.00	0.00
402	066340	Log Sys 800 Mhz Radio Sys	118,787.61	0.00	0.00	118,787.61	0.00	0.00	0.00
402	066350	Computer Sys Repl/Enhance	511,449.95	0.00	0.00	511,449.95	0.00	0.00	0.00
402	067120	Plgnd Splashpad Park Surfs	3,095,280.61	0.00	0.00	3,024,686.42	0.00	0.00	70,594.19
402	067130	Playground Equip Repl/Renov	1,063,517.00	0.00	0.00	1,054,597.78	0.00	0.00	8,919.22
402	067170	Carl Smith Facil Devel	235,421.96	0.00	0.00	231,991.95	3,430.01	0.00	0.00
402	067510	Trails Resurf And Widening	2,924,423.01	0.00	0.00	2,924,423.01	0.00	0.00	0.00
402	067520	EST BANK IMPR 11TH-21STS	5,250,000.00	0.00	0.00	346,031.29	0.00	4,903,968.71	0.00
402	067530	RVR WST FESTIVAL PRK RENOV	7,491,683.05	0.00	0.00	7,491,683.05	0.00	0.00	0.00
402	067540	RIVER PRKS FACIL REHAB/REPL	345,186.15	0.00	0.00	345,186.15	0.00	0.00	0.00
402	068100	Tda Downtown Prop Acq	1,720,000.00	0.00	0.00	1,720,000.00	0.00	0.00	0.00
402	068110	Kendall Whittier Plan Impl	5,000,000.00	0.00	0.00	5,000,000.00	0.00	0.00	0.00
402	068120	Dirty Butter Crk Acq Ph2	2,096,066.28	0.00	0.00	2,096,066.28	0.00	0.00	0.00
402	068130	Downtown Signage	1,813,710.24	0.00	0.00	1,813,710.24	0.00	0.00	0.00
402	068140	Econ Devel Infrastructure	3,000,000.00	0.00	0.00	3,000,000.00	0.00	0.00	0.00
402	068160	New Parking Garage	5,000,000.00	0.00	2,186,582.21	4,488,308.60	511,691.40	0.00	0.00
402	069100	Mtta System Projects	2,410,000.00	0.00	0.00	2,409,999.89	0.00	0.00	0.11
402	096005	Electronic Ticketing Equip	182,707.40	0.00	0.00	182,707.40	0.00	0.00	0.00
402	144104	Riverside Dr & Rltd Infrstr	250,252.64	0.00	0.00	250,252.64	0.00	0.00	0.00
402	146200	Fire - SCBA	94,389.51	0.00	0.00	94,389.51	0.00	0.00	0.00
402	156000	Radio Sys Upgrd & Assc Equip	3,545,000.00	0.00	0.00	3,545,000.00	0.00	0.00	0.00
402	170101	Capital Equipment	172,000.00	0.00	0.00	172,000.00	0.00	0.00	0.00
402	203400001Z	Tulsa Zoo Department	1,027,836.86	0.00	0.00	451,650.93	0.00	0.00	576,185.93
402	914411	Tulsa Trails	1,492,500.00	0.00	0.00	1,492,500.00	0.00	0.00	(0.00)
402	962301	Tulsa Convention Center Impr	2,000,000.00	0.00	0.00	1,981,869.61	0.00	0.00	18,130.39
402	966120	Gilcrease Exp Osage Exp-41st	4,500,000.00	0.00	0.00	4,500,000.00	0.00	0.00	0.00
			<b>\$ 272,920,362.47</b>	<b>\$ 906.73</b>	<b>\$ 2,482,574.98</b>	<b>\$ 263,775,069.38</b>	<b>\$ 885,138.40</b>	<b>\$ 4,903,968.71</b>	<b>\$ 3,356,185.98</b>

# **2014 EXTENDED 1.1% SALES TAX**

**FUND 405**

**(2014 EXTENDED 1.1% SALES TAX FUND)**

**CITY OF TULSA, OKLAHOMA  
SALES TAX OVERVIEW COMMITTEE REPORT  
FUND 405 - 2014 EXTENDED 1.1% SALES TAX**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES  
FOR THE NINE MONTHS ENDED MARCH 31, 2023**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<b>Revenue</b>					
Sales Tax	\$	\$	\$	\$ 551,323,376.53	\$
Donations					
Interest on Investments		310,535.38	2,264,549.91	18,529,190.39	(2,264,549.91)
Intergovernmental Revenue					
Federal, State & Local grants					
Transfers from other funds					
Miscellaneous Revenue				98,580.75	
Total Revenue		<u>310,535.38</u>	<u>2,264,549.91</u>	<u>569,951,147.67</u>	<u>-2,264,549.91</u>
<b>Expenditures</b>					
Project Expenditures	579,639,705.22	4,177,261.39	32,215,245.09	399,613,259.74	180,026,445.48
Total Expenditures	<u>579,639,705.22</u>	<u>4,177,261.39</u>	<u>32,215,245.09</u>	<u>399,613,259.74</u>	<u>180,026,445.48</u>
<b>Excess (Deficiency) of Revenue</b>					
Over Expenditures			(29,950,695.18)	170,337,887.93	
<b>Completed Projects</b>					
Encumbrances			<u>41,976,547.75</u>	<u>41,976,547.75</u>	
<b>Excess (Deficiency) of Revenue Over</b>					
Expenditures and Encumbrances			(71,927,242.93)	128,361,340.18	
<b>June 30, 2022 Ending Fund Balance</b>					
Prior year expenditures			144,422,310.56		
<b>June 30, 2022 Encumbrances</b>					
			<u>55,866,272.55</u>		
<b>Adjusted Beginning Fund Balance</b>					
			<u>200,288,583.11</u>		
<b>Ending Fund Balance</b>					
			<u>\$ 128,361,340.18</u>	<u>\$ 128,361,340.18</u>	



**Fund 405**

**2014 SALES TAX**

as of: 3/31/2023

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
405	140040	Cng Fuel Expansion	1,800,000.00	0.00	0.00	1,787,810.17	0.00	0.00	12,189.83
405	140050	Radio Frequency ID Devices	750,000.00	0.00	0.00	0.00	0.00	0.00	750,000.00
405	140060	Emd Emergency Generators	200,000.00	0.00	0.00	196,879.85	3,120.15	0.00	0.00
405	140070	Emd Facilities Maintenance	1,000,000.00	0.00	22,955.00	855,975.46	(0.00)	0.00	144,024.54
405	140080	Emd Lights, Hvac, Plumbing	2,300,000.00	0.00	0.00	1,310,944.70	200,542.19	19,615.00	768,898.11
405	140100	Capital Equipment	46,235,000.00	0.00	0.00	46,234,996.00	0.00	0.00	4.00
405	143001	Levee District #12 Rehab	3,400,000.00	0.00	16,401.20	406,618.50	120,002.85	0.00	2,873,378.65
405	144003	Citywide Guardrail Repl	1,000,000.00	13,320.44	54,912.46	534,302.82	62,369.43	0.00	403,327.75
405	144004	CW Traffic Signalization	2,000,000.00	4,051.06	160,550.52	1,417,332.59	66,941.59	0.00	515,725.82
405	144005	Roadway & Pedestrian Lights	1,000,000.00	12,289.28	21,535.35	885,610.45	114,389.55	0.00	0.00
405	144006	Signing Pvmt Mark Dlintion	2,510,000.00	0.00	242,705.12	1,767,148.58	209,423.44	0.00	533,427.98
405	144007	Traffic Calming & Safety	1,000,000.00	0.00	0.00	1,000,000.00	(0.00)	0.00	0.00
405	144008	TRAFFIC SIGNAL INSTALLATION	3,045,164.92	0.00	74,319.50	2,551,928.06	111,302.80	0.00	381,934.06
405	144009	TRAFFIC SIGNAL POLE RPL	1,000,000.00	42,466.20	42,466.20	819,100.37	17,464.78	0.00	163,434.85
405	144010	Creek Turnpike Trail Bridge	200,000.00	0.00	85,316.09	85,316.09	8,583.91	0.00	106,100.00
405	144011	GPS Emgency Vehicle Preemp Sys	400,000.00	0.00	0.00	400,000.00	0.00	0.00	0.00
405	144017	Art Street Rehab & Citywide	127,340,000.00	1,952,969.22	5,553,430.56	72,120,970.47	6,876,785.00	0.00	48,342,244.53
405	144018	Bike Ped Master Plan Improv	4,200,000.00	744.00	19,049.19	4,173,216.08	24,978.92	0.00	1,805.00
405	144019	IDL Entrance Rehab	3,000,000.00	0.00	0.00	3,000,000.00	(0.00)	0.00	0.00
405	144020	Citywide-Arterial Rt&Pv Main	3,120,000.00	0.00	614,860.70	3,037,318.98	(0.00)	0.00	82,681.02
405	144063	Bridge Replacement And Rehab	14,685,000.00	0.00	750,064.90	8,513,517.93	29,126.69	0.00	6,142,355.38
405	144093	Citywide Matching Funds	3,429,500.00	0.00	0.00	3,429,500.00	0.00	0.00	0.00
405	144094	ODOT Rehab & Replacement	3,800,000.00	0.00	27,962.00	3,770,928.06	29,071.94	0.00	0.00
405	144101	Yale Ave 81St - 91St Wdn	35,250,000.00	1,368,561.11	7,158,758.74	14,719,206.79	11,936,232.96	0.00	8,594,560.25
405	144102	81St St Sheridan - Meml Wdn	12,000,000.00	3,495.00	482,749.59	10,116,768.57	107,804.18	0.00	1,775,427.25
405	144103	Yale 96th - 101st St Wdn	13,000,000.00	0.00	0.00	11,406,496.12	168,336.52	0.00	1,425,167.36
405	144104	Riverside Dr & Ritd Infrstr	19,678,159.48	0.00	1,263,954.46	19,657,945.32	20,214.16	0.00	0.00
405	144105	25 W Ave: Edison-Apache (DS-W)	750,000.00	0.00	270,260.08	750,000.00	0.00	0.00	(0.00)
405	144108	Pine St: Mingo-U.S. 169 (DS-W)	500,000.00	0.00	0.00	0.00	0.00	0.00	500,000.00
405	144109	Ada Transition Plan - Street	10,200,000.00	108,390.63	1,240,139.35	6,310,697.41	359,028.21	0.00	3,530,274.38
405	144120	Gilcrease Exp Local Match	7,500,000.00	0.00	4,026.44	3,439,884.37	1,025,000.00	0.00	3,035,115.63
405	145100	Ada Transition Plan - Bldgs	1,275,000.00	0.00	5,692.61	499,305.20	150,550.42	0.00	625,144.38
405	145200	Ada Transition Plan - Parks	1,140,000.00	7,570.00	15,757.00	937,270.19	37,027.05	0.00	165,702.76
405	145300	Public Facilities, Otc	3,295,000.00	0.00	405,559.53	1,413,169.77	13,455.11	352,377.50	1,515,997.62
405	145330	Pac - Fire Alarm System	520,000.00	1,444.55	1,444.55	280,532.62	33,453.30	0.00	206,014.08
405	145340	Pac - Fire Sprinklers	1,140,000.00	0.00	0.00	536,750.40	7,795.85	0.00	595,453.75
405	145350	Pac - Renovations	1,840,000.00	772.17	5,675.45	1,106,676.11	599,816.18	0.00	133,507.71
405	145360	Pac - Fan Coil Replacement	555,000.00	0.00	0.00	548,127.45	6,872.55	0.00	0.00
405	145370	Pac - Hvac Motor Replacement	175,000.00	0.00	0.00	20,000.00	155,000.00	0.00	0.00
405	145380	PAC: Roof Replacement	1,300,000.00	0.00	(0.01)	1,241,015.27	10,353.77	0.00	48,630.96
405	145400	Public Facilities, Roofing	3,000,000.00	527.15	34,486.03	2,355,067.87	636,847.13	0.00	8,085.00
405	145500	Animal Shelter Expn Ph 1	8,850,000.00	0.00	24,053.21	214,191.95	329,317.46	0.00	8,306,490.59
405	145600	Animal Shelter Facility Imp	750,000.00	0.00	0.00	705,467.71	0.00	0.00	44,532.29
405	145610	Gm - Cctv Camera Upgrade	491,854.46	0.00	0.00	491,854.46	0.00	0.00	0.00

**Fund 405**

**2014 SALES TAX**

as of: 3/31/2023

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
405	145620	Gilcrease Lib/Arch Storage	300,000.00	0.00	0.00	300,000.00	0.00	0.00	0.00
405	145630	Helmerich Hall Floor Repl	1,374.12	0.00	0.00	1,374.12	0.00	0.00	(0.00)
405	145640	Gilcrease: Gallery wood floor	0.00	0.00	0.00	0.00	0.00	0.00	0.00
405	145650	GM - Grease Trap & Sewer	54,047.48	0.00	0.00	54,047.48	0.00	0.00	0.00
405	145660	GM - Gallery Lighting Cntrls	218,393.61	0.00	0.00	218,393.61	0.00	0.00	(0.00)
405	145670	GM - Fire Suppression	43,119.58	0.00	0.00	43,119.51	0.00	0.00	0.07
405	145680	Gilcrease: Kitchen renovation	0.00	0.00	0.00	0.00	0.00	0.00	0.00
405	145690	GM - Perimeter Fence	30,595.39	0.00	0.00	30,595.39	0.00	0.00	0.00
405	145700	GM - Public Restroom	11,553.31	0.00	0.00	11,553.31	0.00	0.00	0.00
405	145710	Gilcrease: Restore N Park	0.00	0.00	0.00	0.00	0.00	0.00	0.00
405	145710A	Gilcrease: Restore N Park	0.00	0.00	0.00	0.00	0.00	0.00	0.00
405	145720	GM HVAC Humidification	1,078,145.54	0.00	0.00	976,129.11	0.00	0.00	102,016.43
405	145730	Gilcrease: Chromatic Glass	0.00	0.00	0.00	0.00	0.00	0.00	0.00
405	145740	GM Chilled Water Drive	155,000.00	0.00	0.00	155,000.00	0.00	0.00	0.00
405	145750	GM HVAC Controls	400,000.00	0.00	0.00	400,000.00	0.00	0.00	0.00
405	145760	GM - Halon Fire Suppression	632,623.06	0.00	0.00	632,623.06	0.00	0.00	(0.00)
405	145770	Gilcrease: Parking Expansion	0.00	0.00	0.00	0.00	0.00	0.00	0.00
405	145780	GM - Roof Replacement	1,322,531.58	0.00	0.00	1,322,531.58	0.00	0.00	(0.00)
405	145790	GM - Thoms Gilcrease Roof	518,324.73	0.00	0.00	518,324.73	0.00	0.00	0.00
405	145800	Tulsa Centrl Library Project	10,000,000.00	0.00	0.00	10,000,000.00	0.00	0.00	0.00
405	146100	Helicopter Replacement	2,802,000.00	0.00	0.00	2,802,000.00	0.00	0.00	0.00
405	146110	Police Academy-Crt-Compstat	4,040,000.00	0.00	0.00	2,924,212.92	10,488.26	0.00	1,105,298.82
405	146120	Uniform Division Renovations	3,000,000.00	19,354.98	19,354.98	325,572.80	65,090.20	0.00	2,609,337.00
405	146130	Police Capital Equipment	22,265,000.00	0.00	0.00	22,265,000.00	0.00	0.00	0.00
405	146200	Fire - SCBA	2,600,000.00	0.00	0.00	2,600,000.00	0.00	0.00	0.00
405	146210	Apparatus Replacement	17,000,000.00	0.00	0.00	16,166,371.83	794,765.36	0.00	38,862.81
405	146220	Fire Station Rehabilitation	7,250,000.00	116,151.50	240,421.18	6,594,786.31	386,242.44	0.00	268,971.25
405	146230	Fire Station Generators	1,500,000.00	0.00	387,308.68	1,480,149.52	19,850.48	0.00	0.00
405	146240	Fire Department Facilities	2,000,000.00	2,957.17	7,421.56	176,101.00	66,561.00	0.00	1,757,338.00
405	146300	Financial Sys Replacement	10,000,000.00	0.00	11,680.00	8,517,341.86	657,687.63	0.00	824,970.51
405	146310	Law Enforcement Records Mgmt	7,030,000.00	64,240.00	405,235.77	5,666,150.34	820,311.17	85,000.00	458,538.49
405	147100	Rp - Park Facilities Refurb	4,000,000.00	8,500.00	165,855.40	3,246,610.73	0.00	0.00	753,389.27
405	147120	Reed - Pool Reconstruction	2,410,000.00	0.00	272,438.31	2,349,599.84	60,400.16	0.00	(0.00)
405	147130	Security System Upgrades	160,000.00	0.00	4,985.44	140,896.78	0.00	0.00	19,103.22
405	147140	Tiger & Snow Leopard Exhibit	3,165,497.09	0.00	0.00	3,165,497.09	0.00	0.00	0.00
405	147150	Carnivores Exhibits	8,000,000.00	0.00	0.00	619.32	7,999,380.68	0.00	0.00
405	147160	Hicks Park Improvements	635,000.00	0.00	5,403.56	492,632.88	1,686.55	140,680.57	0.00
405	147170	Hunter: Restroom (Exp & Repr)	400,000.00	0.00	0.00	0.00	0.00	0.00	400,000.00
405	147180	Lacy Park Master Plan - Ph 1	3,600,000.00	0.00	0.00	3,600,000.00	0.00	0.00	(0.00)
405	147190	Water Playgrounds	1,580,000.00	0.00	0.00	1,580,000.00	0.00	0.00	(0.00)
405	147200	Rp - Pedestrian Bridge Imp	7,760,000.00	0.00	0.00	7,743,717.33	16,281.67	0.00	1.00
405	147210	Mohawk Golf Club House	265,000.00	0.00	0.00	185,360.51	0.00	0.00	79,639.49
405	147220	Page Belcher Improvements	400,000.00	0.00	0.00	176,814.20	0.00	0.00	223,185.80
405	147230	Savage Park Improvements	120,000.00	0.00	0.00	15,313.82	8,501.87	0.00	96,184.31

**Fund 405**

**2014 SALES TAX**

as of: 3/31/2023

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
405	147240	Whiteside Plumbing Repairs	355,000.00	0.00	0.00	251,097.34	(0.00)	0.00	103,902.66
405	147250	Woodward: Comp Landscaping	4,850,000.00	42,516.58	595,694.76	1,077,146.49	147,531.31	0.00	3,625,322.20
405	147260	Cousins Park Improvements	1,975,000.00	0.00	0.00	0.00	0.00	0.00	1,975,000.00
405	147270	Carl Smith Improvements	185,000.00	0.00	54,160.00	76,935.35	7,388.98	0.00	100,675.67
405	147300	Chamberlain - Pool Reconstruct	2,424,185.98	0.00	175,426.76	241,526.09	25,057.68	0.00	2,157,602.21
405	147400	Lacy - Pool	2,640,000.00	0.00	0.00	2,633,975.84	2,450.08	0.00	3,574.08
405	147500	Mcclure - Pool	4,725,000.00	0.00	0.00	4,487,848.77	10,372.73	33,985.43	192,793.07
405	147510	Whiteside Pool	1,350,000.00	0.00	0.00	1,342,501.62	3,552.57	0.00	3,945.81
405	147520	Playground Safety Surfaces	7,300,000.00	27,697.67	82,838.37	2,750,933.65	229,271.37	0.00	4,319,794.98
405	148100	Annual Economic Development	6,675,000.00	0.00	225,038.44	4,342,636.61	1,241,135.64	0.00	1,091,227.75
405	148110	Op Ser - Strategic Mobility	1,500,000.00	0.00	0.00	528,679.00	20,000.00	0.00	951,321.00
405	148120	Op Ser - Corridor & Small Ar	2,000,000.00	0.00	86,804.70	1,132,935.44	7,390.19	0.00	859,674.37
405	148130	Op Ser - Northland Str. Acq	5,000,000.00	289,314.35	1,525,936.38	2,034,975.61	673,959.74	0.00	2,291,064.65
405	148140	Retail and Res Development	4,000,000.00	0.00	0.00	3,998,400.00	0.00	0.00	1,600.00
405	148150	Pearl District Flood Control	5,000,000.00	0.00	0.00	2,747,184.21	120,865.36	0.00	2,131,950.43
405	148160	Charles Page Boulevard - Plan	445,000.00	0.00	24,317.10	24,317.10	47,500.00	13,295.96	359,886.94
405	148170	Eugene Field Redevelopment	10,900,000.00	26,692.33	954,910.41	8,412,042.32	2,457,897.55	0.00	30,060.13
405	148180	Route 66 Restrooms & Parking	550,000.00	0.00	0.00	524,394.54	0.00	0.00	25,605.46
405	149100	Transit Coach & Lift Match	14,750,000.00	63,236.00	385,052.00	9,322,573.60	0.00	0.00	5,427,426.40
405	149200	Peoria (Brt) Project	14,052,005.06	0.00	20.50	13,634,729.05	2.00	0.00	417,274.01
405	193400000Z	Zoo Playground	1,650,000.00	0.00	0.00	1,451,728.18	0.00	0.00	198,271.82
405	2059FR0046	Consulting Services - Match	70,500.00	0.00	0.00	27,488.00	0.00	0.00	43,012.00
405	2125X0001Z	Computer Aided Dispatch (CAD)	660,000.00	0.00	0.00	264,955.00	395,045.00	0.00	0.00
405	2132X0001Z	MTTA Parking Lot	947,994.94	0.00	0.00	689,501.75	0.00	0.00	258,493.19
405	2134B0001Z	Gilcrease Museum Facility Imp	8,262,134.89	0.00	0.00	225,990.90	1,563,717.53	0.00	6,472,426.46
			<b>\$ 579,639,705.22</b>	<b>\$ 4,177,261.39</b>	<b>\$ 24,229,390.12</b>	<b>\$ 404,152,780.18</b>	<b>\$ 41,331,593.29</b>	<b>\$ 644,954.46</b>	<b>\$ 133,510,377.29</b>

# **2020 SALES TAX**

**FUND 409**

**(2020 SALES TAX FUND)**

**CITY OF TULSA, OKLAHOMA  
SALES TAX OVERVIEW COMMITTEE REPORT  
FUND 409 - 2020 SALES TAX**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES  
FOR THE NINE MONTHS ENDED MARCH 31, 2023**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<b>Revenue</b>					
Sales Tax	\$ 40,064,077.00	\$ 3,266,844.58	\$ 31,804,750.16	\$ 75,064,838.53	8,259,326.84
Donations					
Interest on Investments		65,870.84	428,996.27	550,441.91	(428,996.27)
Intergovernmental Revenue					
Federal, State & Local grants					
Transfers from other funds					
Miscellaneous Revenue					
Total Revenue	<u>40,064,077.00</u>	<u>3,332,715.42</u>	<u>32,233,746.43</u>	<u>75,615,280.44</u>	<u>7,830,330.57</u>
<b>Expenditures</b>					
Project Expenditures	<u>73,955,556.00</u>	<u>5,883,816.02</u>	<u>19,923,301.06</u>	<u>38,675,149.26</u>	<u>35,280,406.74</u>
Total Expenditures	<u>73,955,556.00</u>	<u>5,883,816.02</u>	<u>19,923,301.06</u>	<u>38,675,149.26</u>	<u>35,280,406.74</u>
Excess (Deficiency) of Revenue Over Expenditures			12,310,445.37	36,940,131.18	
Completed Projects Encumbrances			<u>15,875,534.31</u>	<u>15,875,534.31</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(3,565,088.94)	21,064,596.87	
June 30, 2022 Ending Fund Balance			17,441,841.63		
Prior year expenditures					
June 30, 2022 Encumbrances			<u>7,187,844.18</u>		
Adjusted Beginning Fund Balance			<u>24,629,685.81</u>		
Ending Fund Balance			<u>\$ 21,064,596.87</u>	<u>\$ 21,064,596.87</u>	

**Fund 409**

**2022 SALES TAX**

as of: 3/31/2023

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
409	2215X00001	Capital Equipment	22,555,556.00	939,814.83	8,458,333.47	19,736,111.43	0.00	0.00	2,819,444.57
409	2225X00013	Fire Apparatus and Equipment	14,300,000.00	4,924,082.49	7,020,987.82	10,106,664.35	3,402,129.57	689,858.66	101,347.42
409	2225X00014	911 Station Alert System	3,000,000.00	0.00	0.00	0.00	0.00	0.00	3,000,000.00
409	2225X00015	Police Helicopter Replacement	4,500,000.00	0.00	0.00	0.00	3,506,538.00	516,096.00	477,366.00
409	2225X00016	Municipal Lockup Data Storage	510,000.00	0.00	0.00	0.00	0.00	0.00	510,000.00
409	2234B00000	Greenwood Cultural Center Reha	850,000.00	0.00	70,957.77	232,578.36	35,869.87	0.00	581,551.77
409	2234B00004	Gilcrease Museum Improvements	6,660,000.00	0.00	0.00	0.00	6,660,000.00	0.00	0.00
409	2234B00006	CW- Public Facilities - Roofs	1,000,000.00	709.28	709.28	709.28	616,909.30	0.00	382,381.42
409	2234B00007	Animal Shelter Phase II	2,080,000.00	0.00	0.00	0.00	0.00	0.00	2,080,000.00
409	2234B00008	One Technology Center - Maint/	300,000.00	10,626.92	15,817.34	21,961.45	2,965.55	0.00	275,073.00
409	2234B00024	CW - Public Facilities Rehab/R	600,000.00	0.00	0.00	0.00	0.00	0.00	600,000.00
409	2234B00025	ADA Imp for City Facilities	350,000.00	0.00	0.00	0.00	0.00	0.00	350,000.00
409	2235X00019	Transit Fleet Replacement	2,500,000.00	0.00	0.00	225,101.80	0.00	0.00	2,274,898.20
409	2236S00002	Parking Facilities	8,000,000.00	0.00	4,000,000.00	8,000,000.00	0.00	0.00	0.00
409	2242P00030	Swan Lake Rehabilitation	500,000.00	0.00	0.00	0.00	0.00	0.00	500,000.00
409	2244B00009	CW - Park Facilities	2,500,000.00	8,582.50	135,206.83	135,206.83	213,684.36	91,991.00	2,059,117.81
409	2244P00010	CW - Outdoor Park Play Ameniti	500,000.00	0.00	0.00	0.00	0.00	0.00	500,000.00
409	2244P00011	CW - Tennis Court Rehab/Replac	1,200,000.00	0.00	0.00	0.00	0.00	0.00	1,200,000.00
409	2244P00012	Fred Johnson Rehab	500,000.00	0.00	27,338.00	34,638.00	5,312.00	0.00	460,050.00
409	2258X00017	CW - Eco Devo Infrastructure	1,200,000.00	0.00	0.00	0.00	0.00	0.00	1,200,000.00
409	2259X00018	CW - Commtty Dev Priority Proje	350,000.00	0.00	60,607.08	192,591.06	134,180.00	0.00	23,228.94
			<b>\$ 73,955,556.00</b>	<b>\$ 5,883,816.02</b>	<b>\$ 19,789,957.59</b>	<b>\$ 38,685,562.56</b>	<b>\$ 14,577,588.65</b>	<b>\$ 1,297,945.66</b>	<b>\$ 19,394,459.13</b>

**2016 VISION TULSA ECONOMIC  
DEVELOPMENT SALES FUND**

**FUND 4000**

**(2016 LIMITED PURPOSE TEMPORARY SALES TAX FUND)**

**CITY OF TULSA, OKLAHOMA  
SALES TAX OVERVIEW COMMITTEE REPORT  
FUND 4000 - 2016 VISION TULSA ECONOMIC DEVELOPMENT**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES  
FOR THE NINE MONTHS ENDED MARCH 31, 2023**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<b>Revenue</b>					
Sales Tax	\$ 80,678,302.00	\$ 6,554,616.27	\$ 67,014,425.36	\$ 278,592,288.40	\$ 13,663,876.64
Donations					
Interest on Investments		115,657.45	736,428.17	2,993,268.40	(736,428.17)
Intergovernmental Revenue					
Federal, State & Local grants					
Transfers from other funds					
Miscellaneous Revenue					
Total Revenue	<u>80,678,302.00</u>	<u>6,670,273.72</u>	<u>67,750,853.53</u>	<u>281,585,556.80</u>	<u>12,927,448.47</u>
<b>Expenditures</b>					
Project Expenditures	<u>256,926,894.98</u>	<u>5,660,176.76</u>	<u>55,493,507.07</u>	<u>208,346,014.12</u>	<u>48,580,880.86</u>
Total Expenditures	<u>256,926,894.98</u>	<u>5,660,176.76</u>	<u>55,493,507.07</u>	<u>208,346,014.12</u>	<u>48,580,880.86</u>
Excess (Deficiency) of Revenue Over Expenditures			12,257,346.46	73,239,542.68	
Completed Projects Encumbrances			<u>3,740,423.91</u>	<u>3,740,423.91</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			8,516,922.55	69,499,118.77	
June 30, 2022 Ending Fund Balance			47,345,384.77		
Prior year expenditures					
June 30, 2022 Encumbrances			<u>13,636,811.45</u>		
Adjusted Beginning Fund Balance			60,982,196.22		
Ending Fund Balance			<u>\$ 69,499,118.77</u>	<u>\$ 69,499,118.77</u>	



**Fund 4000**  
**2016 VISION ED CAPITAL PROJ**

as of: 3/31/2023

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4000	170000	Zink Lake and Related Improvem	21,690,000.00	0.00	6,742,759.66	17,077,838.05	3,207,308.02	0.00	1,404,853.93
4000	170010	Turkey Mountain Urban Wilderne	2,600,000.00	0.00	1,604,071.75	2,600,000.00	0.00	0.00	0.00
4000	170015	Levee Dist #12 Rehab (Match)	5,000,000.00	0.00	0.00	0.00	0.00	0.00	5,000,000.00
4000	170020	Trail E Bank 101 Cousins Park	2,400,000.00	0.00	0.00	69,165.48	19.59	0.00	2,330,814.93
4000	170025	23rd Jackson Redevelop Study	1,000,000.00	0.00	850.00	762,600.95	610.71	0.00	236,788.34
4000	170035	Cox Center & Dist Master Plan	14,100,000.00	0.00	0.00	14,100,000.00	(0.00)	0.00	0.00
4000	170060	BMX National Headquarters	5,801.19	0.00	0.00	0.00	0.00	0.00	5,801.19
4000	170065	South Mingo Corridor	1,000,000.00	0.00	973,706.50	977,296.50	0.00	0.00	22,703.50
4000	170075	Capital Equip (Non Pub Safety)	6,000,000.00	250,000.00	2,250,000.00	5,250,000.00	0.00	0.00	750,000.00
4000	170080ENGR	CW & Rt 66 Beaut Rvst_ENGR	1,237,500.00	0.00	0.00	0.00	0.00	0.00	1,237,500.00
4000	170080MOED	CW & Rt 66 Beaut Rvst_MOED	3,550,000.00	0.00	0.00	2,357,000.00	228,000.00	0.00	965,000.00
4000	170080PLAN	CW & Rt 66 Beaut Rvst_PLAN	1,357,593.79	2,622.00	51,792.64	696,149.05	137,692.78	100,000.00	423,751.96
4000	170085	Peoria - Mohawk: Business Park	3,300,000.00	0.00	0.00	1,817,410.02	0.00	0.00	1,482,589.98
4000	170090	Public School Partnership	7,200,000.00	576,197.98	2,366,947.32	5,353,154.65	0.00	0.00	1,846,845.35
4000	170095	Community Health Connection	4,570,000.00	0.00	0.00	4,570,000.00	0.00	0.00	0.00
4000	170105	Discovery Lab Site	0.00	0.00	0.00	0.00	0.00	0.00	0.00
4000	170110	N Peoria Conn 56-Mohawk	3,100,000.00	0.00	0.00	0.00	0.00	0.00	3,100,000.00
4000	170125	McCullough Park	3,060,000.00	94,223.45	2,058,816.04	3,015,613.89	395.00	0.00	43,991.11
4000	170145	Tulsa Arts Commission	900,000.00	0.00	110,602.19	643,689.19	66,397.81	0.00	189,913.00
4000	170155	PAC Improvement Master Plan	1,000,000.00	0.00	0.00	1,000,000.00	0.00	0.00	0.00
4000	170160	Transfer to TPFA 2017	173,856,000.00	4,737,133.33	40,494,048.73	148,586,015.25	0.00	0.00	25,269,984.75
			<b>\$ 256,926,894.98</b>	<b>\$ 5,660,176.76</b>	<b>\$ 56,653,594.83</b>	<b>\$ 208,875,933.03</b>	<b>\$ 3,640,423.91</b>	<b>\$ 100,000.00</b>	<b>\$ 44,310,538.04</b>

# **2016 VISION ADVANCE FUNDED REVENUE BOND FUND**

**FUND 4001**

**(2016 ADVANCE FUNDED BOND FUND)**

**CITY OF TULSA, OKLAHOMA  
SALES TAX OVERVIEW COMMITTEE REPORT  
FUND 4001 - 2017 VISION ECONOMIC DEVELOPMENT BOND ISSUE 1**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES  
FOR THE NINE MONTHS ENDED MARCH 31, 2023**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<b>Revenue</b>					
Bond Sale Receipts	\$	\$	\$	\$ 115,300,000.00	\$
Donations					
Miscellaneous Revenue				3,175,000.00	
<b>Total Revenue</b>				<u>118,475,000.00</u>	
<b>Expenditures</b>					
Project Expenditures	118,475,000.00	29,843.71	136,961.98	114,631,767.78	3,843,232.22
<b>Total Expenditures</b>	<u>118,475,000.00</u>	<u>29,843.71</u>	<u>136,961.98</u>	<u>114,631,767.78</u>	<u>3,843,232.22</u>
Excess (Deficiency) of Revenue Over Expenditures			(136,961.98)	3,843,232.22	
Completed Projects Encumbrances			<u>1,481,778.12</u>	<u>1,481,778.12</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(1,618,740.10)	2,361,454.10	
June 30, 2022 Ending Fund Balance			2,718,708.84		
Prior year expenditures					
June 30, 2022 Encumbrances			<u>1,261,485.36</u>		
Adjusted Beginning Fund Balance			3,980,194.20		
Ending Fund Balance			<u>\$ 2,361,454.10</u>	<u>\$ 2,361,454.10</u>	

**Fund 4001**  
**2017 VISION ED ISSUE 1**

as of: 3/31/2023

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4001	170000	Zink Lake and Related Improve	24,425,000.00	3,106.00	3,106.00	24,299,862.85	125,137.15	0.00	(0.00)
4001	170030	Gilcrease Museum Expansion	1,000,000.00	0.00	0.00	1,000,000.00	0.00	0.00	(0.00)
4001	170035	Cox Center & Dist Master Plan	13,250,000.00	0.00	0.00	13,144,135.27	105,864.73	0.00	(0.00)
4001	170040	Tulsa Fairgrounds	26,325,000.00	0.00	0.00	26,325,000.00	0.00	0.00	(0.00)
4001	170045	Airport Infrastructure	9,100,000.00	0.00	0.00	8,879,996.59	217,044.20	0.00	2,959.21
4001	170055	Langston Health Complex Exp	1,800,000.00	0.00	0.00	1,800,000.00	0.00	0.00	0.00
4001	170060	BMX National Headquarters	1,350,000.00	0.00	0.00	1,350,000.00	(0.00)	0.00	0.00
4001	170065	South Mingo Corridor	11,000,000.00	26,737.71	131,676.33	8,394,763.03	738,938.70	0.00	1,866,298.27
4001	170070	Public School Safety First	5,000,000.00	0.00	1,156.57	4,727,681.38	253,744.62	0.00	18,574.00
4001	170095	Community Health Connection	5,405,000.00	0.00	0.00	5,405,000.00	0.00	0.00	0.00
4001	170100	Air National Guard Training Ce	9,400,000.00	0.00	476.22	9,358,951.28	41,048.72	0.00	(0.00)
4001	170110	N Peoria Conn 56-Mohawk	900,000.00	0.00	0.00	900,000.00	0.00	0.00	(0.00)
4001	170115	TCC Career Placement	5,320,000.00	0.00	0.00	5,320,000.00	0.00	0.00	0.00
4001	170120	UCAT Auth OSU Tulsa	0.00	0.00	0.00	0.00	0.00	0.00	0.00
4001	170130	Mohawk Sports Complex	3,500,000.00	0.00	0.00	3,475,000.00	(0.00)	0.00	25,000.00
4001	170135	Go Plan Priority Projects	0.00	0.00	0.00	0.00	0.00	0.00	0.00
4001	170140	Rt 66 Village Train Depot	400,000.00	0.00	546.86	400,000.00	0.00	0.00	0.00
4001	170150A	2017 Vision ED Issue Costs_1	300,000.00	0.00	0.00	226,339.38	0.00	0.00	73,660.62
			<b>\$ 118,475,000.00</b>	<b>\$ 29,843.71</b>	<b>\$ 136,961.98</b>	<b>\$ 115,006,729.78</b>	<b>\$ 1,481,778.12</b>	<b>\$ -</b>	<b>\$ 1,986,492.10</b>

**2016 VISION ADVANCE FUNDED  
REVENUE BOND FUND**

**FUND 4003**

**(2016 ADVANCE FUNDED BOND FUND)**

**CITY OF TULSA, OKLAHOMA  
SALES TAX OVERVIEW COMMITTEE REPORT  
FUND 4003 - 2017 VISION ECONOMIC DEVELOPMENT BOND ISSUE 2**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES  
FOR THE NINE MONTHS ENDED MARCH 31, 2023**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<b>Revenue</b>					
Bond Sale Receipts	\$	\$	\$	\$ 118,100,000.00	\$
Donations					
Miscellaneous Revenue					
Total Revenue				<u>118,100,000.00</u>	
<b>Expenditures</b>					
Project Expenditures	118,100,000.00	1,588,410.87	8,190,215.94	106,693,118.16	11,406,881.84
Total Expenditures	<u>118,100,000.00</u>	<u>1,588,410.87</u>	<u>8,190,215.94</u>	<u>106,693,118.16</u>	<u>11,406,881.84</u>
Excess (Deficiency) of Revenue Over Expenditures			(8,190,215.94)	11,406,881.84	
Completed Projects Encumbrances			<u>9,791,606.39</u>	<u>9,791,606.39</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(17,981,822.33)	1,615,275.45	
June 30, 2022 Ending Fund Balance			2,732,349.16		
Prior year expenditures					
June 30, 2022 Encumbrances			<u>16,864,748.62</u>		
Adjusted Beginning Fund Balance			19,597,097.78		
Ending Fund Balance			<u>\$ 1,615,275.45</u>	<u>\$ 1,615,275.45</u>	

**Fund 4003**  
**2017 VISION ED ISSUE 2**

as of: 3/31/2023

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4003	170000	Zink Lake and Related Improvem	16,885,000.00	1,544,640.11	6,101,138.92	9,100,964.89	7,784,035.11	0.00	0.00
4003	170005	Low-Water Dam and Pedestrian B	0.00	0.00	0.00	0.00	0.00	0.00	0.00
4003	170010	Turkey Mountain Urban Wilderne	5,000,000.00	0.00	(20.00)	4,999,980.00	0.00	0.00	20.00
4003	170030	Gilcrease Museum Expansion	6,000,000.00	0.00	488,500.51	5,996,747.24	3,252.76	0.00	(0.00)
4003	170035	Cox Center & Dist Master Plan	27,650,000.00	0.00	3,600.00	27,187,101.05	225,830.59	0.00	237,068.36
4003	170040	Tulsa Fairgrounds	3,675,000.00	0.00	0.00	3,675,000.00	0.00	0.00	0.00
4003	170045	Airport Infrastructure	9,100,000.00	0.00	0.00	9,100,000.00	0.00	0.00	0.00
4003	170050	Tulsa Zoo & Living Museum	3,000,000.00	39,691.65	543,186.53	2,946,935.98	53,064.02	0.00	(0.00)
4003	170055	Langston Health Complex Exp	11,450,000.00	0.00	0.00	11,450,000.00	0.00	0.00	0.00
4003	170060	BMX National Headquarters	13,650,000.00	0.00	140.49	13,411,382.92	0.00	0.00	238,617.08
4003	170070	Public School Safety First	4,750,000.00	0.00	9,200.00	3,953,209.75	796,790.25	0.00	0.00
4003	170085	Peoria - Mohawk: Business Park	2,500,000.00	0.00	0.00	2,500,000.00	0.00	0.00	0.00
4003	170105	Discovery Lab Site	8,000,000.00	0.00	0.00	8,000,000.00	0.00	0.00	0.00
4003	170110	N Peoria Conn 56-Mohawk	3,000,000.00	0.00	0.00	1,799,055.95	917,763.40	0.00	283,180.65
4003	170125	McCullough Park	540,000.00	4,079.11	15,369.60	529,129.74	10,870.26	0.00	(0.00)
4003	170140	Rt 66 Village Train Depot	2,600,000.00	0.00	7,224.76	2,575,337.93	0.00	0.00	24,662.07
4003	170150B	2017 Vision ED Issue Bond Cost	300,000.00	0.00	0.00	266,171.09	0.00	0.00	33,828.91
			<b>\$ 118,100,000.00</b>	<b>\$ 1,588,410.87</b>	<b>\$ 7,168,340.81</b>	<b>\$ 107,491,016.54</b>	<b>\$ 9,791,606.39</b>	<b>\$ -</b>	<b>\$ 817,377.07</b>

**2016 VISION ADVANCE FUNDED  
REVENUE BOND FUND**

**FUND 4004**

**(2016 ADVANCE FUNDED BOND FUND)**



**CITY OF TULSA, OKLAHOMA  
SALES TAX OVERVIEW COMMITTEE REPORT  
FUND 4004 - 2017 VISION ECONOMIC DEVELOPMENT BOND ISSUE 3**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES  
FOR THE NINE MONTHS ENDED MARCH 31, 2023**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<b>Revenue</b>					
Bond Sale Receipts	\$	\$	\$	\$ 114,025,000.00	\$
Donations					
Miscellaneous Revenue					
Total Revenue				<u>114,025,000.00</u>	
<b>Expenditures</b>					
Project Expenditures	114,025,000.00	2,392,858.04	25,849,011.15	49,703,022.50	64,321,977.50
Total Expenditures	<u>114,025,000.00</u>	<u>2,392,858.04</u>	<u>25,849,011.15</u>	<u>49,703,022.50</u>	<u>64,321,977.50</u>
Excess (Deficiency) of Revenue Over Expenditures			(25,849,011.15)	64,321,977.50	
Completed Projects Encumbrances			<u>45,525,411.43</u>	<u>45,525,411.43</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(71,374,422.58)	18,796,566.07	
June 30, 2022 Ending Fund Balance			44,421,290.55		
Prior year expenditures					
June 30, 2022 Encumbrances			<u>45,749,698.10</u>		
Adjusted Beginning Fund Balance			90,170,988.65		
Ending Fund Balance			<u>\$ 18,796,566.07</u>	<u>\$ 18,796,566.07</u>	

**Fund 4004**  
**2017 VISION ED ISSUE 3**

as of: 3/31/2023

FUND	PROJECT	TITLE	REVISED BUDGET	MTD ACTUAL	YTD ACTUAL	LTD ACTUAL	ENC	COMM	BALANCE
4004	170005	Low-Water Dam and Pedestrian B	2,800,000.00	0.00	0.00	47.05	0.00	0.00	2,799,952.95
4004	170030	Gilcrease Museum Expansion	58,000,000.00	2,001,074.67	20,066,719.83	34,639,699.81	22,463,280.91	0.00	897,019.28
4004	170045	Airport Infrastructure	9,100,000.00	1,769.65	906,309.51	2,105,486.61	673,598.66	0.00	6,320,914.73
4004	170050	Tulsa Zoo & Living Museum	22,000,000.00	390,013.72	4,355,039.14	4,367,929.14	17,632,070.86	0.00	0.00
4004	170055	Langston Health Complex Exp	3,000,000.00	0.00	0.00	3,000,000.00	0.00	0.00	0.00
4004	170060	BMX National Headquarters	3,600,000.00	0.00	0.00	3,600,000.00	(0.00)	0.00	0.00
4004	170065	South Mingo Corridor	3,000,000.00	0.00	0.00	0.00	0.00	0.00	3,000,000.00
4004	170070	Public School Safety First	4,750,000.00	0.00	0.00	0.00	4,750,000.00	0.00	0.00
4004	170080MOED	CW & Rt 66 Beaut Reinvestment_	150,000.00	0.00	0.00	0.00	0.00	0.00	150,000.00
4004	170085	Peoria - Mohawk Business Park	4,200,000.00	0.00	0.00	1,832,704.40	6,461.00	0.00	2,360,834.60
4004	170135	Go Plan Priority Projects	3,125,000.00	0.00	0.00	3,125,000.00	(0.00)	0.00	0.00
4004	170150C	2017 Vision ED Issue Bond Cost	300,000.00	0.00	0.00	251,746.96	0.00	0.00	48,253.04
			<b>\$ 114,025,000.00</b>	<b>\$ 2,392,858.04</b>	<b>\$ 25,328,068.48</b>	<b>\$ 52,922,613.97</b>	<b>\$ 45,525,411.43</b>	<b>\$ -</b>	<b>\$ 15,576,974.60</b>

# **2008 GO BOND FUNDS**

**FUNDS 4260-4266 COMBINED**

**(2008 GENERAL OBLIGATION BOND FUNDS)**

**CITY OF TULSA, OKLAHOMA  
SALES TAX OVERVIEW COMMITTEE REPORT  
FUND 4260-4266 - 2008 GO BOND FUNDS**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES  
FOR THE NINE MONTHS ENDED MARCH 31, 2023**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<b>Revenue</b>					
Bond Sale Receipts	\$	\$	\$	\$ 285,000,000.00	\$
Donations					
Miscellaneous Revenue					
Total Revenue				285,000,000.00	
<b>Expenditures</b>					
Project Expenditures	230,054,936.55		2,786,947.31	220,687,407.61	9,367,528.94
Total Expenditures	230,054,936.55		2,786,947.31	220,687,407.61	9,367,528.94
Excess (Deficiency) of Revenue Over Expenditures			(2,786,947.31)	64,312,592.39	
Completed Projects Encumbrances			5,602,232.82	5,602,232.82	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(8,389,180.13)	3,765,296.12	
June 30, 2022 Ending Fund Balance			5,545,228.91		
Prior year expenditures					
June 30, 2022 Encumbrances			6,609,247.34		
Adjusted Beginning Fund Balance			12,154,476.25		
Ending Fund Balance			\$ 3,765,296.12	\$ 3,765,296.12	

**Fund**  
**2008 GO BOND**

**426**

as of: 3/31/2023

\$ 230,054,936.55 \$ - \$ 2,416,593.30 \$ 220,687,407.61 \$ 5,602,232.82 \$ - \$ 3,765,296.12

Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumb	Committed	Balance
104003	61st S-33rd W Ave to Union	1,556,527.90	-	-	1,396,673.54	-	-	159,854.36
104004	71st S-Hwy 75 to Arkansas Rive	3,960,048.74	-	-	3,960,048.74	-	-	-
104005	81ST S-YALE AVE TO SHERIDAN	923,488.36	-	-	923,488.36	-	-	-
104006	101St S-Harvard Ave To Yale	5,330,591.00	-	-	4,708,361.56	(0.00)	-	622,229.44
104008	129th E Ave-21st S to 11th	1,024,994.29	-	-	1,024,994.29	-	-	-
104009	Citywide-Arterial Rehab&Cons	245,000.00	-	-	245,000.00	-	-	-
104010	Citywide-Arterial Sidewalk R	400,000.00	-	-	400,000.00	-	-	-
104011	Citywide - Trails	1,000,000.00	-	-	1,000,000.00	-	-	-
104012	Citywide-Railroad Crossings	500,000.00	-	-	500,000.00	-	-	-
104013	Citywide - Local Match	3,000,000.00	-	-	2,817,486.95	153,220.27	-	29,292.78
104014	Citywide General Eng/Test/In	164,140.00	-	-	148,744.47	15,395.53	-	-
104015	Citywide Nonarterial Reh&Re	2,870,000.00	-	990,076.35	2,843,219.25	14,384.38	-	12,396.37
104016	Citywide Nonarterial Sidewk	300,000.00	-	-	274,492.22	25,507.78	-	-
104018	129th E Ave Admiral to Pine	2,266,780.70	-	-	2,266,780.70	0.00	-	0.00
104020	Citywide-Arterial Rt&Pv Main	3,694,184.00	-	-	3,694,184.00	(0.00)	-	0.00
104023	Lewis Ave 21st to 11th	-	-	-	-	-	-	-
104024	Memorial Ave 11Th To Admiral	-	-	-	-	-	-	-
1040316324	Admiral & Memorial Intersect	445,721.30	-	-	445,721.30	-	-	-
104032	River Road - 111th to 101st	884,830.08	-	-	884,830.08	-	-	-
104033	61St & Memorial Intersection	817,595.75	-	-	817,595.75	-	-	-
104035	Pine St 129th E Ave Intersec	1,083,614.80	-	-	1,083,614.80	-	-	(0.00)
104036	Harvard Ave - 61St S To 51St	4,124,138.14	-	-	4,124,138.14	-	-	-
104037	Apache St-Yale To Sheridan	395,997.45	-	-	395,997.45	(0.00)	-	0.00
104038	Cinci/Detroit-I244 To Jasper	710,000.00	-	-	710,000.00	-	-	-
104039	Harvard Ave-Admiral To Pine	426,655.29	-	-	426,655.29	-	-	-
104040	Lewis Ave-36Th St N To 46Th	450,400.19	-	-	450,400.19	-	-	(0.00)
104041	Memorial Dr-21St St S To 11Th	1,067,161.62	-	-	1,066,589.14	-	-	572.48
104043	PINE ST-YALE TO SHERIDAN RD	411,176.00	-	13,108.65	411,176.00	0.00	-	(0.00)
104045	River Rd-111Th St S To 101St	297,000.00	-	-	297,000.00	-	-	-
104046	Riverside Dr-41St St S To 31	472,541.00	-	-	472,541.00	-	-	-
104047	Union Ave-51St St S To 41St	700,000.00	-	-	700,000.00	-	-	-
104049	21st St S Utica Ave Intersect	200,000.00	-	-	200,000.00	-	-	-
104050	31St St S-Harvard Intersect	300,000.00	-	-	300,000.00	-	-	-
104051	36TH ST N-LEWIS AVE INTERSEC	248,140.69	-	-	248,140.69	0.00	-	(0.00)
104052	41St St S-Harvard Intersect	413,881.00	-	-	413,881.00	-	-	-
104053	Pine St- Yale Ave Intersect	500,000.00	-	-	500,000.00	-	-	-
104054	Citywide-Gen Engr/Test/Inspe	451,860.00	-	-	451,860.00	-	-	-
104060	Bridge 160-5400 E. Apache St	3,444,992.49	-	-	3,444,992.49	-	-	-
104061	Bridge 163-100 S Boulder Ave	7,284,170.84	-	-	7,284,170.84	-	-	-
104062	Bridge 228-3200 S. Riverside	288,476.00	-	-	288,476.00	-	-	0.00
104063	Bridge 234-4200 S. Union Ave	497,012.27	-	-	497,012.27	-	-	-
104064	Bridge 290-200 N 49th W Ave	1,687,083.90	-	-	1,687,083.90	-	-	(0.00)
104065	Bridge 318A 10100 S 72nd E A	3,837,026.52	-	-	3,837,026.52	-	-	(0.00)
104102	Maintenance Zone 1001 (Sw)	2,024,232.64	-	-	2,024,232.64	-	-	-
104106	Maintenance Zone 1006	3,155,338.38	-	-	3,155,338.38	-	-	-
104107	Maintenance Zone 1007	8,150,395.66	-	4,081.93	8,150,155.45	0.00	-	240.21
104171	Maintenance Zone 1071	1,670,676.50	-	-	1,662,194.41	-	-	8,482.09
104230	Maintenance Zone 2130	757,539.81	-	-	757,539.81	-	-	-

**Fund**  
**2008 GO BOND**

**426**

as of: 3/31/2023

\$ 230,054,936.55 \$ - \$ 2,416,593.30 \$ 220,687,407.61 \$ 5,602,232.82 \$ - \$ 3,765,296.12

Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumb	Committed	Balance
104231	Maintenance Zone 2131	2,455,563.00	-	-	2,451,015.56	-	-	4,547.44
104266	Maintenance Zone 2065 C	6,851,597.00	-	-	5,429,106.70	0.00	-	1,422,490.30
104303	Maintenance Zone 3003	1,715,018.19	-	-	1,715,018.19	-	-	-
104307	Maintenance Zone 3007	1,685,140.62	-	-	1,685,140.62	-	-	-
104309	Maintenance Zone 3009	3,664,377.59	-	-	3,664,377.59	-	-	-
104310	Maintenance Zone 3010	3,825,661.04	-	-	3,825,661.04	-	-	-
104311	Maintenance Zone 3011	678,300.11	-	-	678,300.11	-	-	-
104317	Maintenance Zone 3017	1,680,461.55	-	-	1,672,100.70	-	-	8,360.85
104413	Maintenance Zone 4013	4,745,128.27	-	-	4,725,252.22	-	-	19,876.05
104415	Maintenance Zone 4015	3,037,188.65	-	-	3,037,188.65	-	-	(0.00)
104416	Maintenance Zone 4016	7,304,489.05	-	-	7,304,489.05	-	-	-
104467	Maintenance Zone 4067 (A)	3,000,140.22	-	-	3,000,140.22	-	-	-
104525	Maintenance Zone 5025	5,142,414.45	-	-	5,027,770.95	(0.00)	-	114,643.50
104533	Maintenance Zone 5033	2,527,651.81	-	-	2,527,651.81	-	-	(0.00)
104534	Maintenance Zone 5034	5,535,532.71	-	-	5,535,532.71	-	-	(0.00)
104541	Maintenance Zone 5041	5,454,744.30	-	-	5,454,744.30	-	-	-
104619	Maintenance Zone 6019	1,769,054.10	-	-	1,769,054.10	-	-	-
104628	Maintenance Zone 6028	6,365,510.34	-	-	6,365,510.34	-	-	-
104642	Maintenance Zone 6042	3,548,988.07	-	-	3,548,988.07	-	-	-
104651	Maintenance Zone 6151	5,090,498.00	-	-	5,090,498.00	-	-	(0.00)
104747	Maintenance Zone 7046	2,285,961.71	-	-	2,285,961.71	-	-	-
104753	Maintenance Zone 7053	6,766,990.82	-	-	6,766,990.82	-	-	0.00
104759	Maintenance Zone 7059	2,180,027.87	-	-	2,180,027.87	-	-	-
104760	Maintenance Zone 7060	1,404,314.01	-	-	1,404,314.01	-	-	-
104803	Maintenance Zone 8103	3,883,263.82	-	-	3,883,263.82	-	-	(0.00)
104807	Maintenance Zone 8107	1,865,736.82	-	-	1,865,736.82	-	-	-
104813	Maintenance Zone 8113	3,451,308.54	-	-	3,451,308.54	-	-	-
104863	Maintenance Zone 8063	4,744,774.00	-	-	4,744,774.00	-	-	-
104928	Maintenance Zone 9029 (W)	8,101,606.56	-	-	8,101,606.56	-	-	(0.00)
104930	Maintenance Zone 9030	3,387,206.36	-	-	3,387,206.36	-	-	-
104931	Maintenance Zone 9031	148,855.68	-	-	148,855.68	-	-	-
104936	Maintenance Zone 9036	2,360,756.60	-	-	2,360,756.60	-	-	-
104937	Maintenance Zone 9037	986,951.95	-	-	986,951.95	-	-	-
104944	Maintenance Zone 9044	579,000.00	-	-	579,000.00	-	-	-
134001	5th Street Frisco to Denver	7,221,994.13	-	-	7,221,994.13	-	-	-
144022	Art/NonArt Routine & Preventio	4,250,000.00	-	-	4,249,947.47	52.53	-	0.00
144023	CW - Arterial Rt & Pv Main	8,853,905.93	-	-	8,853,905.93	0.00	-	(0.00)
144063	Bridge Replacement And Rehab	2,200,000.00	-	-	-	2,173,910.00	-	26,090.00
144101	Yale Ave 81st - 91st Wdn	10,886,657.08	-	1,268,722.52	7,666,894.75	3,219,762.33	-	-
144467	Maintenance Zone 4067	1,336,220.25	-	-	-	-	-	1,336,220.25
144642	Maintenance Zone 6142	400,000.00	-	140,603.85	400,000.00	-	-	-
147200	RP - Pedestrian Bridge Imp	2,248,532.04	-	-	2,248,532.04	-	-	-

# 2014 GO BOND FUNDS

FUND 4270~4274 COMBINED

(2014 GENERAL OBLIGATION BOND FUNDS)

**CITY OF TULSA, OKLAHOMA  
SALES TAX OVERVIEW COMMITTEE REPORT  
FUND 4270-4276 - 2014 GO BOND FUNDS**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES  
FOR THE NINE MONTHS ENDED MARCH 31, 2023**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<b>Revenue</b>					
Bond Sale Receipts	\$	\$	\$ 7,060,000.00	\$ 313,615,000.00	\$ (7,060,000.00)
Donations					
Miscellaneous Revenue					
Total Revenue			<u>7,060,000.00</u>	<u>313,615,000.00</u>	<u>-7,060,000.00</u>
<b>Expenditures</b>					
Project Expenditures	<u>313,615,000.00</u>	<u>1,633,738.50</u>	<u>14,939,622.84</u>	<u>224,304,705.20</u>	<u>89,310,294.80</u>
Total Expenditures	<u>313,615,000.00</u>	<u>1,633,738.50</u>	<u>14,939,622.84</u>	<u>224,304,705.20</u>	<u>89,310,294.80</u>
Excess (Deficiency) of Revenue Over Expenditures			(7,879,622.84)	89,310,294.80	
Completed Projects Encumbrances			<u>35,014,820.99</u>	<u>35,014,820.99</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			(42,894,443.83)	54,295,473.81	
June 30, 2022 Ending Fund Balance			77,469,715.28		
Prior year expenditures					
June 30, 2022 Encumbrances			<u>19,720,202.36</u>		
Adjusted Beginning Fund Balance			<u>97,189,917.64</u>		
Ending Fund Balance			<u>\$ 54,295,473.81</u>	<u>\$ 54,295,473.81</u>	



**Fund**  
**2014 GO BOND**

**427**

as of: 3/31/2023

\$ 313,615,000.00 \$ 1,633,738.50 \$ 13,064,003.90 \$ 223,531,170.39 \$ 35,014,820.99 \$ - \$ 55,069,008.62

Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumb	Committed	Balance
144000	Bond Issuance Costs	579,999.78	-	-	578,425.68	-	-	1,574.10
144015	Citywide Nonarterial Reh&Re	2,999,950.00	-	-	1,540,027.27	1,349,722.24	-	110,200.49
144016	Citywide Non-Art Sidewalks	500,000.00	-	-	500,000.00	-	-	0.00
144020	Citywide-Arterial Rt&Pv Main	22,167,489.89	-	175,259.08	22,116,270.49	(0.00)	-	51,219.40
144021	Citywide-Nonarterial Rt&Pv M	52,153,841.85	20,791.76	1,184,865.10	51,147,480.32	885,354.64	-	121,006.89
144060	Bridge189 - 4700 N. Iroquois	191,321.19	-	-	191,321.19	-	-	-
144061	Bridge298 - 2100 E. 61St St	66,650.26	-	-	66,650.26	-	-	-
144061	Bridge298 - 2100 E. 61St St	543,739.50	-	-	543,739.50	-	-	-
144062	Bridge323B - 12000 E. 21St	60,000.00	-	-	60,000.00	-	-	-
144093	Citywide Matching Funds	3,103,170.00	-	4,350.00	2,936,231.16	166,938.84	-	0.00
144094	ODOT Rehab & Replacement	8,200,000.00	-	11,189.06	5,282,853.58	240,994.67	-	2,676,151.75
144106	Maintenance Zone 1006	2,408,802.62	-	4,999.48	2,394,359.09	14,443.53	-	0.00
144107	Maintenance Zone 1007	530,000.00	-	-	530,000.00	-	-	-
144110	Citywide-Arterial Sidewalks	1,500,000.00	-	-	1,500,000.00	(0.00)	-	(0.00)
144111	Maintenance Zone 1001	8,275,000.00	287,077.46	1,677,206.48	4,811,256.48	3,148,975.22	-	314,768.30
144153	Maintenance Zone 1153	4,020,000.00	121.77	14,747.87	392,523.40	3,439,780.33	-	187,696.27
144157	Maintenance Zone 1157	3,612,823.69	-	-	3,612,823.69	0.00	-	0.00
144158	Maintenance Zone 1157	2,326,843.29	-	-	2,318,648.48	8,194.81	-	(0.00)
144168	Maintenance Zone 1068	3,600,000.00	-	-	332,346.88	52,340.85	-	3,215,312.27
144173	Maintenance Zone 1073	458,552.85	-	-	458,552.85	-	-	(0.00)
144176	Maintenance Zone 1076	1,678,019.41	-	-	1,678,019.41	0.00	-	-
144199	Maintenance Zone 1099	3,120,000.00	33,155.00	42,107.00	2,497,049.59	30,449.22	-	592,501.19
144200	Architect and Engineering Serv	330,000.00	-	-	330,000.00	-	-	-
144200	36 St: N MLK - Peoria Ave	2,920,000.00	-	458,180.21	2,789,989.17	3,175.00	-	126,835.83
144201	Apache St: Milk - Peoria	2,692,774.79	-	246.93	2,692,774.79	0.00	-	(0.00)
144202	Apachee: Peoria - Lewis Ave	300,000.00	-	-	300,000.00	-	-	-
144202	Apache: Peoria - Lewis Ave	2,365,000.00	-	1,278.00	28,643.71	26,139.29	-	2,310,217.00
144203	W 41st St S 41st W - S 33rd W	1,685,000.00	316,942.30	842,940.96	1,018,870.98	666,129.02	-	-
144204	S33rd W: 41st St to 51st St	2,730,000.00	-	1,482.20	443,324.77	1,935,911.17	-	350,764.06
144205	Apache St: Lewis To Harvard	2,070,000.00	-	896,252.63	1,707,115.02	17,556.00	-	345,328.98
144206	11th St: Peoria to Utica	1,820,000.00	-	-	1,820,000.00	(0.00)	-	0.00
144207	11Th St: Lewis Ave - Harvard	200,000.00	-	-	200,000.00	-	-	-
144208	11th St: Sheridan - Memorial	1,780,000.00	109,824.45	964,787.87	1,625,764.67	154,235.33	-	(0.00)
144209	21St St: Garnett To 129Th E	300,000.00	-	-	300,000.00	-	-	-
144209	21st St: Garnett to 129th E	2,435,050.00	-	-	2,017,895.64	27,500.00	-	389,654.36
144210	21St St-129Th East Ave Inter	250,000.00	-	621.67	249,200.48	799.52	-	0.00
144210	21st St-129th East Ave Inter	-	-	-	-	-	-	-
144210	21st St-129th East Ave INTERSC	1,965,000.00	68,134.96	75,529.60	1,828,247.11	136,752.89	-	-
144211	41St: Garnett - 129 E Ave	1,601,612.81	-	-	1,601,612.81	(0.00)	-	0.00
144212	51st St Sheridan to Memorial	1,055,651.29	-	-	1,047,661.29	0.00	-	7,990.00
144213	91st Harvard - Yale	285,000.00	-	-	176,003.18	18,903.29	-	90,093.53
144214	Sheridan 81st to 91st	1,525,950.99	-	-	1,525,950.99	(0.00)	-	0.00
144215	Peoria: 41St St - 51St St.	300,000.00	-	-	300,000.00	-	-	-
144215	Peoria: 41st - 51st	2,885,000.00	-	1,536.08	5,141.75	2,538,962.00	-	340,896.25
144216	41st St: Lewis to Harvard	2,730,000.00	-	2,275.57	2,721,437.50	8,562.50	-	(0.00)
144217	Apache & Harvard Intersectio	197,740.00	-	-	196,823.70	-	-	916.30
144217	Apache & Harvard Intersect	785,000.00	381,379.22	763,103.61	763,138.61	21,861.39	-	-
144217	Apache & Harvard INTERSCTN	990,000.00	111,831.37	111,831.37	111,831.37	878,168.63	-	-
144218	41st St & Lewis Intersection	2,055,000.00	-	9,470.09	2,055,000.00	-	-	-
144219	Maintenance Zone 2119	367,980.36	-	-	366,480.36	1,500.00	-	(0.00)
144225	Maintenance Zone 2125	2,574,462.36	-	(47,500.00)	2,526,962.36	(0.00)	-	47,500.00
144226	Maintenance Zone 2126	349,710.26	-	-	349,710.26	-	-	0.00
144230	Maintenance Zone 2130	3,895,000.00	9,062.50	21,649.00	3,692,277.47	3,787.79	-	198,934.74

**Fund**  
**2014 GO BOND**

**427**

as of: 3/31/2023

**\$ 313,615,000.00 \$ 1,633,738.50 \$ 13,064,003.90 \$ 223,531,170.39 \$ 35,014,820.99 \$ - \$ 55,069,008.62**

Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumb	Committed	Balance
144255	Maintenance Zone 2055	1,269,095.86	-	-	1,268,068.10	1,027.76	-	0.00
144256	Maintenance Zone 2056	1,268,393.91	-	-	1,268,393.91	-	-	(0.00)
144264	Maintenance Zone 2064	1,266,509.88	-	-	1,266,509.88	0.00	-	(0.00)
144265	Maintenance Zone 2065	959,200.67	-	-	957,942.60	-	-	1,258.07
144303	Maintenance Zone 3003	625,681.40	-	-	625,681.40	-	-	(0.00)
144304	Maintenance Zone 3004	1,412,273.54	-	-	1,412,273.54	0.00	-	0.00
144309	Citywide - Arterial Rehab	13,095,677.29	36,132.64	1,692,619.23	4,275,947.10	238,728.49	-	8,581,001.70
144310	Maintenance Zone 3010	7,929,998.00	-	10,470.20	722,785.21	20,486.91	-	7,186,725.88
144311	Maintenance Zone 3011	9,485,000.00	-	-	7,933,694.64	84,200.00	-	1,467,105.36
144317	Maintenance Zone 3017	750,000.00	-	-	599,915.15	63,268.44	-	86,816.41
144318	Maintenance Zone 3018	417,056.72	-	-	415,498.17	1,558.55	-	(0.00)
144320	Maintenance Zone 3020	4,500,000.00	-	8,991.05	335,436.20	30,718.85	-	4,133,844.95
144380	Maintenance Zone 3080	189,047.02	-	-	189,047.02	-	-	0.00
144413	Maintenance Zone 4013	535,058.95	-	-	511,528.37	23,530.58	-	(0.00)
144415	Maintenance Zone 4015	637,042.77	-	-	637,042.77	-	-	-
144421	Maintenance Zone 4021	3,655,000.00	17,425.58	17,425.58	352,296.45	50,930.09	-	3,251,773.46
144430	Maintenance Zone 4030	1,686,709.57	-	-	1,686,709.57	-	-	0.00
144431	Maintenance Zone 4031	11,680,000.00	7,703.06	1,359,333.48	2,136,641.67	9,382,544.53	-	160,813.80
144452	Maintenance Zone 4152	600,000.00	-	-	380,196.06	29,806.79	-	189,997.15
144467	Maintenance Zone 4067	4,855,000.00	9,461.36	9,461.36	3,371,805.21	15,329.36	-	1,467,865.43
144527	Maintenance Zone 5027	1,387,897.01	-	-	1,387,897.01	-	-	-
144533	Maintenance Zone 5033	4,880,000.00	-	1,730.30	4,879,987.32	-	-	12.68
144539	Maintenance Zone 5039	3,382,395.92	-	-	3,382,395.92	0.00	-	(0.00)
144546	Maintenance Zone 5046	600,000.00	-	-	600,000.00	(0.00)	-	0.00
144547	Maintenance Zone 5047	10,470,000.00	102.00	44,488.55	946,583.12	1,802,814.82	-	7,720,602.06
144627	Maintenance Zone 6027	1,006,165.51	-	-	1,006,165.51	-	-	(0.00)
144628	Maintenance Zone 6028	8,060,000.00	450.00	1,892,116.28	2,821,836.85	1,065,265.94	-	4,172,897.21
144635	Maintenance Zone 6035	3,306,365.97	-	-	3,304,854.80	0.00	-	1,511.17
144642	Maintenance Zone 6142	900,000.00	-	115,881.60	625,380.24	206,239.66	-	68,380.10
144645	Maintenance Zone 6145	2,640,000.00	-	3,512.50	2,544,554.52	18,488.01	-	76,957.47
144647	Maintenance Zone 6147	991,060.09	-	-	991,060.09	-	-	0.00
144700	Maintenance Zone 7100	1,313,991.88	-	-	1,313,991.88	(0.00)	-	0.00
144733	Maintenance Zone 7133	950,370.76	-	-	950,370.76	-	-	-
144740	Maintenance Zone 7040	3,275,000.00	-	-	3,224,845.00	50,155.00	-	(0.00)
144748	Maintenance Zone 7048	1,181,565.79	-	-	1,181,565.79	(0.00)	-	-
144754	Maintenance Zone 7054	1,000,000.00	-	104.50	727,510.40	18,989.60	-	253,500.00
144760	Maintenance Zone 7060	3,320,928.33	-	-	3,320,928.33	-	-	(0.00)
144803	Maintenance Zone 8103	1,775,162.45	-	-	1,775,162.45	-	-	(0.00)
144812	Maintenance Zone 8112	1,778,077.06	-	-	1,778,077.06	-	-	0.00
144857	Maintenance Zone 8057	2,570,000.00	-	-	2,134,255.27	126,682.34	-	309,062.39
144863	Maintenance Zone 8063	6,620,000.00	81,442.34	176,790.21	864,599.43	2,384,335.42	-	3,371,065.15
144931	Maintenance Zone 9031	518,453.57	-	-	518,453.57	-	-	(0.00)
144943	Maintenance Zone 9043	2,615,462.22	-	-	2,615,462.22	0.00	-	(0.00)
144944	Maintenance Zone 9044	4,000,000.00	-	4,347.73	3,906,614.67	88,116.37	-	5,268.96
144945	Maintenance Zone 9045	3,860,000.00	-	-	3,381,803.09	(0.00)	-	478,196.91
144949	Maintenance Zone 9049	1,200,000.00	-	2,726.36	694,919.86	75,735.48	-	429,344.66
144950	Maintenance Zone 9050	2,975,000.00	142,092.73	504,783.44	760,827.64	2,081,275.12	-	132,897.24
144951	Maintenance Zone 9051	1,550,000.00	608.00	811.67	129,996.59	1,377,454.71	-	42,548.70
144958	Maintenance Zone 9058	936,390.67	-	-	936,390.67	-	-	(0.00)
193140000Z	Mingo Creek Trail - 41st to 51	196,830.00	-	-	196,830.00	-	-	-

# **2020 GO BOND FUNDS**

**FUND 4281~428x COMBINED**

**(2020 GENERAL OBLIGATION BOND FUNDS)**

**CITY OF TULSA, OKLAHOMA  
SALES TAX OVERVIEW COMMITTEE REPORT  
FUND 4281-4283 - 2020 GO BOND FUNDS**

**STATEMENT OF REVENUES, EXPENDITURES AND ENCUMBRANCES  
FOR THE NINE MONTHS ENDED MARCH 31, 2023**

	FY ESTIMATED REVENUES/ LIFE-TO-DATE APPROPRIATIONS	CURRENT MONTH	ACTUAL YEAR TO DATE	LIFE TO DATE	OUTSTANDING REVENUES/ BALANCE OF APPROPRIATIONS
<b>Revenue</b>					
Bond Sale Receipts	\$	\$	\$ 57,620,000.00	\$ 149,015,000.00	\$ (57,620,000.00)
Donations					
Miscellaneous Revenue					
Total Revenue			<u>57,620,000.00</u>	<u>149,015,000.00</u>	<u>-57,620,000.00</u>
<b>Expenditures</b>					
Project Expenditures	<u>149,015,000.00</u>	<u>1,392,717.12</u>	<u>14,295,302.37</u>	<u>23,733,480.59</u>	<u>125,281,519.41</u>
Total Expenditures	<u>149,015,000.00</u>	<u>1,392,717.12</u>	<u>14,295,302.37</u>	<u>23,733,480.59</u>	<u>125,281,519.41</u>
Excess (Deficiency) of Revenue Over Expenditures			43,324,697.63	125,281,519.41	
Completed Projects Encumbrances			<u>20,500,730.80</u>	<u>20,500,730.80</u>	
Excess (Deficiency) of Revenue Over Expenditures and Encumbrances			22,823,966.83	104,780,788.61	
June 30, 2022 Ending Fund Balance			64,082,214.01		
Prior year expenditures					
June 30, 2022 Encumbrances			<u>17,874,607.77</u>		
Adjusted Beginning Fund Balance			<u>81,956,821.78</u>		
Ending Fund Balance			<u>\$ 104,780,788.61</u>	<u>\$ 104,780,788.61</u>	

Fund

428

2020 GO BOND

as of: 3/31/2023

\$ 149,015,000.00 \$ 1,392,717.12 \$ 13,934,887.86 \$ 25,202,302.33 \$ 20,018,230.80 \$ 482,500.00 \$ 103,311,966.87

Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumb	Committed	Balance
2019X0000Z	Bond Issuance Cost	432,542.00	-	140,451.99	347,105.11	-	-	85,436.89
2035X0001Z	Transit-MTTA - Route 66 BRT	5,330,000.00	51,229.14	283,386.90	1,050,406.59	1,118,707.72	-	3,160,885.69
2036A0007Z	Apache St: Harvard Ave - Yale	990,000.00	-	-	-	49,500.00	-	940,500.00
2036A0013Z	Gilcrease Rd: Apache St - Pine	800,000.00	-	-	-	-	-	800,000.00
2036A0025Z	41st St S: Union Ave - Elwood	250,000.00	-	-	-	169,949.00	-	80,051.00
2036A0035Z	41st St S & Elwood Ave INTERSC	50,000.00	-	-	-	50,000.00	-	-
2036A0042Z	Pine St: Lewis Ave - Harvard A	200,000.00	-	-	-	200,000.00	-	-
2036A0043Z	Pine St: State Hwy 11 - Mingo	175,000.00	-	-	-	175,000.00	-	-
2036A0047Z	Admiral Pl: Memorial Dr - Ming	240,000.00	-	8,000.00	8,000.00	0.00	-	232,000.00
2036A0050Z	Yale Ave: Apache St - Pine St	150,000.00	-	-	-	-	-	150,000.00
2036A0055Z	129th E Ave: Apache St - Pine	150,000.00	57,499.69	57,499.69	57,499.69	69,500.31	-	23,000.00
2036A0058Z	Pine St & Mingo Rd INTERSCTN	200,000.00	7,287.61	14,214.51	14,214.51	295.49	-	185,490.00
2036A0064Z	11th St S: Utica Ave - Lewis A	500,000.00	-	-	20,360.60	470,000.00	-	9,639.40
2036A0072Z	11th St S & Lewis Ave INTERSCT	270,000.00	-	-	-	270,000.00	-	-
2036A0092Z	31st St S: Garnett Rd - 129th	200,000.00	-	-	-	-	-	200,000.00
2036A0119Z	Sheridan Rd: 71st St S - 81st	200,000.00	-	-	-	137,700.00	-	62,300.00
2036A1000Z	CW Arterial Routine & Preventi	14,567,575.89	10,143.30	4,164,555.81	7,121,914.06	3,110,054.27	-	4,335,607.56
2036A1001Z	R&P: Pavement Reinspection	500,000.00	38,744.52	115,426.67	453,525.73	46,474.27	-	(0.00)
2036D0002Z	CBD: MLK & Detroit north of BN	1,400,000.00	-	-	1,323,755.38	21,427.61	-	54,817.01
2036D0004Z	CBD: Detroit Ave south of BNSF	1,090,000.00	-	10,080.60	140,000.00	-	-	950,000.00
2036D0005Z	CBD: Reconciliation Way	765,000.00	-	-	83,102.75	-	-	681,897.25
2036D0007Z	CBD: Alleyways	695,000.00	-	34,493.70	229,884.38	0.00	-	465,115.62
2036N0001Z	CW NonArterial Routine & Preve	18,399,914.34	624,716.93	5,774,945.16	6,870,634.99	7,569,821.48	-	3,959,457.87
2036N1007Z	Maintenance Zone 1007	119,999.77	-	-	84,055.86	11,706.24	-	24,237.67
2036N1070Z	Maintenance Zone 1070	250,000.00	-	648.45	218,900.00	(0.00)	-	31,100.00
2036N1076Z	Maintenance Zone 1076	250,000.00	-	7,316.21	224,661.26	23,594.95	-	1,743.79
2036N1078Z	Maintenance Zone 1078	300,000.00	-	-	226,834.03	26,097.54	-	47,068.43
2036N2056Z	Maintenance Zone 2056	200,000.00	-	-	-	110,220.45	-	89,779.55
2036N2065Z	Maintenance Zone 2065	3,802,167.00	255.30	985.77	202,096.62	25,513.38	-	3,574,557.00
2036N2066Z	Maintenance Zone 2066	187,833.00	3,147.58	3,147.58	111,053.63	11,113.37	-	65,666.00
2036N3081Z	Maintenance Zone 3081	840,000.00	-	-	66,380.11	3,807.17	-	769,812.72
2036N4014Z	Maintenance Zone 4014	200,000.00	-	-	125,713.48	9,520.52	-	64,766.00
2036N4021Z	Maintenance Zone 4021	330,000.00	11,337.62	34,311.08	219,344.16	36,564.90	-	74,090.94
2036N4022Z	Maintenance Zone 4022	3,450,000.00	-	-	288,916.94	12,280.08	-	3,148,802.98
2036N4030Z	Maintenance Zone 4030	1,030,000.00	222,142.54	222,430.70	375,983.20	611,380.80	-	42,636.00
2036N5040Z	Maintenance Zone 5040	780,000.00	3,356.43	26,997.71	78,753.14	11,670.38	-	689,576.48
2036N6035Z	Maintenance Zone 6035	1,140,000.00	-	-	-	80,055.00	-	1,059,945.00
2036N7048Z	Maintenance Zone 7048	251,630.00	-	23,657.00	233,128.08	18,501.92	-	-
2036N7060Z	Maintenance Zone 7060	990,000.00	-	902.39	67,673.82	15,830.57	-	906,495.61
2036N8057Z	Maintenance Zone 8057	1,900,000.00	-	16,979.30	118,438.17	19,757.49	-	1,761,804.34
2036N8102Z	Maintenance Zone 8102	2,550,000.00	-	-	158,157.62	13,076.38	-	2,378,766.00
2036N9037Z	Maintenance Zone 9037	2,030,000.00	-	9,844.00	155,375.32	10,000.00	-	1,864,624.68
2036N9038Z	Maintenance Zone 9038	890,000.00	-	-	72,611.70	11,556.14	-	805,832.16
2036N9044Z	Maintenance Zone 9044	350,000.00	-	106,226.81	106,226.81	95,534.12	-	148,239.07
2036N9050Z	Maintenance Zone 9050	1,350,000.00	20,570.59	25,233.72	97,728.33	10,028.33	-	1,242,243.34
2036N9051Z	Maintenance Zone 9051	110,000.00	-	-	84,053.27	11,054.44	-	14,892.29
2036S0001Z	ADA: Sidewalk Corridors	2,660,000.00	-	-	-	-	-	2,660,000.00
2036S0002Z	BPI: Go Plan Implement - ENG	2,500,000.00	1,673.13	307,377.97	307,377.97	358,405.23	-	1,834,216.80
2036S0003Z	BPI: Go Plan Implement - Traff	40,000.00	-	-	-	-	-	40,000.00
2036S0004Z	BPI: Arterial Sidewalk	1,000,000.00	1,915.00	602,241.65	686,239.02	1,132.90	-	312,628.08

Fund

428

2020 GO BOND

as of: 3/31/2023

\$ 149,015,000.00 \$ 1,392,717.12 \$ 13,934,887.86 \$ 25,202,302.33 \$ 20,018,230.80 \$ 482,500.00 \$ 103,311,966.87

Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumb	Committed	Balance
2036S0005Z	BPI: Non Arterial Sidewalk	300,000.00	4,495.00	12,304.72	93,677.43	16,506.00	7,500.00	182,316.57
2036W0004Z	91 St S: Memorial - Mingo Rd W	2,200,000.00	-	-	-	-	-	2,200,000.00
2036X0001Z	ADA: Transition Plan Update	250,000.00	-	17,124.86	244,767.89	5,232.11	-	(0.00)
2036X0002Z	ADA: Transit Stops	190,000.00	-	-	-	-	-	190,000.00
2036X0003Z	ADA: Signalized Intersections	960,000.00	-	-	-	-	-	960,000.00
2036X0005Z	TE: Signal Coord and Communica	520,000.00	-	-	-	-	-	520,000.00
2036X0006Z	TE: Signal Instal, Repair and	1,560,000.00	-	-	-	-	-	1,560,000.00
2036X0007Z	TE: Traffic Calming	470,000.00	-	-	30,438.44	124,561.56	-	315,000.00
2036X0008Z	TE: Lighting Repair and Replac	310,000.00	-	-	-	-	100,000.00	210,000.00
2036X0009Z	TE: Pavement Markings and Sign	1,950,000.00	-	-	-	-	375,000.00	1,575,000.00
2036X0010Z	TE: Guardrail Repair and Repl	260,000.00	-	-	-	-	-	260,000.00
2036X0011Z	Arena District Master Pln Impl	582,458.00	-	-	-	-	-	582,458.00
2037B0167Z	Bridge #167	130,000.00	-	-	15,300.00	-	-	114,700.00
2037B0173Z	Bridge #173	400,000.00	-	-	-	-	-	400,000.00
2037B0201C	Bridge #201C	100,000.00	-	-	-	8,000.00	-	92,000.00
2037B0204Z	Bridge #204	1,200,000.00	-	29,269.93	105,130.20	33,568.31	-	1,061,301.49
2037B0232A	Bridge #232A	700,000.00	-	-	22,300.00	-	-	677,700.00
2037B0241Z	Bridge #241	1,100,000.00	-	-	53,948.26	10,000.00	-	1,036,051.74
2037B0245Z	Bridge #245	860,000.00	2,476.95	15,880.39	47,059.87	41,640.13	-	771,300.00
2037B0258Z	Bridge #258	275,000.00	-	-	35,000.00	-	-	240,000.00
2037B0261A	Bridge #261A	175,000.00	-	-	24,000.00	-	-	151,000.00
2037B0261B	Bridge #261B	175,000.00	-	-	24,000.00	-	-	151,000.00
2037B0263Z	Bridge #263	465,000.00	3,540.69	3,540.69	33,540.69	1,459.31	-	430,000.00
2037B0269Z	Bridge #269	400,000.00	-	-	-	25,000.00	-	375,000.00
2037B0286Z	Bridge #286	150,000.00	-	-	-	8,000.00	-	142,000.00
2037B0301A	Bridge #301A	200,000.00	-	2,068.60	23,527.23	1,472.77	-	175,000.00
2037B0301Z	Bridge #301	165,000.00	1,171.97	13,569.00	13,569.00	21,431.00	-	130,000.00
2037B0343Z	Bridge #343	50,000.00	-	-	-	4,000.00	-	46,000.00
2037B0359Z	Bridge #359	50,000.00	-	-	15,000.00	-	-	35,000.00
2037B0423Z	Bridge #423	100,000.00	-	-	-	8,000.00	-	92,000.00
2037B1000Z	CW Bridge Rehab and Inspection	300,000.00	-	61,215.77	113,347.00	-	-	186,653.00
2039X0009Z	TE: Traffic Studies	100,000.00	-	-	25,000.00	-	-	75,000.00
2036A0002Z	46th St N: Peoria Ave - Lewis	1,200,000.00	-	135,668.32	150,000.00	(0.00)	-	1,050,000.00
2036A0005Z	36 St N: Osage County Ln - MLK	75,000.00	-	-	-	-	-	75,000.00
2036A0008Z	Pine St: Gilcrease Rd - Union	470,000.00	-	-	-	-	-	470,000.00
2036A0009Z	Pine St: Peoria Ave - Lewis Av	340,000.00	-	20,000.00	20,000.00	320,000.00	-	-
2036A0010Z	Edison St: 33rd W Ave - Union	1,050,000.00	-	-	-	-	-	1,050,000.00
2036A0011Z	33rd W Ave: Apache St - Pine S	1,350,000.00	-	-	-	-	-	1,350,000.00
2036A0012Z	33rd W Ave: Pine St - Edison S	700,000.00	-	-	-	-	-	700,000.00
2036A0015Z	MLK Jr Blvd: 36th St N - Apach	1,950,000.00	-	-	-	-	-	1,950,000.00
2036A0016Z	MLK Jr Blvd: Apache St - Pine	75,000.00	-	-	-	-	-	75,000.00
2036A0017Z	Peoria Ave: 56th St N - 46th S	850,000.00	-	3,336.80	55,000.00	-	-	795,000.00
2036A0018Z	Peoria Ave: 46th St N - 36th S	900,000.00	-	6,468.48	68,444.72	-	-	831,555.28
2036A0020Z	Lewis Ave: Pine St - Admiral P	320,000.00	-	-	-	320,000.00	-	-
2036A0021Z	Harvard Ave: Mohawk Blvd - 36	500,000.00	-	-	-	38,765.21	-	461,234.79
2036A0022Z	36 St N & Harvard Ave INTERSCT	20,000.00	-	-	-	11,000.00	-	9,000.00
2036A0023Z	Apache St & MLK Blvd INTERSCTN	50,000.00	-	-	-	-	-	50,000.00
2036A0024Z	Pine St & Gilcrease Rd INTERSC	100,000.00	-	-	-	-	-	100,000.00
2036A0027Z	61st St S: Lewis Ave - Harvard	1,020,000.00	-	-	-	49,500.00	-	970,500.00
2036A0031Z	Delaware Ave: 81st St S - 91st	1,400,000.00	-	-	-	-	-	1,400,000.00

Fund

428

2020 GO BOND

as of: 3/31/2023

\$ 149,015,000.00 \$ 1,392,717.12 \$ 13,934,887.86 \$ 25,202,302.33 \$ 20,018,230.80 \$ 482,500.00 \$ 103,311,966.87

Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumb	Committed	Balance
2036A0039Z	36th St N: Garnett Rd - 129th	200,000.00	-	-	-	35,389.87	-	164,610.13
2036A0045Z	Pine St: Garnett Rd - 129th E	150,000.00	-	-	-	-	-	150,000.00
2036A0046Z	Admiral: Sheridan Rd - Memoria	1,200,000.00	-	10,000.00	10,000.00	-	-	1,190,000.00
2036A0048Z	Admiral: Garnett Rd - 129th E	140,000.00	344.73	8,000.00	8,000.00	-	-	132,000.00
2036A0056Z	36 St N & 129th E Ave INTERSCT	75,000.00	53,881.24	53,881.24	53,881.24	21,118.76	-	-
2036A0059Z	Pine St & Garnett Rd INTERSCTN	75,000.00	-	-	-	-	-	75,000.00
2036A0060Z	Admiral & Sheridan Rd INTERSCT	200,000.00	-	-	-	-	-	200,000.00
2036A0067Z	15th St S: Harvard Ave - Yale	200,000.00	-	5,747.17	5,747.17	104,252.83	-	90,000.00
2036A0074Z	15th St S & Harvard INTERSCTN	100,000.00	-	-	-	52,120.00	-	47,880.00
2036A0076Z	31st St S & Peoria Ave INTERSC	52,097.00	-	-	-	52,097.00	-	-
2036A0086Z	Admiral: 225 E Av - 22200 E Ad	850,000.00	-	-	-	-	-	850,000.00
2036A0089Z	11 St S: 177th E Ave - 193rd E	140,000.00	-	-	-	-	-	140,000.00
2036A0097Z	161st E Ave: 11th St S - 21st	200,000.00	-	-	-	-	-	200,000.00
2036A0099Z	11 St S & 161st E Ave INTERSCT	50,000.00	-	-	-	-	-	50,000.00
2036A0101Z	11 St S & 193rd E Ave INTERSCT	70,000.00	-	-	-	-	-	70,000.00
2036A0110Z	Mingo Rd: 61st St S - 71st St	200,000.00	-	-	-	-	-	200,000.00
2036A0124Z	Peoria Ave: 31st St S - 41st S	125,000.00	-	-	-	68,768.00	-	56,232.00
2036A0125Z	Lewis Ave: 41st St S - I-44	1,530,000.00	-	85,277.10	85,277.10	0.00	-	1,444,722.90
2036D0001Z	CBD: 4th St	325,000.00	-	-	-	310,153.00	-	14,847.00
2036N1097Z	Maintenance Zone 1097	1,210,000.00	-	-	-	15,000.00	-	1,195,000.00
2036N1153Z	Maintenance Zone 1153	300,000.00	18,248.78	133,916.29	146,777.20	23,257.80	-	129,965.00
2036N1155Z	Maintenance Zone 1155	510,000.00	-	21,417.76	50,000.00	2,248.00	-	457,752.00
2036N1157Z	Maintenance Zone 1157	110,000.00	-	-	-	-	-	110,000.00
2036N3010Z	Maintenance Zone 3010	200,000.00	-	77,732.50	77,732.50	52,267.50	-	70,000.00
2036N3075Z	Maintenance Zone 3075	280,000.00	-	45,000.00	45,000.00	23,076.00	-	211,924.00
2036N4023Z	Maintenance Zone 4023	490,000.00	-	42,337.54	42,337.54	12,989.46	-	434,673.00
2036N4067Z	Maintenance Zone 4067	1,070,000.00	8,050.16	13,060.93	15,000.00	(0.00)	-	1,055,000.00
2036N4069Z	Maintenance Zone 4069	400,000.00	34,474.90	140,018.92	140,018.92	59,981.08	-	200,000.00
2036N5016Z	Maintenance Zone 5016	800,000.00	22,007.78	229,135.09	247,037.39	328,962.61	-	224,000.00
2036N5027Z	Maintenance Zone 5027	100,000.00	392.95	49,147.92	50,558.67	0.00	-	49,441.33
2036N5039Z	Maintenance Zone 5039	1,530,000.00	-	-	1,773.44	13,226.56	-	1,515,000.00
2036N6142Z	Maintenance Zone 6142	1,048,370.00	7,347.65	42,267.09	43,657.85	22,175.15	-	982,537.00
2036N8113Z	Maintenance Zone 8113	240,000.00	-	21,000.00	21,000.00	8,000.00	-	211,000.00
2036N9036Z	Maintenance Zone 9036	420,000.00	101,092.62	119,383.87	119,383.87	116,591.61	-	184,024.52
2036N9045Z	Maintenance Zone 9045	580,000.00	-	-	-	29,000.00	-	551,000.00
2036N9049Z	Maintenance Zone 9049	400,000.00	-	149,961.35	209,825.79	12,174.21	-	178,000.00
2036N9052Z	Maintenance Zone 9052	180,000.00	-	9,119.66	9,119.66	19,826.60	-	151,053.74
2036W0001Z	Gilcrease Rd: Pine St - Admira	12,000,000.00	41,636.96	128,272.84	154,155.93	468,691.70	-	11,377,152.37
2036W0005Z	101st St S & Sheridan INTERSCT	1,200,000.00	-	-	-	-	-	1,200,000.00
2036W0006Z	81 St S: Harvard Ave - Yale Av	1,500,000.00	-	-	-	20,000.00	-	1,480,000.00
2036X0004Z	CW Infrastructure Partnership	4,070,413.00	39,535.36	238,407.66	422,861.00	1,521,894.21	-	2,125,657.79
2036A0033Z	Harvard Ave-71st St to 81st St	150,000.00	-	-	-	-	-	150,000.00
2036A0054Z	129th E Ave-36th St N to Apach	200,000.00	-	-	-	-	-	200,000.00
2036A0075Z	21st St S & Harvard Intersect	150,000.00	-	-	-	-	-	150,000.00
2036A0083Z	Sheridan Rd-41st St to 51st St	750,000.00	-	-	-	-	-	750,000.00
2036A0088Z	11th St S-161st to 177th	100,000.00	-	-	-	-	-	100,000.00
2036A0100Z	11th St S & 177th E Intersect	75,000.00	-	-	-	-	-	75,000.00
2036A0109Z	Memorial Dr-51st St S 61st St	1,000,000.00	-	-	-	-	-	1,000,000.00
2036A0118Z	Yale Ave-111th St to 121st St	150,000.00	-	-	-	-	-	150,000.00
2036A0121Z	111th St S & Yale Ave Intersec	50,000.00	-	-	-	-	-	50,000.00

**Fund**  
**2020 GO BOND**

**428**

as of: 3/31/2023

**\$ 149,015,000.00 \$ 1,392,717.12 \$ 13,934,887.86 \$ 25,202,302.33 \$ 20,018,230.80 \$ 482,500.00 \$ 103,311,966.87**

Project	Project Title	Revised Budget	MTD Actual	YTD Actual	LTD Actual	Encumb	Committed	Balance
2036D0003Z	CBD: Cincinnati Ave	500,000.00	-	-	-	500,000.00	-	-
2036D0006Z	CBD: Lansing Ave	80,000.00	-	-	-	80,000.00	-	-
2036N1068Z	Maintenance Zone 1068	300,000.00	-	-	-	-	-	300,000.00
2036N1071Z	Maintenance Zone 1071	180,000.00	-	-	-	-	-	180,000.00
2036N1072Z	Maintenance Zone 1072	300,000.00	-	-	-	-	-	300,000.00
2036N3004Z	Maintenance Zone 3004	150,000.00	-	-	-	-	-	150,000.00
2036N3005Z	Maintenance Zone 3005	350,000.00	-	-	-	-	-	350,000.00
2036N3011Z	Maintenance Zone 3011	325,000.00	-	-	-	-	-	325,000.00
2036N3017Z	Maintenance Zone 3017	300,000.00	-	-	-	-	-	300,000.00
2036N4015Z	Maintenance Zone 4015	100,000.00	-	-	-	-	-	100,000.00
2036N4031Z	Maintenance Zone 4031	350,000.00	-	-	-	-	-	350,000.00
2036N5033Z	Maintenance Zone 5033	280,000.00	-	-	-	-	-	280,000.00
2036N6149Z	Maintenance Zone 6149	200,000.00	-	-	-	-	-	200,000.00
2036N6150Z	Maintenance Zone 6150	450,000.00	-	-	-	-	-	450,000.00
2036N7109Z	Maintenance Zone 7109	175,000.00	-	-	-	-	-	175,000.00
2036N8116Z	Maintenance Zone 8116	100,000.00	-	-	-	-	-	100,000.00
2036W0002Z	81st St S-Tacoma to Maybelle	900,000.00	-	-	-	-	-	900,000.00
2036W0003Z	81st St S & Elwood Intersect	755,000.00	-	-	-	-	-	755,000.00



# COMBINED STATEMENT OF OTHER FUND ACTIVITY

FUNDS 400, 401, 403, 404, 425

SALES TAX OVERVIEW COMMITTEE REPORT  
(FUNDS 401, 403, 404, 425)  
Combined Statement of Fund Activity  
March 31, 2023

Fund	LIFE-TO-DATE APPROPRIATIONS	EXPEDITURES			ENCUMBERED/ COMMITTED	BALANCE
		CURRENT MONTH	FISCAL YEAR-TO-DATE	LIFE-TO-DATE		
<b>FUND 401 - 2001 SALES TAX FUND</b>	<b>\$ 84,905,730.03</b>	<b>\$ -</b>	<b>\$ -</b>	<b>\$ 84,826,058.10</b>	<b>\$ (0.00)</b>	<b>\$ 79,671.93</b>
017110 General Park Improvements	4,751,480.30	-	-	4,738,892.94	-	12,587.36
914411 Tulsa Trails	3,857,231.30	-	-	3,842,871.73	-	14,359.57
962201 Gilcrease Museum Renovation	1,116,205.00	-	-	1,063,480.00	-	52,725.00
<b>FUND 403 - 2006 EXT SALES TAX ADVACE FUND</b>	<b>\$ 27,705,922.61</b>	<b>\$ -</b>	<b>\$ -</b>	<b>\$ 27,705,676.78</b>	<b>\$ -</b>	<b>\$ 245.83</b>
017150 Woodward & Forestry Impr.	470,000.00	-	-	469,754.17	-	245.83
<b>FUND 404 - 2008 SPECIAL TEMP SALES TAX</b>	<b>\$ 145,493,500.00</b>	<b>\$ -</b>	<b>\$ 67,687.00</b>	<b>\$ 145,298,037.28</b>	<b>\$ 157,930.92</b>	<b>\$ 37,531.80</b>
104017 Art Rehab Citywide	81,942,000.00	-	-	81,859,132.39	82,867.61	-
104021 Citywide Non-arterial RTPV	34,082,000.00	-	64,381.82	34,048,044.35	-	33,955.65
104022 Citywide General Engineering	1,383,000.00	-	-	1,304,364.54	75,059.31	3,576.15
104023 Bridge Repair and Rehab	90,000.00	-	-	90,000.00	-	-
144104 Riverside Dr & Rltd Infrstr	5,500,000.00	-	3,305.18	5,499,996.00	4.00	-
<b>FUND 425 - 2005 BOND ISSUE (4250-4255)</b>	<b>\$ 74,919,257.38</b>	<b>\$ 25,326.14</b>	<b>\$ 25,326.14</b>	<b>\$ 74,845,023.01</b>	<b>\$ 831.76</b>	<b>\$ 73,402.61</b>
016100 Forensic Lab Expansion	23,599,535.03	-	-	23,592,682.62	-	6,852.41
055103 UDE Renovation	102,015.18	7,273.62	7,273.62	91,744.20	-	10,270.98
055105 UDSW Renovation	491,642.36	18,052.52	18,052.52	482,306.95	-	9,335.41
055200 Fire Trng Ctr/Reloc Sta 16	12,042,434.64	-	-	12,004,228.91	-	38,205.73
147200 RP - Pedestrian Bridge Imp	751,467.96	-	-	751,467.96	-	-
155107 Police Courts Renovation	673,959.36	-	-	673,959.36	-	0.00
203400001Z Tulsa Zoo Department	2,811.76	-	-	1,980.00	831.76	-
104021 Garnett Pine to Apache	300,000.00	-	-	291,261.92	-	8,738.08

# **ALL FUNDS BUDGET ACTIONS**

Held in Munis Notable to Approve

DocuSign Envelope ID: 882EE8A9-2ABB-456B-A8CE-4377B51020D6

DocuSign Envelope ID: 4E345771-E098-48D6-BC0C-C11D984E8FF1

RFA Form System

ORDINANCE NO.  
**25005**

**APPROVED**

MAR 01 2023

**Tulsa City Council**



# Ordinance

Version 3.2 released on 8/3/21

### CITY COUNCIL USE ONLY

Date Received: \_\_\_\_\_

Committee Date: 2-22-23

1<sup>st</sup> Agenda Date: 2-22-23

Tracking #: 23-125-1

Committee: UED

Hearing Date: \_\_\_\_\_

2<sup>nd</sup> Agenda Date: 3-1-23

### CITY CLERK USE ONLY

Scanned

Date: 03.08.2023

Posted

Item #: 2302-00341

All department items requiring Council approval must be submitted through the Mayor's Office.

### Primary Details

Dept. Tracking No.	Board Approval	Other Board Name	City Council Approval <input checked="" type="radio"/> Yes <input type="radio"/> No
Department Finance	Contact Name Jarrod Moore	Email jmoore@cityoftulsa.org	Phone 918-596-7809
Subject (Description) Gilcrease Museum & Animal Shelter Additional Funding		Ordinance Type Budget Amendment	
Section	Township	Range	Lot
Block	Address		BA / CT Number BA4051843
Amending Ord. No.	TRO Title No.	TRO Subtitle	Property/Non-Property
Council District	Zoning No.	PUD No.	Planning District

### Budget

#### Funding Source(s)

2001 SALES TAX FUND (Fund 401) / Engineering Services / Gilcrease Museum Expansion:	\$52,725.00
2006 SALES TAX FUND (Fund 402) / Engineering Services / Gilcrease Museum Expansion:	\$1,108,658.00
2014 SALES TAX FUND (Fund 405) / Engineering Services / Gilcrease Museum Expansion:	\$4,938,617.00
2014 SALES TAX FUND (Fund 405) / Engineering Services / Animal Shelter Expansion:	\$6,100,000.00
<b>TOTAL:</b>	<b>\$12,200,000.00</b>

### Approvals

JE  JM

Department:

Legal:

Board:

Mayor:

Other:

DocuSigned by:

Tammy Pitts

94C4B97CCEA9409

[Signature]

Date: 2/17/2023

Date: \_\_\_\_\_

Date: \_\_\_\_\_

Date: February 20, 2023

Date: \_\_\_\_\_

**Policy Statement**

**Background Information**

This action will appropriate a total of \$12,200,000.00 to capital outlay accounts for the ENGINEERING SERVICES Department within the 2001 SALES TAX FUND (Fund 401), 2006 SALES TAX FUND (Fund 402), and 2014 SALES TAX FUND (Fund 405).

Additional funding is needed for the Gilcrease Museum and the Animal Shelter. This action will allow both the construction on Gilcrease Museum to continue, as well as the animal shelter to have sufficient funding to build a new facility. \$12,200,000.00 will appropriated to these two projects, from unappropriated fund balance as follows:

Gilcrease Museum Expansion (Total \$6,100,000.00):

- Fund 401: \$ 52,725.00
- Fund 402: \$1,108,658.00
- Fund 405: \$4,938,617.00

Animal Shelter Expansion (Total \$6,100,000.00):

- Fund 405: \$6,100,000.00

**Summation of the Requested Action**

Request that the Mayor and Council approve the attached Budget Amendment, BA4051843: Gilcrease Museum & Animal Shelter Additional Funding | 2014 SALES TAX FUND [FUND 405] | \$12,200,000.00

Emergency Clause?

Reason for Emergency Clause

Yes

No

**Processing Information for City Clerk's Office**

**Post Execution Processing**

- Mail vendor copy (add'l signature copies attached)
- Must be filed with other governmental entity
- Add'l governmental entity approval(s) required

**Additional Routing and Processing Details**

Set to Original – Yes to All

(Published in the Tulsa World

March 12, 2023)

ORDINANCE NO. **25005**

AN ORDINANCE AMENDING THE FISCAL YEAR 2022-23 BUDGET OF THE CITY OF TULSA, OKLAHOMA, IS HEREBY AMENDED TO MAKE SUPPLEMENTAL APPROPRIATIONS OF TWELVE MILLION TWO HUNDRED THOUSAND DOLLARS AND ZERO CENTS (\$12,200,000.00), RECOGNIZED FROM UNAPPROPRIATED FUND BALANCE WITHIN THE 2001 SALES TAX FUND (FUND 401), 2006 SPECIAL EXTENDED SALES TAX FUND (FUND 402), AND THE 2014 SALES TAX FUND (FUND 405) AS FOLLOWS:

BE IT ORDAINED BY THE CITY OF TULSA:

Section 1. That the Fiscal Year 2022-23 Budget of the City of Tulsa, Oklahoma, is hereby amended to make supplemental appropriations of Six Million One Hundred Thousand Dollars and Zero Cents (\$6,100,000.00), recognized from Unappropriated Fund Balance within the 2001 Sales Tax Fund (Fund 401) of Fifty-Two Thousand Seven Hundred Twenty Five Dollars and No Cents (\$52,725.00), 2006 Special Extended Sales Tax Fund (Fund 402) of One Million One Hundred Eight Thousand Six Hundred Fifty-Eight Dollars and Zero Cents (\$1,108,658.00) and the 2014 Sales Tax Fund (Fund 405) of Four Million Nine Hundred Thirty-Eight Thousand Six Hundred Seventeen Dollars and Zero Cents (4,938,617.00) as follows:

**2001 SALES TAX FUND  
ENGINEERING SERVICES DEPARTMENT**

Gilcrease Museum Expansion	\$ 52,725.00
<b>TOTAL FUND INCREASE</b>	<b>\$ 52,725.00</b>

**2006 SPECIAL EXTENDED SALES TAX FUND  
ENGINEERING SERVICES DEPARTMENT**

Gilcrease Museum Expansion	\$ 1,108,658.00
<b>TOTAL FUND INCREASE</b>	<b>\$ 1,108,658.00</b>

**2014 SALES TAX FUND  
ENGINEERING SERVICES DEPARTMENT**

Gilcrease Museum Expansion	\$ 4,938,617.00
<b>TOTAL FUND INCREASE</b>	<b>\$ 4,938,617.00</b>


Section 2. That the Fiscal Year 2022-23 Budget of the City of Tulsa, Oklahoma, is hereby amended to make supplemental appropriations of Six Million One Hundred Thousand Dollars and Zero Cents (\$6,100,000.00), recognized from Unappropriated Fund Balance within the 2014 Sales Tax Fund (Fund 405) as follows:

**2014 SALES TAX FUND  
ENGINEERING SERVICES DEPARTMENT**

Animal Shelter Expansion	\$ 6,100,000.00
<b>TOTAL FUND INCREASE</b>	<b>\$ 6,100,000.00</b>

Section 3. That this ordinance shall take effect immediately from and after its adoption and approval.

Adopted by the Council: MAR 01 2023  
Date

  
Chair of the Council

OFFICE OF THE MAYOR

Received by the Mayor: \_\_\_\_\_, at \_\_\_\_\_  
Date Time

G. T. Bynum, Mayor

By: \_\_\_\_\_  
Secretary

Approved by the Mayor of the City of Tulsa, Oklahoma, MAR 08 2023 at  
Date


\_\_\_\_\_  
Time

  
Mayor


(Seal)

ATTEST:

  
City Clerk



APPROVED:

  
City Attorney

# TULSA WORLD

P.O. Box 1770 Tulsa, Oklahoma 74102-1770 | [tulsa-world.com](http://tulsa-world.com)

Account Number

1030936

Date

March 13, 2023

CITY OF TULSA  
Attn: City Clerk's Office  
175 E. 2ND ST. SUITE 260  
TULSA, OK 74103

Date	Category	Description	Ad Size	Total Cost
03/12/2023	Legal Notices	25005	2 x 84.00 CL	127.52

798092

Published in the Tulsa World, Tulsa County, Oklahoma,  
March 12, 2023

ORDINANCE NO. 25005

AN ORDINANCE AMENDING THE FISCAL YEAR 2022-23 BUDGET OF THE CITY OF TULSA, OKLAHOMA, IS HEREBY AMENDED TO MAKE SUPPLEMENTAL APPROPRIATIONS OF TWELVE MILLION TWO HUNDRED THOUSAND DOLLARS AND ZERO CENTS (\$12,200,000.00), RECOGNIZED FROM UNAPPROPRIATED FUND BALANCE WITHIN THE 2001 SALES TAX FUND (FUND 401), 2006 SPECIAL EXTENDED SALES TAX FUND (FUND 402), AND THE 2014 SALES TAX FUND (FUND 405) AS FOLLOWS:

BE IT ORDAINED BY THE CITY OF TULSA:

Section 1. That the Fiscal Year 2022-23 Budget of the City of Tulsa, Oklahoma, is hereby amended to make supplemental appropriations of Six Million One Hundred Thousand Dollars and Zero Cents (\$6,100,000.00), recognized from Unappropriated Fund Balance within the 2001 Sales Tax Fund (Fund 401) of Fifty-Two Thousand Seven Hundred Twenty Five Dollars and No Cents (\$52,725.00), 2006 Special Extended Sales Tax Fund (Fund 402) of One Million One Hundred Eight Thousand Six Hundred Fifty-Eight Dollars and Zero Cents (\$1,108,658.00) and the 2014 Sales Tax Fund (Fund 405) of Four Million Nine Hundred Thirty-Eight Thousand Six Hundred Seventeen Dollars and Zero Cents (4,938,617.00) as follows:

**2001 SALES TAX FUND  
ENGINEERING SERVICES DEPARTMENT**

Gilcrease Museum Expansion \$ 52,725.00  
TOTAL FUND INCREASE \$ 52,725.00

**2006 SPECIAL EXTENDED SALES TAX FUND  
ENGINEERING SERVICES DEPARTMENT**

Gilcrease Museum Expansion \$ 1,108,658.00  
TOTAL FUND INCREASE \$ 1,108,658.00

**2014 SALES TAX FUND  
ENGINEERING SERVICES DEPARTMENT**

Gilcrease Museum Expansion \$ 4,938,617.00  
TOTAL FUND INCREASE \$ 4,938,617.00

Section 2. That the Fiscal Year 2022-23 Budget of the City of Tulsa, Oklahoma, is hereby amended to make supplemental appropriations of Six Million One Hundred Thousand Dollars and Zero Cents (\$6,100,000.00), recognized from Unappropriated Fund Balance within the 2014 Sales Tax Fund (Fund 405) as follows:

**2014 SALES TAX FUND  
ENGINEERING SERVICES DEPARTMENT**

Animal Shelter Expansion \$ 6,100,000.00  
TOTAL FUND INCREASE \$ 6,100,000.00

Section 3. That this ordinance shall take effect immediately from and after its adoption and approval.

ADOPTED by the Tulsa City Council, this 1st Day of March 2023

Crista Patrick, Chair of the City Council

APPROVED by the Mayor of the City of Tulsa, Oklahoma, this 8th Day of March 2023

G. T. Bynum, Mayor

ATTEST: Christina Chappell, City Clerk

APPROVED: Jack Blair, City Attorney



## Affidavit of Publication

**Brenda Brumbaugh**

I, \_\_\_\_\_, of lawful age, am a legal representative of the Tulsa World of Tulsa, Oklahoma, a daily newspaper of general circulation in Tulsa County, Oklahoma, a legal newspaper qualified to publish legal notices, as defined in 25 O.S. § 106 as amended, and thereafter, and complies with all other requirements of the laws of Oklahoma with reference to legal publication. That said notice, a true copy of which is attached hereto, was published in the regular edition of said newspaper during the period and time of publication and not in a supplement, on the DATE(S) LISTED BELOW

03/12/2023

Newspaper reference: 0000798092

*B Brumbaugh*  
\_\_\_\_\_  
Legal Representative

Sworn to and subscribed before me this date: 3/13/23

*A Shell*  
\_\_\_\_\_  
Notary Public

AMBER SHELL  
NOTARY PUBLIC - STATE OF OKLAHOMA  
MY COMMISSION EXPIRES SEP. 11, 2023  
COMMISSION # 19009197

My Commission expires \_\_\_\_\_
